

Battle Lake Weekly Update 4/02/26

- **Installing Dust Collector - 50%**
- **Punch List – 99%**
- **Grading Courtyard – 99%**
- **Doors and Hardware – 99%**
- **Roofing - North Addition – 95%**
- **Duct Work - North Addition – 99%**
- **Duct Work Kitchen – 35%**
- **Life Safety Rough In – 75%**
- **Hydronic Lines – 99%**
- **Insulating Duct Work – 99%**
- **AL Windows – 55%**
- **Tile – 80%**
- **Sheetrock – 100%**
- **Hydronic Lines - 99%**
- **Electric Rough In – 99%**
- **Painting – 45%**
- **Taping – 99%**
- **HVAC Finishes – 65%**
- **Plumbing Finishes – 40%**



2-Week Look Ahead

- Life Safety Rough In
- AL Frames & Windows
- Doors and Hardware - Phase 2
- Hydronic Lines
- Tile bathrooms
- Plumbing Hydronic Lines
- Electrical Rough In
- Insulation
- Finishes
- Punch List Epoxy floor
- Bathroom Partitions


Corridor B108




Ceiling Grid B122



Doors & Frame A74

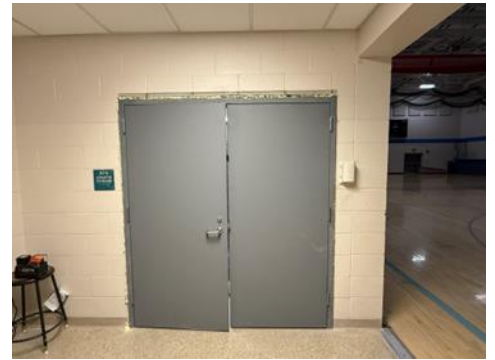

Tile Floor B125

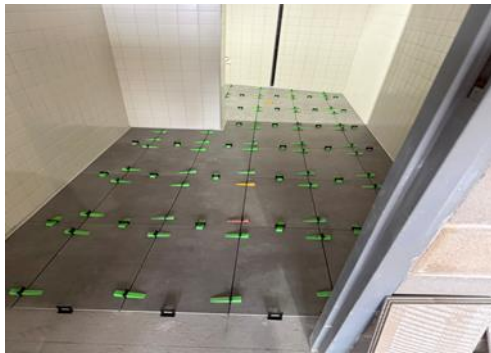

Finishes B125



AL Windows B106A

