

PINE TREE ISD

NEW CTE FACILITY

CONSTRUCTION UPDATE

- BUILDING DRY-IN IS COMPLETE.
- DRIVES, APPROACHES, AND STORAGE PAD WORK ARE COMPLETE.
- EXTERIOR BRICK VENEER WORK IS NEARING COMPLETION.
- MECHANICAL, ELECTRICAL, AND PLUMBING OVERHEAD INSTALLATIONS ARE NEARING COMPLETION.
- INTERIOR FINISHES ARE IN PROGRESS.
- STOREFRONT GLASS INSTALLATION IS IN PROGRESS.
- ROOFING AND WALL PANEL INSTALLATIONS ARE SCHEDULED TO BEGIN SOON.



COST SUMMARY

Construction Contingency Balance:	\$458,160
Owner Contingency Balance:	\$150,000
Total Budget:	\$12,663,106
Total Completed & Stored To Date:	\$5,350,037
Percentage Complete:	42%



DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY

PINE TREE ISD

PARKWAY ELEMENTARY RENOVATIONS



CONSTRUCTION UPDATE

- FOUNDATION WORK IS COMPLETE.
- STRUCTURAL STEEL ERECTION IS NEARING COMPLETION.
- EXTERIOR WALL FRAMING AND SHEATHING INSTALLATIONS ARE IN PROGRESS.
- SECOND-FLOOR CONCRETE POURS ARE SCHEDULED TO BEGIN SOON.
- INTERIOR WALL FRAMING IS SCHEDULED TO BEGIN SOON.
- MECHANICAL, ELECTRICAL, AND PLUMBING IN-WALL AND OVERHEAD INSTALLATIONS ARE SCHEDULED TO BEGIN SOON.



COST SUMMARY

Construction Contingency Balance:	\$672,760
Owner Contingency Balance:	\$125,000
Total Budget:	\$11,132,172
Total Completed & Stored To Date:	\$2,761,101
Percentage Complete:	25%

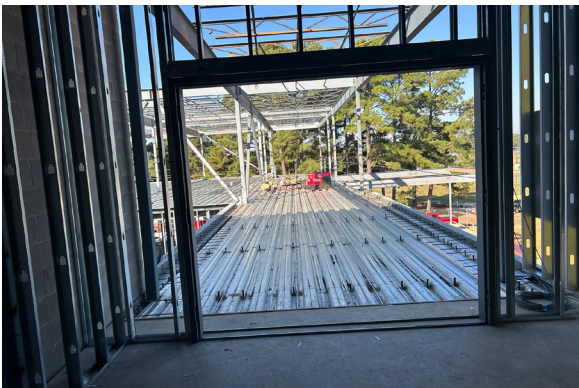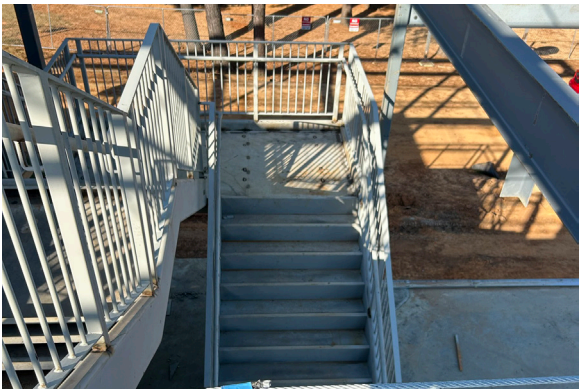

DIFFERENT FROM THE GROUND UP



GALLAGHER
A CUMMING GROUP COMPANY
