



Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
March 13, 2026

A. Activities performed for the period of March 9 – March 13, 2026

• **Central Ave School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review of scheduling and planning.
- Electrical activities are continuing to progress.
- Plumbing activities are continuing to progress.
- Continued installation of CMU walls.
- Grout placement for CMU walls has continued with progression.
- Commenced and completed concrete placement for column diamonds and entry slab to existing building.
- Excavation for the transformer and associated work has commenced.

• **Kings Road School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review and layout.
- Continued electrical work for conduit and boxes within CMU walls.
- Commenced above ceiling electrical work.
- Commenced plumbing work associated with roof drain assemblies and hangers.
- Continued CMU and lintel installation at West wall
- Grout placement for CMU has continued.
- Demolition of existing flooring, ceiling grid, temporary wall and remaining existing CMU block has been completed.
- Crane for HVAC curbs was placed and completed.
- Installation of blocking for HVAC curbs was installed.
- Continued preparation, layout and installation of parapet walls.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



B. Projected Activities for period of March 16 – March 20, 2026

- **Central Ave School:**

- Continue submittal and RFI process.
- Continue township and third-party inspections.
- Continue mobilization of trades.
- Maintain soil management and soil erosion control measures.
- Regrade and refresh site building pad exterior will continue as needed.
- Electrical activities will continue with progress.
- Continue plumbing activities.
- Continue installation of CMU walls.
- Grout placement for CMU walls will continue with progression.
- Commence installation of door bucks.
- Commence installation of blocking in preparation of roof installation.
- Work associated with installation of the transformer and vault will continue.
- Hold project meeting.

- **Kings Road School:**

- Continue submittal and RFI process.
- Continue Madison Township and third-party inspections.
- Continue mobilization of trades.
- Continue delivery of materials.
- Continue soil management and soil erosion control measures.
- Continue transition work at slabs.
- Continue grout placement for CMU walls.
- The exterior brick installation will continue.
- Continue conduit and electrical work at CMU walls.
- Continue rough plumbing work for roof drains.
- Commence installation of parapet walls.
- Commence crane placement for RTU to be lifted on the roof.
- Commence and complete RTU placement and installation.
- Work within existing multi-purpose room will continue.
- Hold project meeting.

Epic Management, Inc.


136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



Western CMU Installation at CAS



Transformer Excavation at CAS

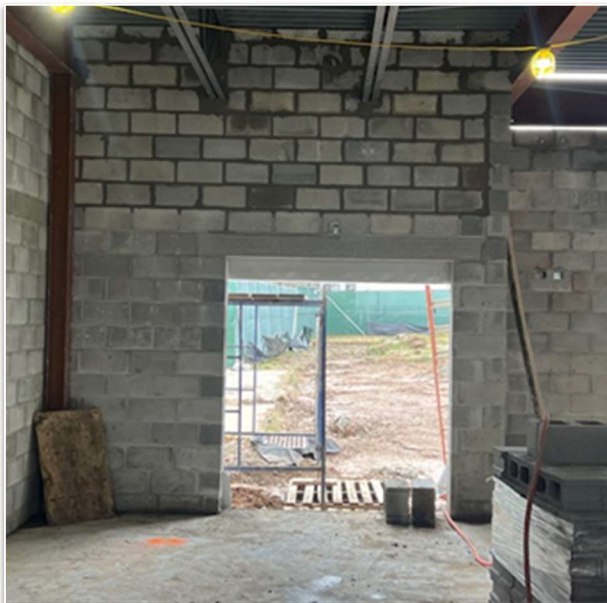

CMU at North entry at CAS



Stone delivery for track pad at CAS



VCT flooring removal at KRS



Drop ceiling removal at KRS



West elevation brick placement at KRS



Track pad reconditioning at KRS
