



**Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
May 1, 2026**

A. Activities performed for the period of April 27 – May 1, 2026

• **Central Ave School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Regrading and added stone continued to be installed at perimeter of site pad as needed.
- Continued review of scheduling and planning.
- Electrical activities are continuing to progress.
- New Transformer was placed.
- Rough plumbing is completed and passed inspections.
- Continued installation of interior CMU walls.
- Continued exterior rigid insulation installation.
- Brick placement has continued.
- Commenced brick washdown.
- Commenced installation of blocking for coping.
- HVAC work has continued.
- Window frame and glazing installation have commenced.
- Held project meeting.

• **Kings Road School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review and layout.
- Above ceiling and rough electrical work has continued.
- Commenced block retaining wall installation.
- Continued HVAC ductwork installation.
- Lay out and form work for sidewalks and stairs continued.
- Rebar, form installation and concrete placement for sidewalks and stairs are progressing.
- Held project meeting.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



B. Projected Activities for period of May 4 – May 8, 2026

• **Central Ave School:**

- Continue submittal and RFI process.
- Continue township and third-party inspections.
- Continue mobilization of trades.
- Maintain soil management and soil erosion control measures.
- Regrade and refresh site building pad exterior will continue as needed.
- Electrical activities will continue with progress.
- Continue rough above grade plumbing work within the new building.
- Interior CMU cleanup activities will continue.
- Continue installation of exterior brick.
- Exterior masonry washdown and cleanup will continue.
- Commence demobilization of mason contractor.
- Continue installation of blocking for coping.
- Work associated with the installation of the transformer and switch gear will continue.
- Continue window frame and glazing installation activities.

• **Kings Road School:**


- Continue submittal and RFI process.
- Continue Madison Township and third-party inspections.
- Continue mobilization of trades.
- Continue delivery of materials.
- Continue soil management and soil erosion control measures.
- Grading and seeding preparation will commence.
- Block retaining wall installation will continue.
- Transition work at slabs will continue.
- Continuing conduit and electrical work at existing interior walls.
- Continuing electrical work above and below ceiling within existing building.
- Continue HVAC ductwork installation.
- Roofing activities will commence.
- Continue installation of forms and rebar for concrete sidewalks and stairs.
- Concrete Placement for stairs and sidewalks will continue.
- Work within existing multi-purpose room will continue.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106




Southern Elevation Brickwork at CAS

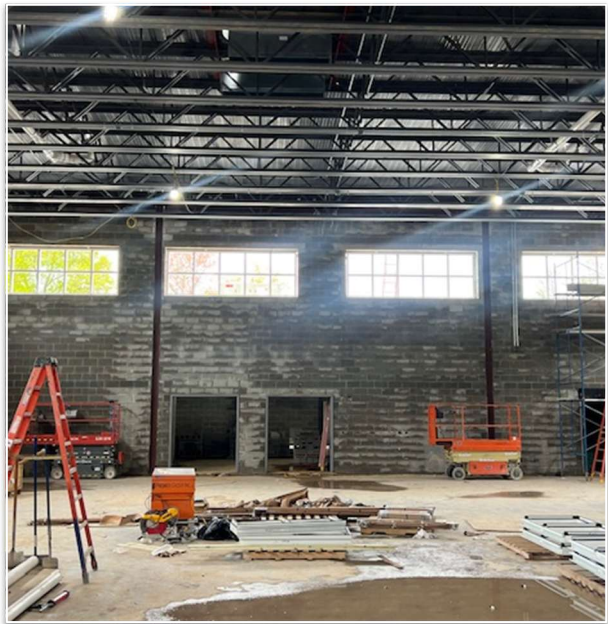

Window Installation at CAS




Transformer Placement at CAS

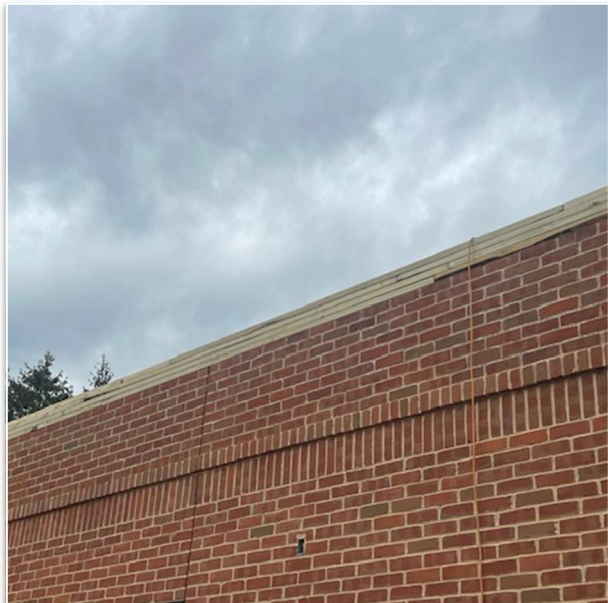

Wood Blocking for Coping at CAS




Rebar and Footings at KRS

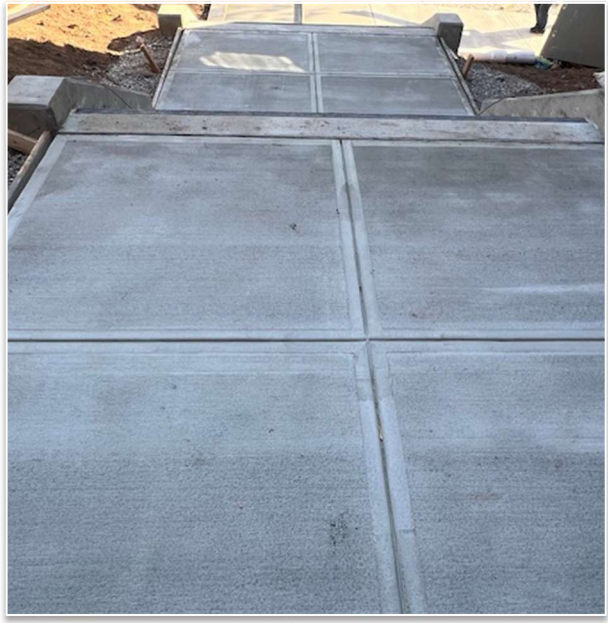

Sidewalk Concrete Placement at KRS



Cleanup and grading at KRS

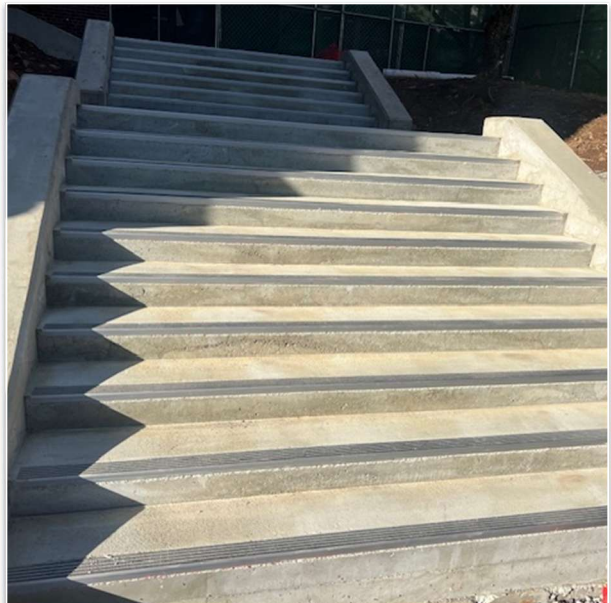

Concrete Stair/Tread Work at KRS
