



Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
June 5, 2026

A. Activities performed for the period of June 1 – June 5, 2026

• **Central Ave School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review of scheduling and planning.
- Regrading and added stone continued to be installed at perimeter of site pad as needed.
- Installation of forms and wire mesh for sidewalks has commenced.
- Concrete placement for sidewalks has commenced.
- Electrical activities are continuing to progress.
- Electrical switchgear work has commenced.
- Exterior caulking has continued.
- HVAC work has continued.
- HVAC controls wiring has commenced
- Fire alarm wiring has commenced.
- Exterior door frame installation has continued.
- Roofing contractors continued with final stages of installation.
- CMU painting activities have commenced.
- Held current issues meeting.

• **Kings Road School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review and layout.
- Above ceiling and rough electrical work has continued.
- Old HVAC room bracing of existing CMU wall has commenced and is completed.
- Continued final roofing installation activities.
- Temporary fence at the auxiliary staging area was removed.
- Held current issues meeting.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



B. Projected Activities for period of June 8 – June 12, 2026

• **Central Ave School:**

- Continue submittal and RFI process.
- Continue township and third-party inspections.
- Continue mobilization of trades.
- Maintain soil management and soil erosion control measures.
- Regrade and refresh site building pad exterior will continue as needed.
- Electrical activities will continue with progress.
- Exterior doorframe installation activities will continue.
- Roofing installation activities will continue.
- Underground storm piping will continue.
- Final grading will continue.
- Exportation of excess soil will continue.
- Continue preparation and concrete placement for sidewalks and pads.
- Interior CMU Painting will continue.
- Hold project meeting.

• **Kings Road School:**


- Continue submittal and RFI process.
- Continue Madison Township and third-party inspections.
- Continue mobilization of trades.
- Continue delivery of materials.
- Transition work at slabs will commence.
- Continuing electrical work on existing interior walls.
- Continuing electrical work above and below ceiling within existing building.
- Work within existing multi-purpose room will continue.
- Interior painting activities will continue.
- Commence ceiling grid installation activities.
- Roofing activities will continue.
- Hold project meeting.



Electrical Switchgear Work at CAS



Concrete sidewalk Placement at CAS

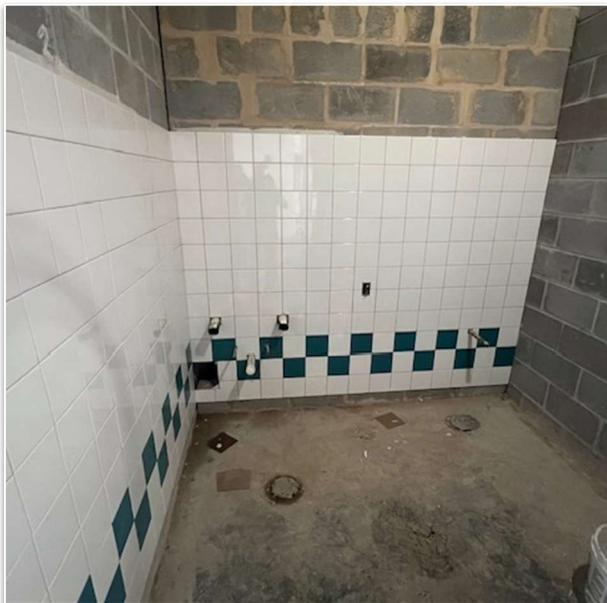

Class Bathroom Tiling at CAS



Hallway Painting at CAS



Exterior Lights Installation at KRS



HVAC Room Wall Bracing at KRS



Transition Roofing at KRS



Aux Temp Fencing Removal at KRS
