



Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
August 7, 2026

A. Activities performed for the period of August 3 – August 7, 2026

• **Central Ave School:**

- Continued submittal and RFI review process.
- Continued township inspections.
- Continued review of scheduling and planning.
- Electrical activities are continuing to progress.
- Fire alarm wiring has continued.
- HVAC/RTU activities have continued.
- Continued caulking and touch up painting.
- Continued and completed ceiling tile installation activities.
- VCT flooring installation was finalized.
- Cove base installation has continued.
- RTUs start up procedures have continued.
- HVAC balancing was finalized.
- Projector and projector screen installation is ongoing.
- Gym wood flooring coordination meeting was held.
- Held project meeting.

• **Kings Road School:**

- Continued submittal and RFI review process.
- Continued township inspections.
- Continued review of scheduling and planning.
- Above ceiling and rough electrical work was finalized.
- Fire device installation on ceiling was finalized.
- Building, Electrical, and Fire inspections held.
- Flooring Preparation.
- Transition work at slabs has continued.
- Installation of LVT gym flooring will commence.
- Exterior camera installation will be finalized.
- Held AIA and Owner punch list walkthrough.
- Held project meeting.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



B. Projected Activities for period of August 10 – August 14, 2026

- **Central Ave School:**

- Continue submittal and RFI process.
- Continue township inspections.
- Continue mobilization of trades.
- Electrical activities will continue with progress.
- Security device installation activities will continue.
- Interior painting will continue.
- Wood doors glass will be installed.
- RTUs commissioning is scheduled.
- Projector and projector screen installation will be finalized.
- Gym lighting will be finalized.

- **Kings Road School:**

- Continue submittal and RFI process.
- Continue Madison Township inspections.
- Continue mobilization of trades.
- Work within existing multi-purpose room will continue.
- Installation of LVT gym flooring will be finalized.
- Punchlist work will commence.

Epic Management, Inc.


136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



Sidewalk Replacement Work at CAS



Vestibule Painting at CAS

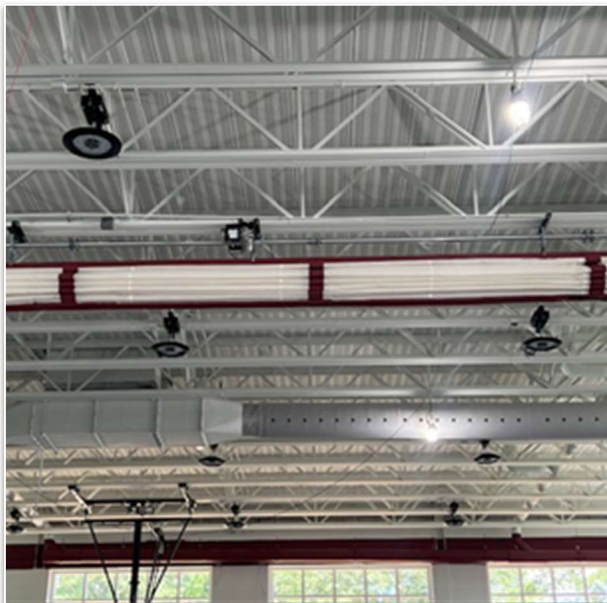


GYM Lights Installation at CAS



Bath Accessories Installation at CAS




Flooring preparation at KRS

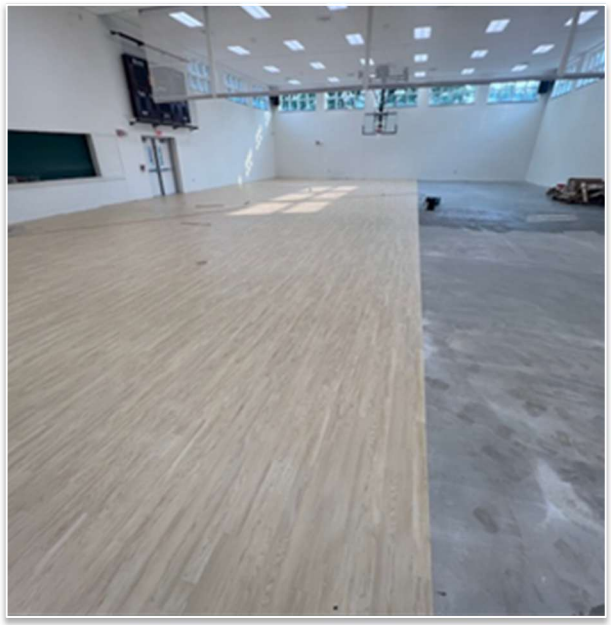

LVT Flooring Installation at KRS



Camera Installation at KRS

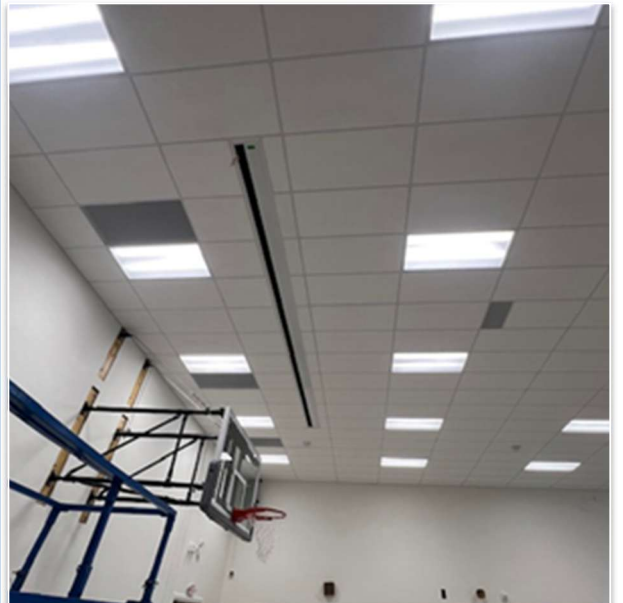

Projector Screen Finalized at KRS
