



**Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
February 13, 2026**

A. Activities performed for the period of February 9 – February 13, 2026

• **Central Ave School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review and layout.
- Continued installation of roof drains.
- Continued hanger installation and rough plumbing work.
- Continued lavatory rack installation.
- Recommended electrical work for conduit and boxes.
- Recommended CMU installation and grout placement.
- Installation of blocking for HVAC curbs and parapet walls will continue to proceed.
- Continued snow removal operations at roof levels and access to building pad.
- Held Pre-con Roofing Meeting.

• **Kings Road School:**

- Continued submittal and RFI review process.
- Continued township and third-party inspections.
- Maintain soil management and erosion control protection.
- Continued review and layout.
- Commenced grading for haunches and transition preparation.
- Commenced layout of roof drains.
- Recommended electrical work for conduit and boxes.
- Wiring and installation of temporary heating units.
- Commenced snow removal operations at roof levels and access to building pad.
- Installed plastic sheeting for heat retention due to winter conditions.
- Held Pre-con Roofing meeting.

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106



B. Projected Activities for period of February 16 – February 20, 2026

• **Central Ave School:**


- Continue submittal and RFI process.
- Continue township and third-party inspections.
- Continue mobilization of trades.
- Maintain soil management and soil erosion control measures.
- Winter storm cleanup activities.
- Continue electrical activities.
- Continue plumbing activities.
- Continue roof drain installation.
- Continue CMU mobilization and deliveries.
- Continue installation of CMU walls.
- Grout placement for CMU walls will resume progression.
- Installation of blocking for HVAC curbs and parapet walls will continue to proceed.

• **Kings Road School:**

- Continue submittal and RFI process.
- Continue Madison Township and third-party inspections.
- Continue mobilization of trades.
- Continue delivery of materials.
- Continue soil management and soil erosion control measures.
- Winter storm cleanup activities.
- Recommence demolition of adjacent 2 ft. walls at existing building.
- Continue slab on grade preparation activities.
- Discuss logistics for crane placement.
- Recommence CMU installation at east and south walls.
- Layout of blocking for HVAC curbs and parapet walls will commence.
- Recommence placement of loose lintels on the east side.
- Continue conduit and electrical work at CMU walls.
- Commence preparation, layout and installation of parapet walls.




Lavatory racks installation at CAS

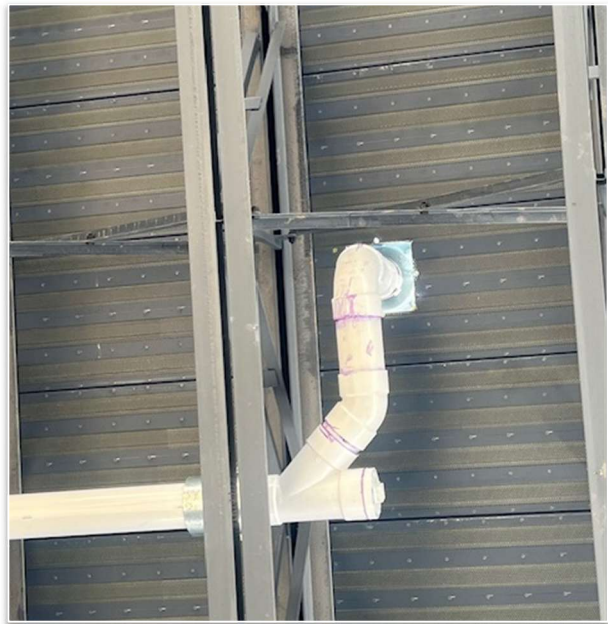

PVC and Roof drain Installation at CAS



Grout and rebar placement at CAS

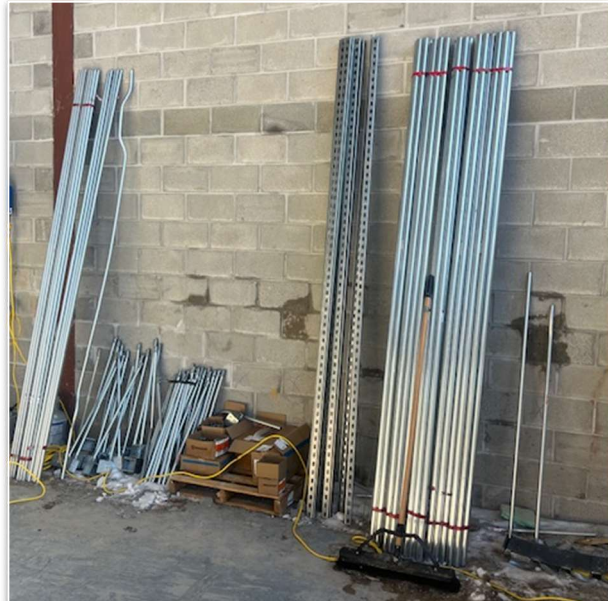


Electrical preparation CAS



Machinery delivery at KRS



Plastic sheeting Installation at KRS

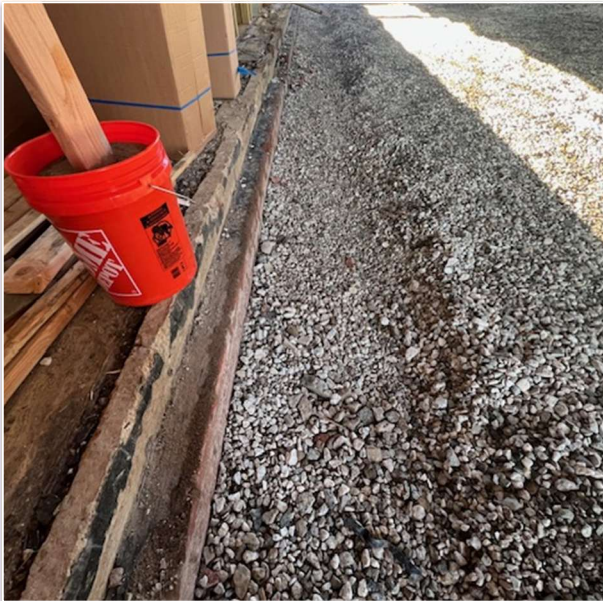

Grading for haunches at KRS



Temporary Heaters at KRS
