



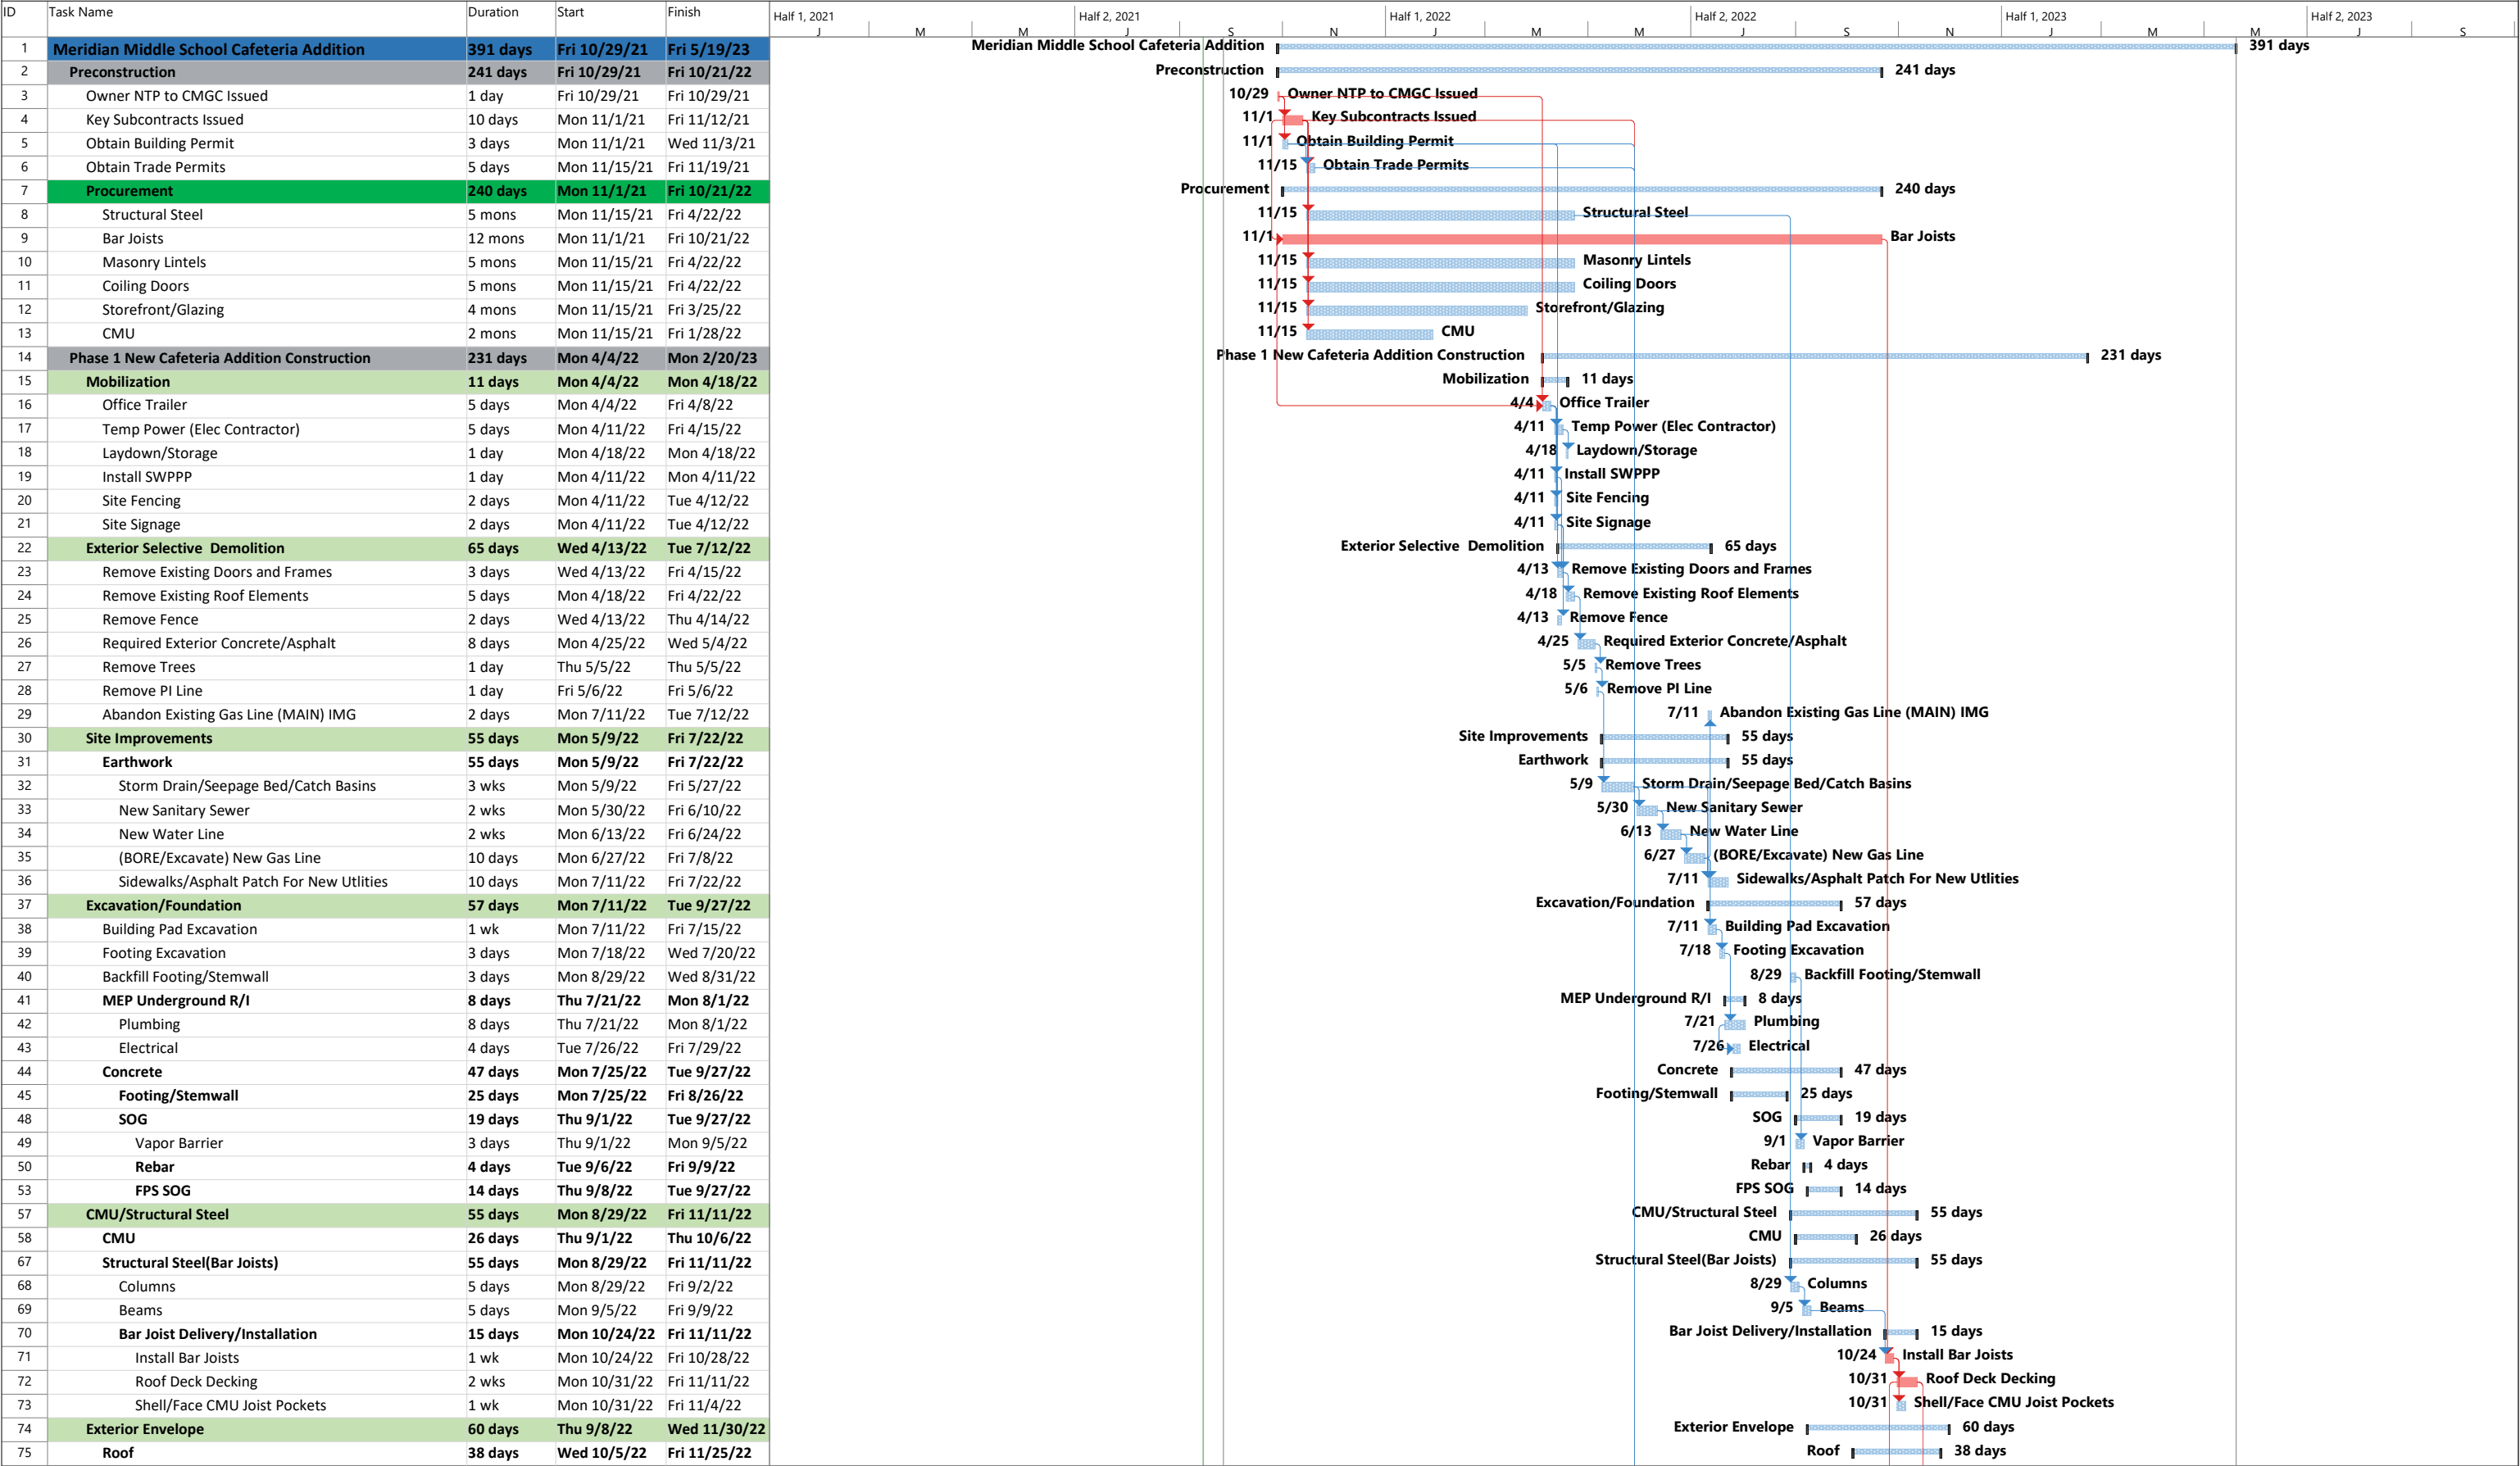

ID	Task Name	Duration	Start	Finish	Half 1, 2021	Half 2, 2021	Half 1, 2022	Half 2, 2022	Half 1, 2023	Half 2, 2023
76	Expansion Joints	10 days	Wed 10/5/22	Tue 10/18/22						
77	Re-Roof Existing	5 days	Wed 11/9/22	Tue 11/15/22						
78	TPO New Structure	2 wks	Mon 11/14/22	Fri 11/25/22						
79	HVAC Equipment	3 days	Mon 11/28/22	Wed 11/30/22						
80	Exterior Soffit Framing	57 days	Thu 9/8/22	Fri 11/25/22						
81	Exterior Soffit/Fascia Framing	10 days	Mon 11/14/22	Fri 11/25/22						
82	Parapet Framing	5 days	Wed 11/2/22	Tue 11/8/22						
83	Doors and Windows	34 days	Thu 9/8/22	Tue 10/25/22						
84	HM Frames in CMU	3 days	Thu 9/8/22	Mon 9/12/22						
85	Storefront	15 days	Wed 10/5/22	Tue 10/25/22						
86	Frames	5 days	Wed 10/5/22	Tue 10/11/22						
87	Glazing	5 days	Wed 10/19/22	Tue 10/25/22						
88	Interior Buildout	61 days	Mon 11/28/22	Mon 2/20/23						
89	Interior Selective Demolition	10 days	Mon 11/28/22	Fri 12/9/22						
90	Demo Existing HM Doors/Frames	1 wk	Mon 11/28/22	Fri 12/2/22						
91	Demo CMU for Coiling Doors	1 wk	Mon 12/5/22	Fri 12/9/22						
92	Metal Wall Framing	10 days	Mon 11/28/22	Fri 12/9/22						
94	Metal Ceiling Framing	3 days	Mon 12/12/22	Wed 12/14/22						
96	MEP+F R/I	43 days	Mon 12/12/22	Wed 2/8/23						
97	Plumbing R/I	2 wks	Mon 12/12/22	Fri 12/23/22						
98	Mechainical R/I	2 wks	Mon 12/26/22	Fri 1/6/23						
99	Electrical R/I	13 days	Mon 1/9/23	Wed 1/25/23						
100	Fire Suppression R/I	2 wks	Thu 1/26/23	Wed 2/8/23						
101	Interior Doors/Windows	9 days	Mon 12/12/22	Thu 12/22/22						
102	O/H Coiling Doors	4 days	Mon 12/12/22	Thu 12/15/22						
103	HM Frames	3 days	Mon 12/12/22	Wed 12/14/22						
104	Storefront Frames	3 days	Mon 12/12/22	Wed 12/14/22						
105	Glazing	3 days	Thu 12/15/22	Mon 12/19/22						
106	Wood Doors	3 days	Tue 12/20/22	Thu 12/22/22						
107	Storefront Doors	2 days	Thu 12/15/22	Fri 12/16/22						
108	GWB	61 days	Mon 11/28/22	Mon 2/20/23						
109	Ceilings	3 days	Thu 12/15/22	Mon 12/19/22						
110	Walls	8 days	Mon 12/12/22	Wed 12/21/22						
111	Tape	1 wk	Thu 12/22/22	Wed 12/28/22						
112	Interior Finishes	44 days	Mon 11/28/22	Thu 1/26/23						
113	Paint	29 days	Mon 11/28/22	Thu 1/5/23						
117	ACT	24 days	Mon 12/26/22	Thu 1/26/23						
121	MEP Trim Out	51 days	Mon 12/12/22	Mon 2/20/23						
122	Electrical	32 days	Fri 1/6/23	Mon 2/20/23						
123	Power	20 days	Fri 1/6/23	Thu 2/2/23						
124	Overhead	5 days	Fri 1/27/23	Thu 2/2/23						
125	Walls	5 days	Fri 1/6/23	Thu 1/12/23						
126	Lights	8 days	Thu 2/9/23	Mon 2/20/23						
127	PA/Fire Alarm	8 days	Fri 1/27/23	Tue 2/7/23						
128	HVAC	14 days	Fri 1/20/23	Wed 2/8/23						
131	Plumbing	5 days	Fri 1/13/23	Thu 1/19/23						
133	Fire Suppression	38 days	Mon 12/12/22	Wed 2/1/23						
134	Kitchen	4 days	Fri 1/27/23	Wed 2/1/23						
135	Cafeteria	5 days	Mon 12/12/22	Fri 12/16/22						
136	Hall 101	5 days	Mon 12/19/22	Fri 12/23/22						
137	Flooring	39 days	Mon 12/26/22	Thu 2/16/23						
138	Sheet Flooring	11 days	Tue 1/17/23	Tue 1/31/23						
141	VCT	39 days	Mon 12/26/22	Thu 2/16/23						
145	Kitchen Equipment	18 days	Fri 1/20/23	Tue 2/14/23						
146	Walk-In Cooler/Freezer	5 days	Fri 1/20/23	Thu 1/26/23						
147	Shelving	3 days	Fri 1/27/23	Tue 1/31/23						
148	Mobile Equipment	5 days	Wed 2/1/23	Tue 2/7/23						
149	Rolling Racks/Shelving	5 days	Wed 2/1/23	Tue 2/7/23						
150	Stationary Equipment	10 days	Wed 2/1/23	Tue 2/14/23						
151	Racks/Shelving	5 days	Wed 2/1/23	Tue 2/7/23						

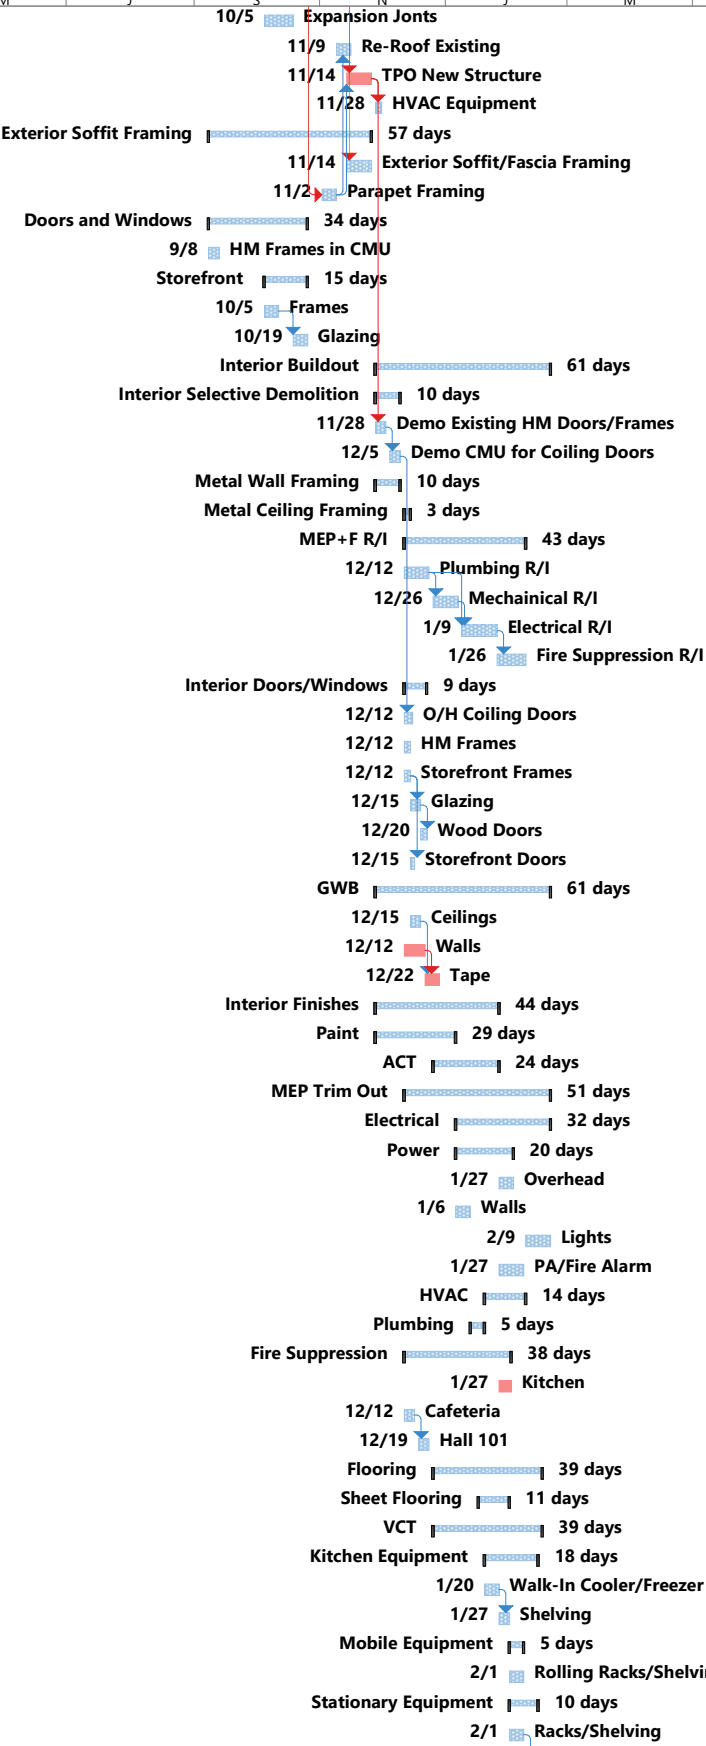

Andersen Construction				Meridian Middle School Cafeteria Addition																Wed 9/15/21						
				Construction Schedule																						
D	Task Name	Duration	Start	Finish	Half 1, 2021			Half 2, 2021			Half 1, 2022			Half 2, 2022			Half 1, 2023			Half 2, 2023						
					J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S					
152	Dish Washing Station	5 days	Wed 2/8/23	Tue 2/14/23																	2/8	Dish Washing Station				
153	Steam Kettles	5 days	Wed 2/1/23	Tue 2/7/23																	2/1	Steam Kettles				
154	Wall Finishes	5 days	Fri 1/6/23	Thu 1/12/23																	1/6	Wall Finishes	5 days			
155	Stainless Steel	2 days	Fri 1/6/23	Mon 1/9/23																	1/6	Stainless Steel				
156	FRP	2 days	Tue 1/10/23	Wed 1/11/23																	1/10	FRP				
157	Corner Guards	1 day	Thu 1/12/23	Thu 1/12/23																	1/12	Corner Guards				
158	Millwork	13 days	Fri 12/30/22	Tue 1/17/23																	12/30	Millwork	13 days			
159	Offices	2 wks	Fri 12/30/22	Thu 1/12/23																	12/30	Offices				
160	Interior/Exterior Signage	3 days	Fri 1/13/23	Tue 1/17/23																	1/13	Interior/Exterior Signage				
161	Turnover	2 days	Fri 2/17/23	Mon 2/20/23																	2/17	Turnover	2 days			
162	Final Inspections	1 day	Fri 2/17/23	Fri 2/17/23																	2/17	Final Inspections				
163	Substantial Completion Cafeteria Addition	1 day	Mon 2/20/23	Mon 2/20/23																	2/20	Substantial Completion Cafeteria Addition				
164	Phase 2 Tenent Improvement	59 days	Tue 2/28/23	Fri 5/19/23																	2/28	Phase 2 Tenent Improvement	59 days			
165	Demolition Kitchen/Restrooms	20 days	Tue 2/28/23	Mon 3/27/23																	2/28	Demolition Kitchen/Restrooms	20 days			
166	Electrical	5 days	Tue 2/28/23	Mon 3/6/23																	2/28	Electrical				
167	HVAC	5 days	Tue 3/7/23	Mon 3/13/23																	3/7	HVAC				
168	Plumbing	5 days	Tue 3/7/23	Mon 3/13/23																	3/7	Plumbing				
169	SOG Demo	7 days	Fri 3/17/23	Mon 3/27/23																	3/17	SOG Demo				
170	Concrete	12 days	Tue 3/28/23	Wed 4/12/23																	3/28	Concrete	12 days			
171	Sub Grade Prep	5 days	Tue 3/28/23	Mon 4/3/23																	3/28	Sub Grade Prep				
172	Vapor Barrier	2 days	Tue 4/4/23	Wed 4/5/23																	4/4	Vapor Barrier				
173	Re-Bar	2 days	Thu 4/6/23	Fri 4/7/23																	4/6	Re-Bar				
174	Place SOG	3 days	Mon 4/10/23	Wed 4/12/23																	4/10	Place SOG				
175	Underground R/I	5 days	Tue 4/4/23	Mon 4/10/23																	4/4	Underground R/I	5 days			
176	Plumbing	5 days	Tue 4/4/23	Mon 4/10/23																	4/4	Plumbing				
177	Electrical	3 days	Tue 4/4/23	Thu 4/6/23																	4/4	Electrical				
178	CMU	27 days	Thu 4/13/23	Fri 5/19/23																	4/13	CMU	27 days			
179	8"	5 days	Thu 4/13/23	Wed 4/19/23																	4/13	8"				
180	6"	5 days	Thu 4/13/23	Wed 4/19/23																	4/13	6"				
181	MEP R/I in CMU/Ceilings	10 days	Thu 4/20/23	Wed 5/3/23																	4/20	MEP R/I in CMU/Ceilings	10 days			
182	Plumbing	5 days	Thu 4/20/23	Wed 4/26/23																	4/20	Plumbing				
183	HVAC	6 days	Thu 4/20/23	Thu 4/27/23																	4/20	HVAC				
184	Electrical	5 days	Thu 4/27/23	Wed 5/3/23																	4/27	Electrical				
185	Interior Framing	7 days	Thu 5/4/23	Fri 5/12/23																	5/4	Interior Framing	7 days			
186	Ceilings	5 days	Thu 5/4/23	Wed 5/10/23																	5/4	Ceilings				
187	Patching	2 days	Thu 5/11/23	Fri 5/12/23																	5/11	Patching				
188	GWB/Tape	7 days	Thu 5/11/23	Fri 5/19/23																	5/11	GWB/Tape	7 days			
189	Ceilings	5 days	Thu 5/11/23	Wed 5/17/23																	5/11	Ceilings				
190	Patching	2 days	Thu 5/18/23	Fri 5/19/23																	5/18	Patching				
191	Interior Finishes	15 days	Mon 4/24/23	Fri 5/12/23																	4/24	Interior Finishes	15 days			
192	Paint	3 days	Mon 4/24/23	Wed 4/26/23																	4/24	Paint				
193	Wall Tile	5 days	Thu 4/27/23	Wed 5/3/23																	4/27	Wall Tile				
194	MEPF Trim	12 days	Thu 4/27/23	Fri 5/12/23																	4/27	MEPF Trim	12 days			
195	Plumbing	4 days	Thu 4/27/23	Tue 5/2/23																	5/2	Plumbing				
196	HVAC	4 days	Wed 5/3/23	Mon 5/8/23																	5/3	HVAC				
197	Electrical	4 days	Tue 5/9/23	Fri 5/12/23																	5/9	Electrical				
198	Flooring	7 days	Wed 5/3/23	Thu 5/11/23																	5/3	Flooring	7 days			
199	VCT	4 days	Mon 5/8/23	Thu 5/11/23																	5/8	VCT				
200	Sheet Flooring	3 days	Wed 5/3/23	Fri 5/5/23																	5/3	Sheet Flooring				
201	Fire Alarm Retro Fit ALL Buildings	49 days	Mon 5/30/22	Thu 8/4/22																	5/30	Fire Alarm Retro Fit ALL Buildings	49 days			
202	Bldg 100 127 devices +-	10 days	Mon 5/30/22	Fri 6/10/22																	6/10	Bldg 100 127 devices +-				
203	Bldg 200 67 devices +-	6 days	Mon 6/13/22	Mon 6/20/22																	6/13	Bldg 200 67 devices +-				
204	Bldg 300 30 devices +-	5 days	Tue 6/21/22	Mon 6/27/22																	6/21	Bldg 300 30 devices +-				
205	Bldg 400 10 devices +-	3 days	Tue 6/28/22	Thu 6/30/22																	6/28	Bldg 400 10 devices +-				
206	Bldg 500 20 devices +-	4 days	Fri 7/1/22	Wed 7/6/22																	7/1	Bldg 500 20 devices +-				
207	Bldg 600 32 devices +-	4 days	Thu 7/7/22	Tue 7/12/22																	7/7	Bldg 600 32 devices +-				
208	Bldg 700 46 devices +-	6 days	Wed 7/13/22	Wed 7/20/22																	7/13	Bldg 700 46 devices +-				
209	Bldg 800 (existing)50 total (includeing new build)	8 days	Thu 7/21/22	Mon 8/1/22																	7/21	Bldg 800 (existing)50 total (includeing new build)				
210	Bldg 900 4 devices +- 2nd floor	3 days	Tue 8/2/22	Thu 8/4/22																	8/2	Bldg 900 4 devices +- 2nd floor				
