


PROJECT UPDATE

Issue No. 19
May 2026

Coupland Jr High & High School




Aerial View - Overall (05.12.2026)

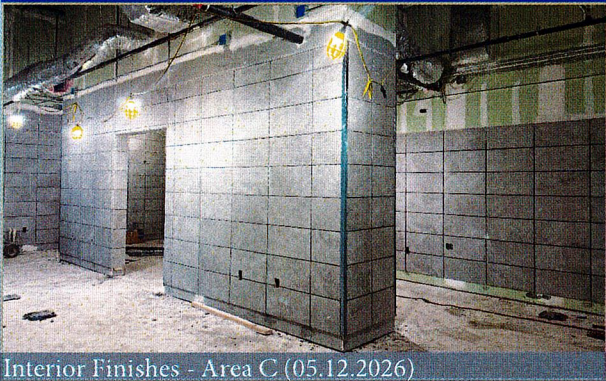

Interior Finishes - Area C (05.12.2026)



Casework Stored On Site (05.12.2026)

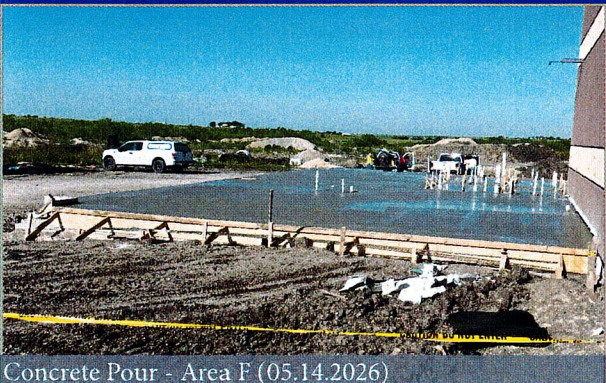

Concrete Pour - Area F (05.14.2026)

Progress to Date

Site

- Began grading for driveways and paving.
- Continued storm drain installation.

Building

- Areas A, B, C, D, & G:
 - Continued insallation of exteior finishes (Metal Panel) at front entrance of Area A.
 - Continued installation of wall tile in Area C.
 - Continued application of paint and texture finishes in all Areas.
 - Continued ceiling grid installation in Area A & B.
 - Began installation of overhead canopies above doorways.
 - Casework was delivered.
- Area F:
 - Completed concrete slab pour.

Looking Ahead

Site

- Continue site prep for concrete drives and parking.

Building

- Areas A, B, C, D, & G:
 - Begin floor tile installation in Area C.
 - Begin wall tile installation in other Areas.
 - Begin casework installaion in all Areas.
 - Complete overhead canopy installation.
 - Complete paint and texture application in all Areas.
- Area F:
 - Begin steel installation and framing.

2023 BOND PROJECT

- Schedule for Current GMP
- Progress of Current Phase
- GMP Money Authorized to Date

Date of Substantial Completion: August 2026	100%	GMP \$22,394,917
08/26		
07/26		
06/26		
05/26		
04/26	83%	\$18,638,014
03/06		
02/26		
01/26		
12/25		
11/25		
10/25		
09/25		
08/25		
07/25		
06/25		
05/25		
04/25		
03/25		
02/25		
01/25		
12/24		
11/24		
10/24		
09/24		



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

