



PROJECT UPDATE

Issue No. 15
January 2026

Coupland Jr High & High School

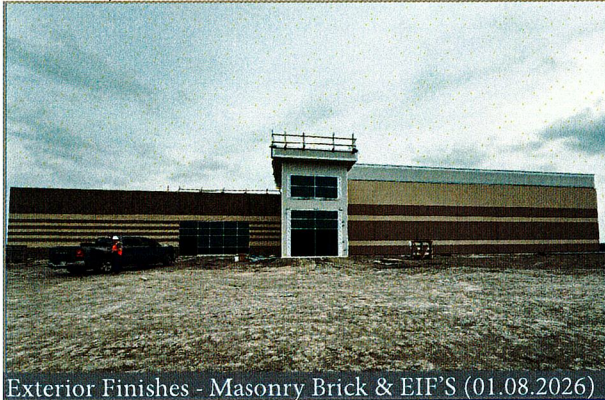


Exterior Finishes - Masonry Brick & EIF'S (01.08.2026)

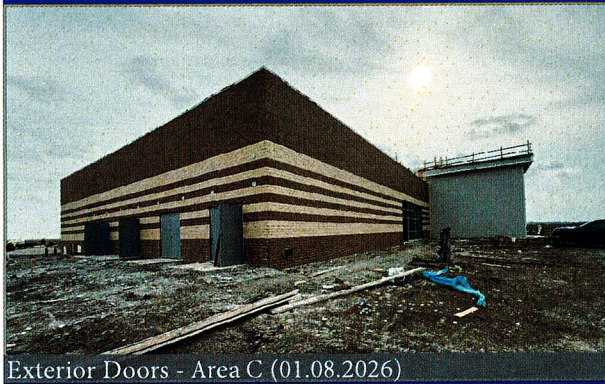

Exterior Doors - Area C (01.08.2026)



Media Center - Area G (01.08.2026)

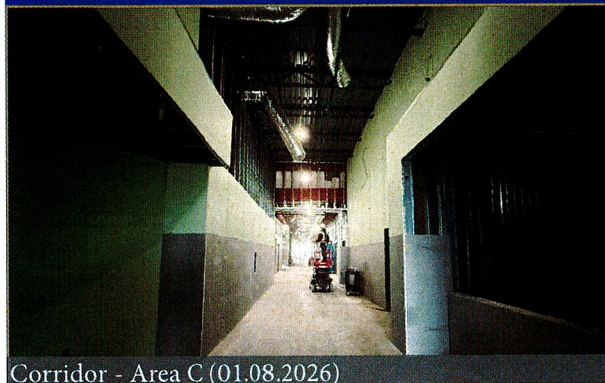

Corridor - Area C (01.08.2026)

Progress to Date

Building

- Continued rigid thermal insulation installation.
- Continued interior gypsum wall board installation.
- Continued exterior door installation.
- Continued plumbing rough-in installation.
- Continued electrical rough-in installation.
- Completed interior & exterior storefront window installation in all area's.
- Completed interior metal stud installation.
- Completed furdawn installation.
- Completed overhead HVAC ductwork installation.
- Completed exterior EIF's installation.

Looking Ahead

Building

- Begin awning installation.
- Begin temporary wall installation.
- Begin interior finishes installation.
- Complete exterior finish installation (Metal Panel & Masonry Brick).
- Complete ceiling grid installation.
- Complete french drain installation.
- Begin door hardware installation.

2023 BOND PROJECT

-  Schedule for Current GMP
-  Progress of Current Phase
-  GMP Money Authorized to Date

Date of Substantial
Completion:
June 2026

100%

GMP
\$20,922,742

Date of Substantial Completion:	100%	GMP
06/26		
05/26		
04/26		
03/06		
02/26		
01/26		
12/25		
11/25	65%	\$13,523,168
10/25		
09/25		
08/25		
07/25		
06/25		
05/25		
04/25		
03/25		
02/25		
01/25		
12/24		
11/24		
10/24		
09/24		



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

