

PROJECT UPDATE

Issue No. 16
February 2026


Coupland Jr High & High School



Exterior Finishes - Metal Panel (02.06.2026)



Control Joints - Interior (02.06.2026)

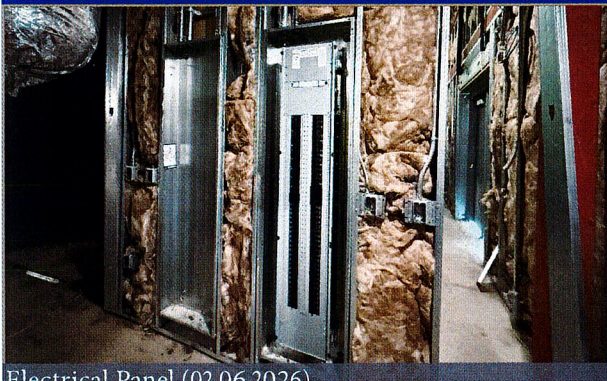

Electrical Panel (02.06.2026)



Media Center - Area G (02.06.2026)

Progress to Date

Site

- Exterior finishes have been delivered on site (Metal Panel).

Building

- Continued interior gypsum wall board installation.
- Continued exterior door installation.
- Continued plumbing rough-in installation.
- Continued electrical rough-in installation.
- Continued exterior finish installation (Masonry Brick).
- Continued control joint installation.
- Completed temporary wall installation.

Looking Ahead

Building

- Begin awning installation.
- Begin interior finishes installation.
- Begin exterior finish installation (Metal Panel).
- Begin exterior door hardware installation.
- Complete ceiling grid installation.
- Complete french drain installation.

2023 BOND PROJECT



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

