

PROJECT UPDATE

Issue No. 22
August 2026

Coupland Jr High & High School



Site Paving - Concrete Drive (08.10.2026)



Wall Graphics - Area A Vestibule (08.10.2026)



Gymnasium Bleachers - Area D (08.10.2026)



Exterior - Area F (08.10.2026)

Progress to Date

Site

- Continued forming & pouring near cafeteria drive for concrete site paving. All other areas completed.

Building

- Areas A, B, C, D & G:
 - Punch list items to be verified.
 - Painted wall graphics have been completed in all areas.
 - Gymnasium bleachers are currently being installed.
 - Fire marshal has signed off on full occupancy.
- Area F:
 - Roof curbs have been installed for the AC units.
 - Began installation of roofing.

Looking Ahead


Site

- Lift station scheduled to arrive on site next week.
- Concrete flumes scheduled to be installed next week.

Building

- Areas A, B, C, D, & G:
 - Backlit building letters will be installed today.
 - Trainings to be coordinated with the district.
 - Gymnasium flooring scheduled to resume next week.
- Area F:
 - Begin waterproofing installation.
 - Begin installation of electrical feeders.
 - Begin hard-lit ceiling installation.
 - Begin overhead plumbing.

2023 BOND PROJECT

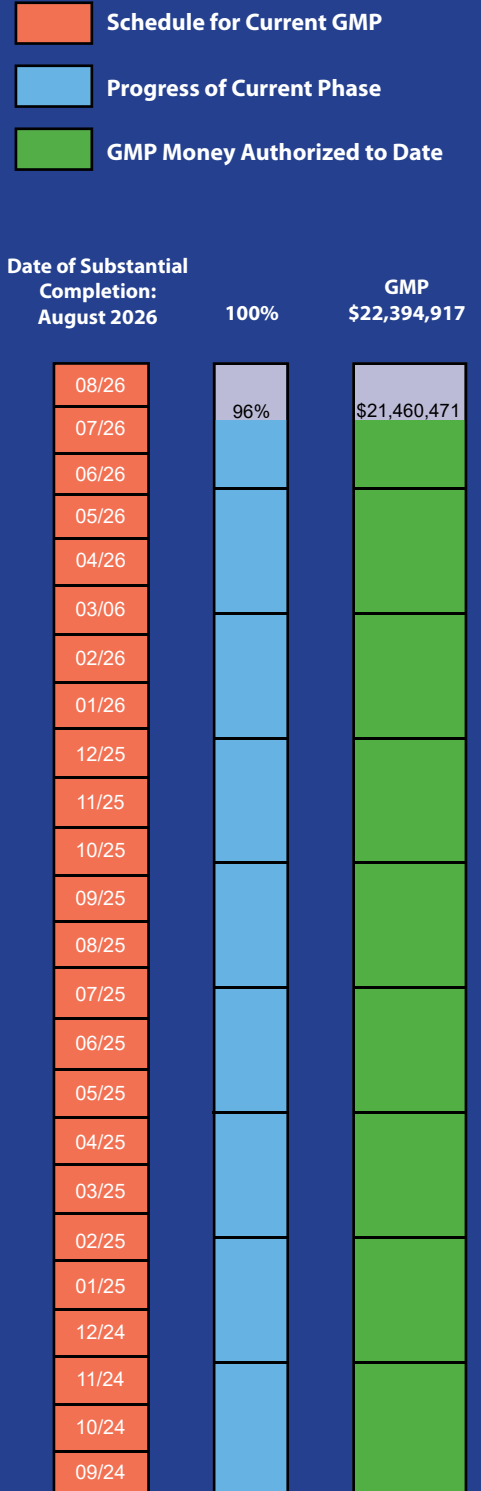

COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

