

PROJECT UPDATE

Issue No. 11
September 2025

Coupland Middle School




Steel - Area A, B, C, D & G (09.04.2025)



Area D - Gymnasium (09.04.2025)



Exterior Metal Study Framing - Area C (09.04.2025)

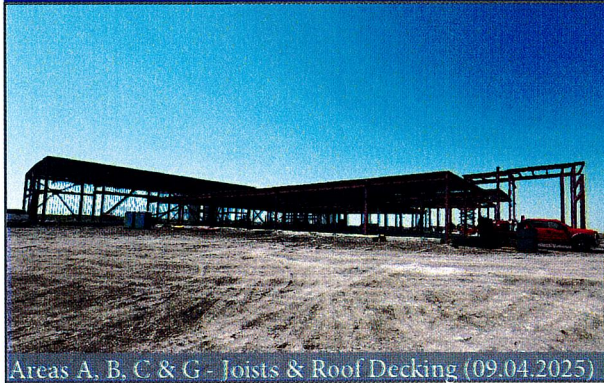

Areas A, B, C & G - Joists & Roof Decking (09.04.2025)

Progress to Date

Building

- Began Metal decking installation in areas B, C & D.
- Began RTU frame installation.
- Continued exterior metal stud installation in areas C & D.
- Continued steel detailing in all areas.
- Completed steel erection in areas A & G.

Looking Ahead

Site

- Continued sewer line for lift station installation.
- Begin water Line installation.

Building

- Complete steel detailing in all areas.
- Continue exterior metal stud framing.
- Continue metal roof deck installation.

2023 BOND PROJECT

-  Schedule for Current GMP
-  Progress of Current Phase
-  GMP Money Authorized to Date

Date of Substantial
Completion:
June 2026

100%

GMP
\$20,922,742

06/26		
05/26		
04/26		
03/06		
02/26		
01/26		
12/25		
11/25		
10/25		
09/25		
08/25		
07/25	45%	\$9,499,082
06/25		
05/25		
04/25		
03/25		
02/25		
01/25		
12/24		
11/24		
10/24		
09/24		



COUPLAND ISD
COUPLAND MIDDLE SCHOOL

