



PROJECT UPDATE

Issue No. 24
October 2026

Coupland Jr High & High School

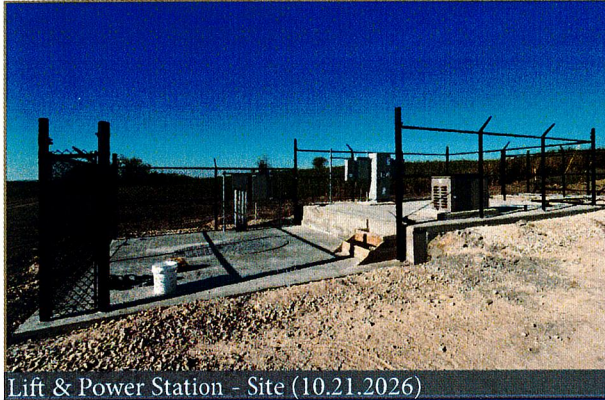


Lift & Power Station - Site (10.21.2026)

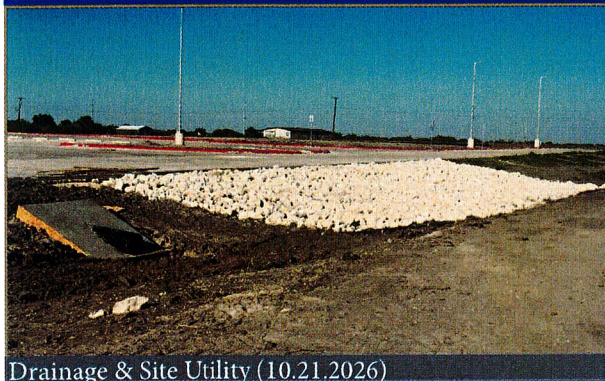

Drainage & Site Utility (10.21.2026)



Interior Finishes (Corridor)- Area F (10.21.2026)

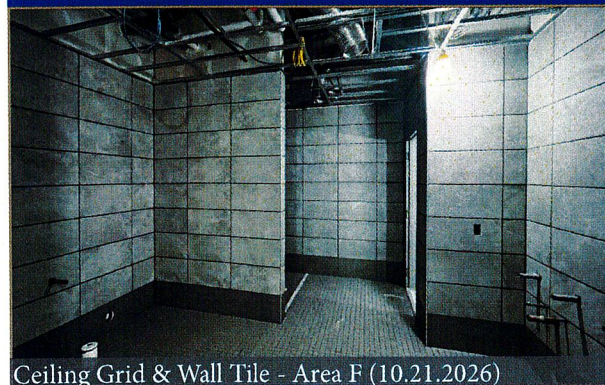

Ceiling Grid & Wall Tile - Area F (10.21.2026)

Progress to Date

Site

- Continued installation of the power & lift station.
- Completed installation of flag poles at front of school.
- Rip rap installation has begun.
- Headwall placement has begun.

Building

- Area A, C, & D:
 - Completed concrete sidewalk pour behind Area C.
 - Continued punch list verification.
- Area F:
 - Exterior finish (EIFS) installation has begun.
 - Ceiling grid installation has begun.
 - Hard lid inspections began.
 - Began sheet rock hard lids.
 - First coat on walls has been completed.
 - Wall tile installation has been completed.

Looking Ahead

Site

- Complete headwall and rip rap installation.

Building

- Areas A, B, C, D, & G:
 - Begin Ansul fire-suppression system testing.
 - Continued work on punch list items.
- Area F:
 - Begin running the RTU systems.
 - Complete exterior finish (EIFS) installation.
 - Complete interior finish installation.
 - Complete ceiling grid & tile installation.

2023 BOND PROJECT

- Schedule for Current GMP
- Progress of Current Phase
- GMP Money Authorized to Date

Date of Substantial
Completion:
August 2026

100%

GMP
\$22,394,917

08/26	99%	\$22,220,584
07/26		
06/26		
05/26		
04/26		
03/06		
02/26		
01/26		
12/25		
11/25		
10/25		
09/25		
08/25		
07/25		
06/25		
05/25		
04/25		
03/25		
02/25		
01/25		
12/24		
11/24		
10/24		
09/24		



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

