


PROJECT UPDATE

Issue No. 17
March 2026

Coupland Jr High & High School




Exterior Finishes - Metal Panel (03.05.2026)

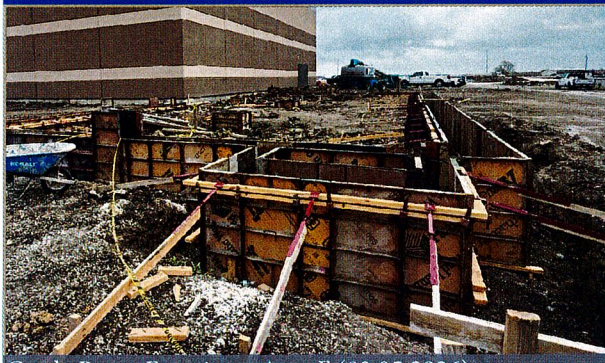

Grade Beam Forming - Area F (03.05.2026)



Electrical Transformer - Site (03.05.2026)

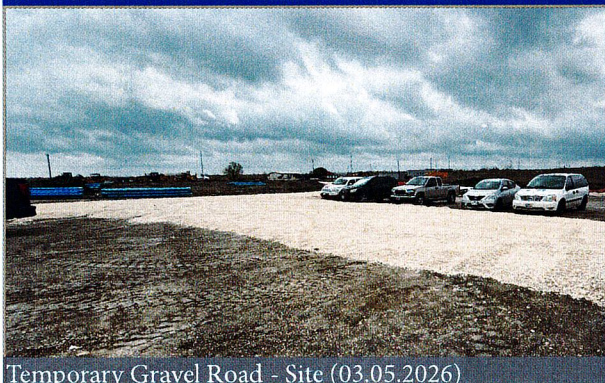

Temporary Gravel Road - Site (03.05.2026)

Progress to Date

Site

- Electrical transformer has been installed on site.
- Temporary gravel road has been installed on site for emergency vehicle access.
- Continued french drain installation.

Building

- Areas A, B, C, D, & G
 - Began exterior metal panel installation.
 - Continued interior gypsum wall board installation.
- Area F:
 - Subgrade testing continues to verify proper compaction.
 - Continued concrete strength testing for piers.
 - Began grade beam forming.

Looking Ahead

Site

- Begin pouring site concrete drives.
- Continue underground utility installation.
- Complete french drain installation.

Building

- Areas A, B, C, D, & G
 - Begin awning installation.
 - Continue interior finishes installation.
- Area F
 - Begin underground void box system installation for plumbing.
 - Begin underslab utility installation.
 - Begin grade beam concrete pours.


2023 BOND PROJECT

- Schedule for Current GMP
- Progress of Current Phase
- GMP Money Authorized to Date

Date of Substantial
Completion:
August 2026

100%

GMP
\$22,394,917

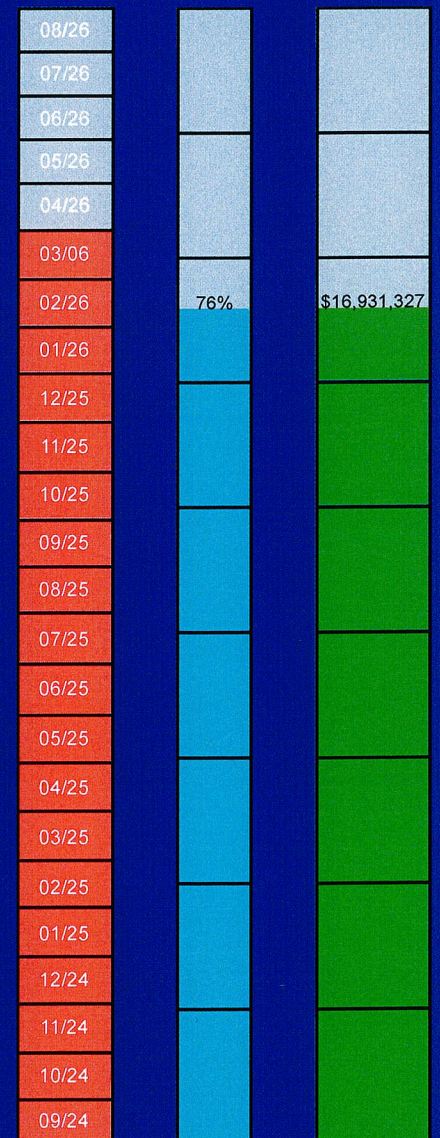

COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

