



PROJECT UPDATE

Issue No. 12
October 2025


Coupland Jr High & High School

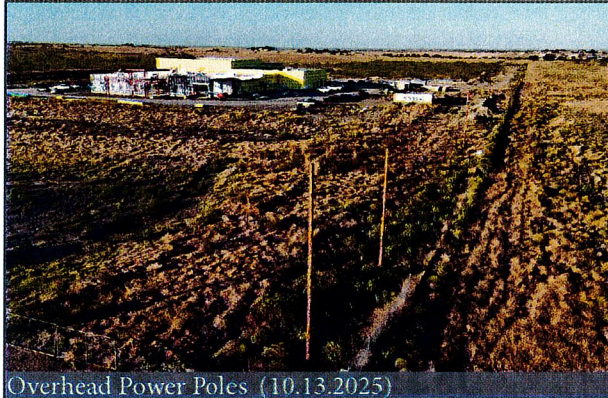

Overhead Power Poles (10.13.2025)

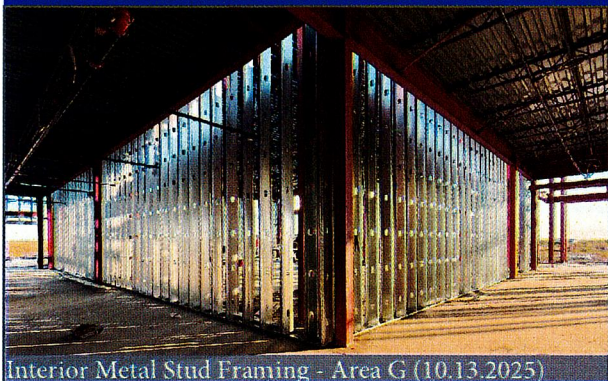

Interior Metal Stud Framing - Area G (10.13.2025)

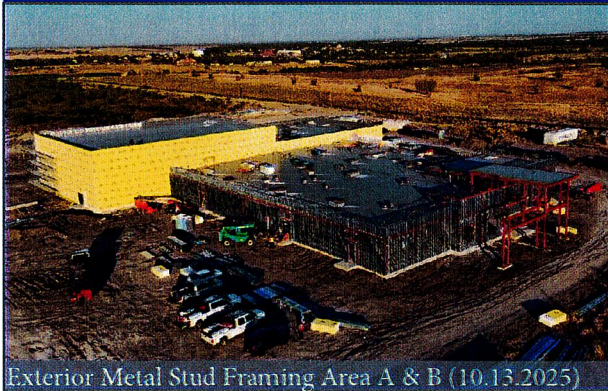

Exterior Metal Stud Framing Area A & B (10.13.2025)



HAVC Ductwork (10.13.2025)

Progress to Date

Site

- Installed overhead power poles.

Building

- Completed Metal roof decking installation in all areas.
- Continued interior metal stud installation in area's A, B, C & G.
- Continued exterior sheathing installation in area's A, B, & G.
- Continued RTU frame installation.
- Continued HVAC ductwork installation.
- Continued steel detailing in all areas.

Looking Ahead

Site

- Continued sewer line for lift station installation.
- Begin water Line installation.

Building

- Complete steel detailing in all areas.
- Begin waterproofing installation in all areas.
- Begin EIF's installtion.
- Begin roofing installation.

2023 BOND PROJECT

- Schedule for Current GMP
- Progress of Current Phase
- GMP Money Authorized to Date

Date of Substantial
Completion:
June 2026

100%

GMP
\$20,922,742

Date of Substantial Completion:	100%	GMP
06/26		
05/26		
04/26		
03/06		
02/26		
01/26		
12/25		
11/25		
10/25		
09/25		
08/25		
07/25	45%	\$9,499,082
06/25		
05/25		
04/25		
03/25		
02/25		
01/25		
12/24		
11/24		
10/24		
09/24		



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

