

PROJECT UPDATE

Issue No. 14
December 2025

Coupland Jr High & High School




Coupland ISD Beam Signing (12.09.2025)



Storefront - Area G (12.09.2025)



Exterior View - Area C (12.09.2025)

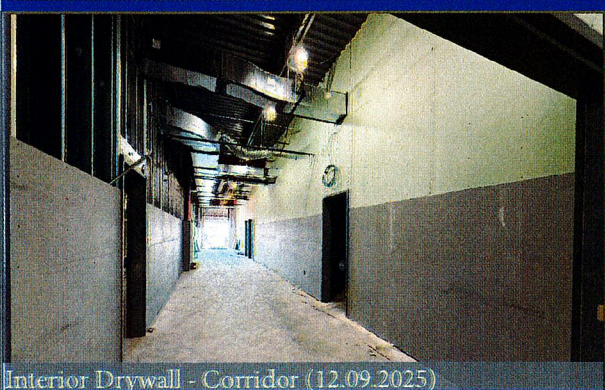

Interior Drywall - Corridor (12.09.2025)

Progress to Date

Building

- Began storefront window installation in all area's.
- Began exterior door installation in all Area's.
- Continued flashing installation at exterior storefront windows.
- Continued exterior wall finish installation (EIF's, Masonry, and Metal Panel).
- Continued Interior Metal Stud installation in Area C.
- Continued drywall installation at all interior locations.

Looking Ahead

Building

- Begin interior finishes installation.
- Continue exterior window and door installation.
- Continue exterior finishes installation.
- Complete metal stud installation.
- Continue interior gypsum board.

2023 BOND PROJECT

- Schedule for Current GMP
- Progress of Current Phase
- GMP Money Authorized to Date

Date of Substantial Completion:	June 2026	100%	GMP \$20,922,742
06/26			
05/26			
04/26			
03/06			
02/26			
01/26			
12/25			
11/25			
10/25			
09/25		58%	\$12,207,821
08/25			
07/25			
06/25			
05/25			
04/25			
03/25			
02/25			
01/25			
12/24			
11/24			
10/24			
09/24			



COUPLAND ISD
COUPLAND JR HIGH & HIGH SCHOOL

