



Spring Hill Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF
6/8-6/12/26

THIS WEEK - 6/8-6/12/26

- Drop Ceiling Tile
- Casework Begins (Delivered) 6/10-6/12 (cont)
- Specialties 6/11-6/12 (cont)
- Fire Alarm Pre -Test 6/12 (cont)


NEXT WEEK - 6/15-6/19/26

- Casework 6/15-6/16
- Specialties 6/15
- Fire Alarm Pre -Test 6/15-6/16
- Flooring 6/17-6/19 (cont)

WEATHER DAYS THIS WEEK



Classroom Signs

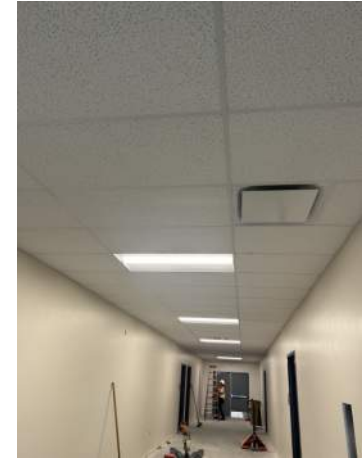

Ceiling Tile Dropped



Stair Rail Complete



Outlets Installed





Prairie Creek Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

6/8-6/12/26

THIS WEEK - 6/8-6/12/26

- Ceiling Clouds Hung 6/10
- Final Grading 6/8-6/9
- Low Voltage 6/8-6/12
- Trim Out MEP 6/8-6/12

NEXT WEEK - 6/15-6/19/26

- Site Concrete 6/15-6/16
- Road Asphalt Patch 6/17-6/18
- Overhead Inspection 6/15
- Bathroom Epoxy Flooring 6/15-6/16
- Doors and Hardware 6/18-6/19
- Landscape 6/17-6/19

WEATHER DAYS THIS WEEK



Trim Out



Acoustical Ceiling Clouds



Display Case Framing



Summer Site Work





Timber Sage Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

6/8-6/12/26

THIS WEEK - 6/8-6/12/26

- Exterior Masonry 6/8-6/12
- Storefront on existing Building 6/8
- Caulk Storefront 6/9
- Paint and Prime 6/8-6/9
- Ceiling Grid 6/10-6/12
- Bathroom Wall Tile 6/10-6/12

NEXT WEEK - 6/15-6/19/26

- Storm Drain Downspout Tie in 6/15-6/17
- Final Grading/ Remove Lay down Area 6/18-6/19
- Wash Exterior Brick Down 6/15
- Glazing and Storefront 6/16-6/17
- Exterior Metal Flashing 6/16-6/19
- Set RTU 6/15
- Bathroom Epoxy Flooring 6/15-6/16
- MEP Trim out 6/15-6/19
- Caulk Windows 6/17

WEATHER DAYS THIS WEEK



Masonry Continues



Masonry Continues



Pour Back



Drywall Finishing

