Madison Public Schools
Central Ave School & Kings Road School Additions & Renovations
Project Manager's Weekly Report
April 24, 2026

A. Activities performed for the period of April 20 – April 24, 2026

- **Central Ave School:**

  - Continued submittal and RFI review process.
  - Continued township and third-party inspections.
  - Maintain soil management and erosion control protection.
  - Regrading and added stone continued to be installed at perimeter of site pad as needed.
  - Continued review of scheduling and planning.
  - Electrical activities are continuing to progress.
  - Continued installation of CMU walls.
  - Continued exterior rigid insulation installation.
  - Brick placement has continued.
  - HVAC work has continued.
  - Held roofing coordination meeting.

- **Kings Road School:**

  - Continued submittal and RFI review process.
  - Continued township and third-party inspections.
  - Maintain soil management and erosion control protection.
  - Continued review and layout.
  - Above ceiling and rough electrical work has continued.
  - Installation of flag pole footing with lighting arrester commenced.
  - Continued HVAC ductwork installation.
  - Continued and completed layout and installation of parapet walls.
  - Lay out and form work for sidewalks and stairs continued.
  - Rebar, form installation and concrete placement for sidewalks and stairs are progressing.
  - Held roofing coordination meeting.

B. Projected Activities for period of April 27 – May 1, 2026

- **Central Ave School:**

  - Continue submittal and RFI process.
  - Continue township and third-party inspections.
  - Continue mobilization of trades.
  - Maintain soil management and soil erosion control measures.
  - Regrade and refresh site building pad exterior will continue as needed.
  - Electrical activities will continue with progress.
  - Continue rough above grade plumbing work within the new building.
  - Continue interior CMU cleanup activities.
  - Continue installation of exterior brick.
  - Exterior masonry washdown and cleanup will continue.
  - Commence installation of blocking for coping.
  - Work associated with the installation of the transformer and switch gear will continue.
  - Hold project meeting.

- **Kings Road School:**

  - Continue submittal and RFI process.
  - Continue Madison Township and third-party inspections.
  - Continue mobilization of trades.
  - Continue delivery of materials.
  - Continue soil management and soil erosion control measures.
  - Grading and seeding preparation will commence.
  - Block retaining wall installation will commence.
  - Transition work at slabs will continue.
  - Continuing conduit and electrical work at existing interior walls.
  - Continuing electrical work above and below ceiling within existing building.
  - Continue HVAC ductwork installation.
  - Roofing activities will continue.
  - Continue installation of forms for concrete sidewalks.
  - Work within existing multi-purpose room will continue.
  - Hold project meeting.

Eastern Elevation Brickwork at CAS

Window Installation Staging at CAS

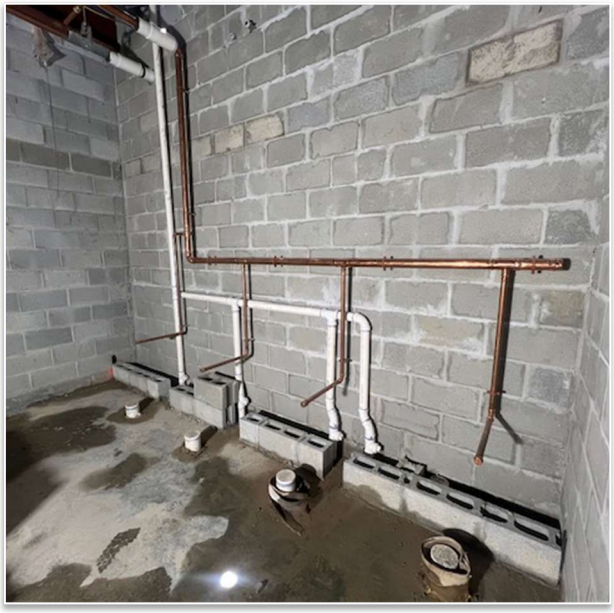

Interior Rough Plumbing at CAS

Northern Elevation Brick Placement at CAS

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106

Safety Shed Removal at KRS

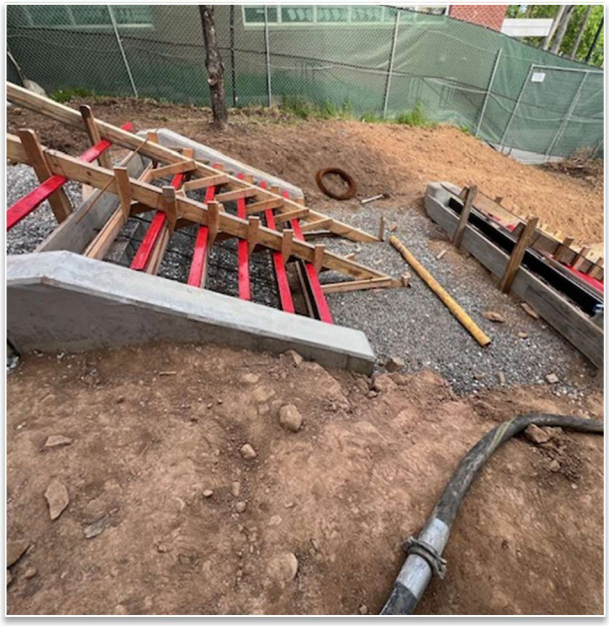

Pump Truck Concrete Placement at KRS

Flagpole Footing and preparation at KRS

Sidewalk and Stair Work at KRS

Epic Management, Inc.

136 Eleventh Street • Piscataway, NJ 08854
732-752-6100 • Fax 732-752-9106
