Spring Hill Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

01/05-01/09/26

THIS WEEK - 01/05-01/09/26

- SOG Pour 1/7
- Strip Forms 1/9
-Cold Formed Metal Framing delivery 1/9
- Blocking Installed around perimeter slab 1/9

NEXT WEEK - 01/12-01/16/26


- 10" Cold Formed Permanent wall construction 1/12-1/14
- Apply Air Barrier at 10" wall 1/15-1/16

WEATHER DAYS THIS WEEK

1/8 Weather Delay




Safety Guard Rails/ Hand Rails

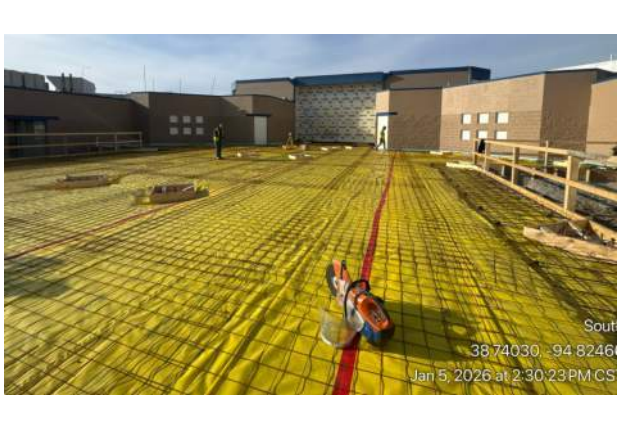

Stego Wrap and Wire Mesh



Slab placement

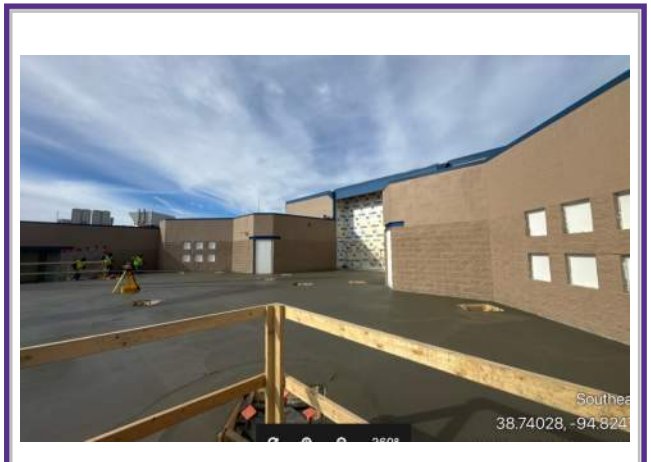

Slab Placed

NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP

Prairie Creek Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

01/05-01/09/26

THIS WEEK - 01/05-01/09/26

- Underground storm line 1/5-1/7
- Demo Stoops 1/9

NEXT WEEK - 01/12-01/16/26

- Building Pad 1/12- 1/13
- Footings and Foundations 1/13-1/16
- Anchor bolt delivery 1/12
- Rebar Delivery 1/13

WEATHER DAYS THIS WEEK

1/8 Rain Weather Delay



Excavating Trench for Storm Line



Storm Line Installed

NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP

Timber Sage Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

01/05-01/09/26

THIS WEEK - 01/05-01/09/26

- Relocate water line 1/5-1/9
- Begin building pad 1/9

NEXT WEEK - 01/12-01/16/26

- Finish Building Pad 1/12-1/13
-Footings and Foundations 1/14-1/16

WEATHER DAYS THIS WEEK


1/8 Weather Delay



Water Line relocate/ Tie in



Tie in complete, Begin Backfill

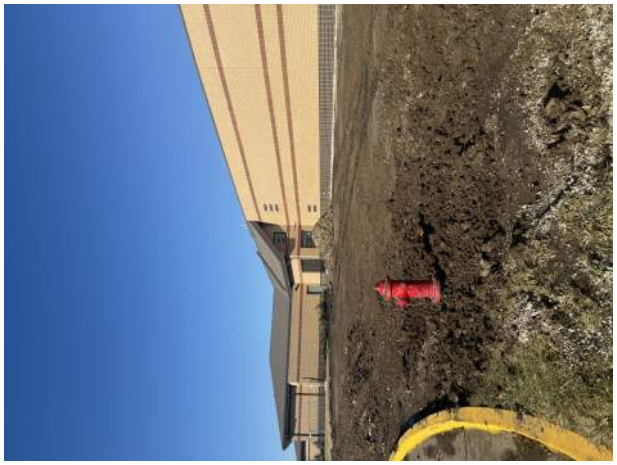

Site Work

NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP
