Spring Hill Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

03/09-03/13/26

THIS WEEK - 03/09-03/13/26

- Ductwork Overhead Rough in- Complete
- Electrical Overhead Rough in 3/9- 3/26
- Plumbing Overhead Rough in- Complete
-In wall blocking 3/9-3/10
- Roofing 3/9-3/20
- Building Dried in 3/13
- in wall Electrical 3/9-3/12
- In wall inspection 3/12

NEXT WEEK - 03/16 -03/20/26

- Temp Windows 3/20-3/23
- Roofing Continues
- Building Dried in 3/23
- Permanent Power Tie in 3/16-3/20
- Run Data Pathways and Sleeves 3/16-3/20
- Insulate Plumbing 3/16-3/20

WEATHER DAYS THIS WEEK



Sheathing and Blocking Complete



OH Duct and Plumbing Complete



Roofing



NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP

Prairie Creek Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

03/09-03/13/26

THIS WEEK - 03/09-03/13/26

- Exterior Framing And sheathing 3/9-3/13
- Window and Door Blocking 3/9-3/11
- Frame Parapet and blocking 3/11-3/13
- Air Barrier and Water Proofing 3/12-3/13
- Interior Framing Begins 3/12-3/13
- Set RTU Curb 3/13

NEXT WEEK - 03/16 -03/20/26

- Air Barrier and Water proofing 3/16 - 3/18
- Roofing 3/18 - 3/20
- Interior Framing 3/16- 3/19
- In wall Blocking 3/20
- In Wall Electrical and plumbing Rough in 3/20
- Conduit Pathways through Mech room 3/16
- 3/20
- Water lines tie in/ insulate 3/16- 3/19
- Sprinkler Main Tie in 3/16- 3/17

WEATHER DAYS THIS WEEK




Exterioir Framing



Decking Installed at Trusses and Flat roof



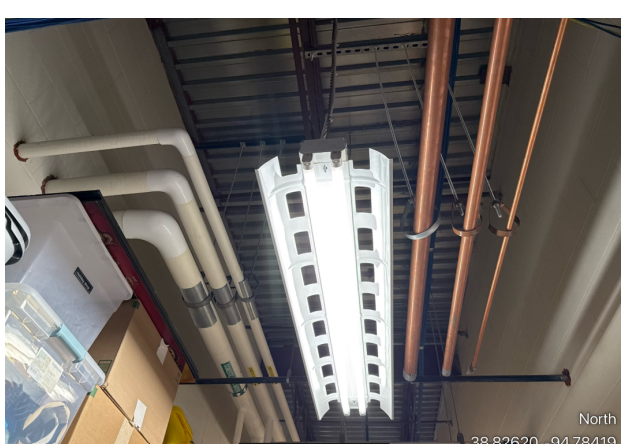

Prep for Spring Break tie-ins

NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP

Timber Sage Elementary

SPRING HILL SCHOOLS

WEEKLY PROGRESS REPORT

WEEK OF

03/09-03/13/26

THIS WEEK - 03/09-03/13/26

- Steel 3/9-3/12
Steel Complete 3/12
- Roof drain Rough in 3/13
- Exterior Framing and Sheathing 3/13
- Run conduit Pathways from main electrical room 3/13
- Set RTU Curb 3/13


NEXT WEEK - 03/16 -03/20/26

- Roof Drain Rough in 3/16
- Exterior Framing and Sheathing 3/16- 3/20
- Set Door Frames 3/18
- Water Lines Tie in/ insulate 3/16-3/20
- Sprinkler Main Tie in 3/17-3/18

WEATHER DAYS THIS WEEK



Beams complete

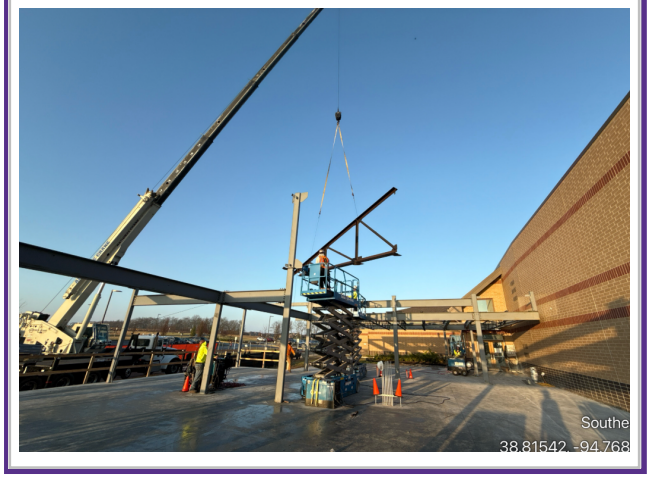

Trusses begin





Tie in Prep for Spring Break

NEWKIRK NOVAK CONSTRUCTION PARTNERS

DLRGROUP
