

Midland CUSD #7
Elementary School Building Demolition

ADDENDUM NO. 1
September 2, 2016

NOTICE:

This Addendum is issued to modify, clarify or change the original drawings, specifications or previous addenda and is hereby made a part of the Contract Documents. Attach this Addendum to your project Specifications and note your receipt of this Addendum on the Bid Form. Failure to recognize any Addendum on the bid form will result in a disqualified bid.

DRAWINGS:

GENERAL INFORMATION:

ADD: Added drawing sheets; C3.2 – Temporary Pavement Plan, S3.1 – Second Floor and Low Roof Framing Plan and S2.5 – Foundation Details. Refer to drawing SK-G001.

CIVIL:

OMIT: Remove exterior concrete stair. Refer to Addendum Sketch SK-C001

CHANGE: Modify the east stair as indicated on Addendum Sketch SK-C002 and SK-C004.

ADD: Added sheet for a Temporary Pavement. Refer to Addendum Sketch SK-C003 and added sheet C3.2.

CHANGE: Provide an Alternate Bid for the Water Main as indicated on Addendum Sketch SK-C005, SK-C006 and SK-C007.

CHANGE: Revise water main entrance into the new building. Refer to SK-C005 and SK-C008.

STRUCTURAL:

CHANGE: Column centerlines have been modified. Refer to SK-C002 and revised sheet S2.1.

ADD: Provide new concrete piers as per SK-S001 also refer to revised sheet S2.1 and SK-S004 for locations.

ADD: New interior concrete stair as per drawings SK-003 and SK-007.

CHANGE: Modify the Foundation Plan as per drawing SK-005.

ARCHITECTURAL:

ADD: Interior concrete stair at STAIR 135. Refer to drawing SK-A001.

REMOVE: Interior Corridor Doors near JANITOR 144. Refer to drawing SK-A002.

REMOVE: Interior Corridor Doors near ELEVATOR 205. Refer to drawing SK-A003.

PROJECT MANUAL:

CHANGE The Project Manual Cover Sheet has been modified

CHANGE: The Table of contents has been modified

ADD: The following Specification Sections have been added:

- 00 2113 Instructions to Bidders
- 00 4100 Bid Form
- 00 5000 Contracting Forms and Supplements
- 00 5200 Agreement Form
- 00 7200 General Conditions
- 01 4216 Definitions
- 07 9200 Joint Sealants

CHANGE: Specification Section 03 2000 has been modified with respect to paragraph 1.02 D is not included at this time.

CHANGE: Specification Section 03 2000 has been modified with respect to paragraph 1.02 E is not included at this time.

End of Addendum No. 1

CIVIL

C1.0 DETAILS AND SCHEDULES

C1.1 STANDARD DRAWINGS

C2.0 EXISTING CONDITIONS SITE PLAN

C3.0 DIMENSIONAL LAYOUT PLAN

C3.1 PAVEMENT PLAN

1 C3.2 TEMPORARY PAVEMENT PLAN

C4.0 GRADING PLAN, DETAILS

C5.0 UTILITY PLAN

C6.0 EROSION CONTROL PLAN

STRUCTURAL

S1.0 GENERAL NOTES

S1.1 SCHEDULES AND DETAILS

1 S2.1 FOUNDATION PLAN

S3.1 SECOND FLOOR AND LOW ROOF FRAMING PLAN


S5.1 FOUNDATION DETAILS

1 S5.2 FOUNDATION DETAILS

DRAWING REFERENCE: G2

© COPYRIGHT CBJ+CGA 2016


NORTH	SK-G001 Bid Phase 1	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL		CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ				
		PROJ. NO.: 16-009.1	DATE 9-2-16				

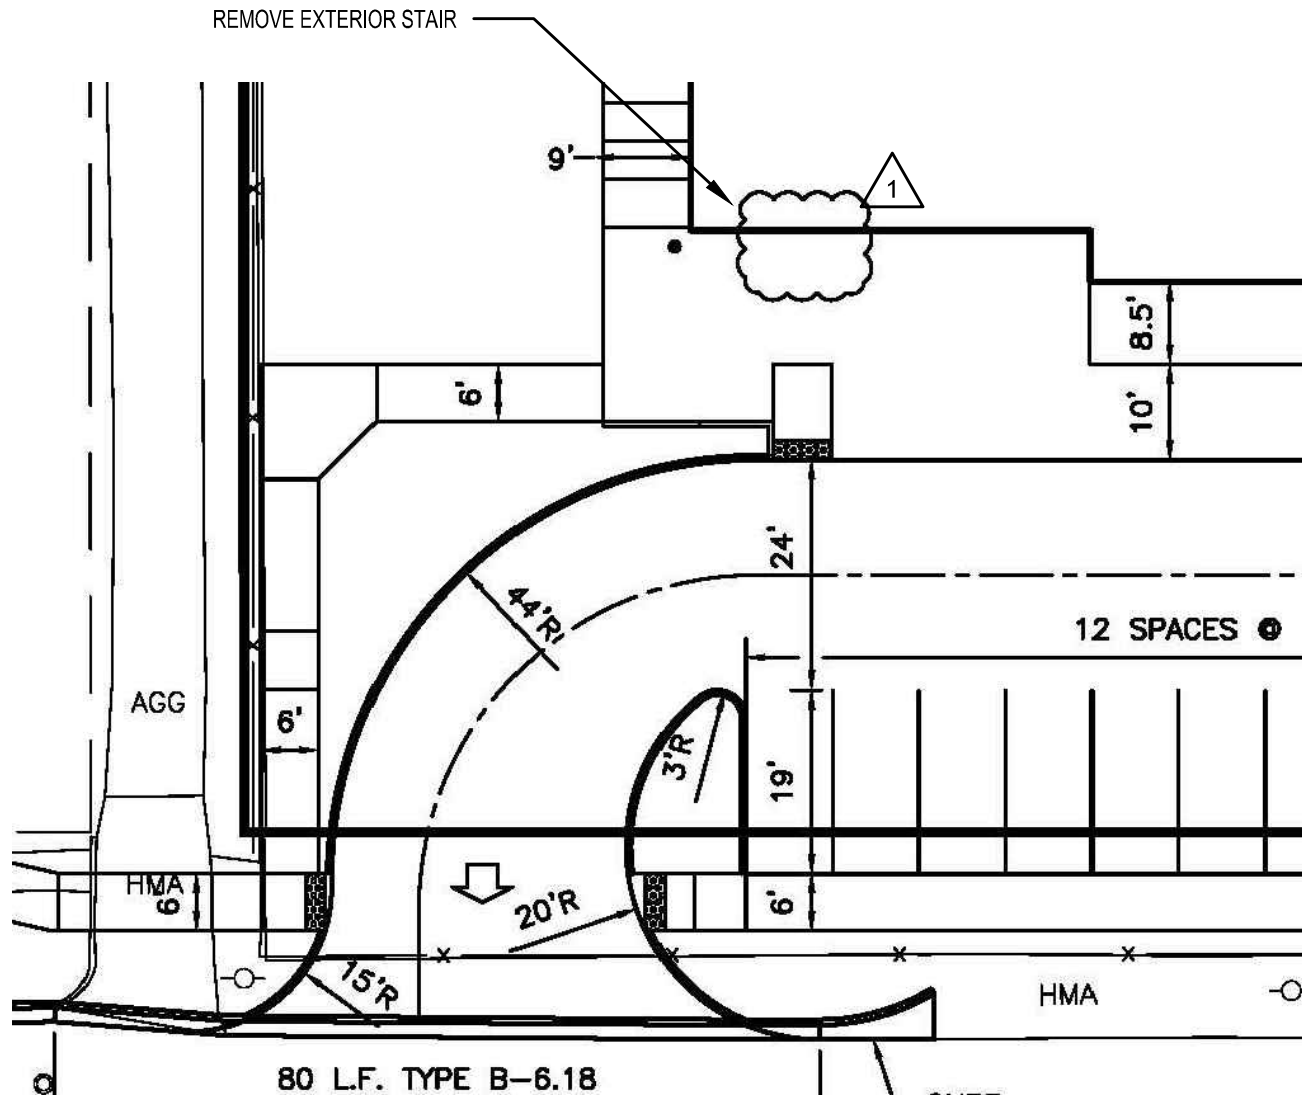

DRAWING REFERENCE: C3.0, C3.1, C3.2, C4.0, C5.0 AND C6.0

© COPYRIGHT CBJ+CGA 2016


NORTH	SK-C001 Bid Phase 1	BID PHASE: 1 SCALE: AS NOTED BY: CBJ PROJ. NO.: 16-009.1 DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	CHAMLIN ASSOCIATES, INC.	CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
-------	------------------------	---	---	-----------------------------	---	---

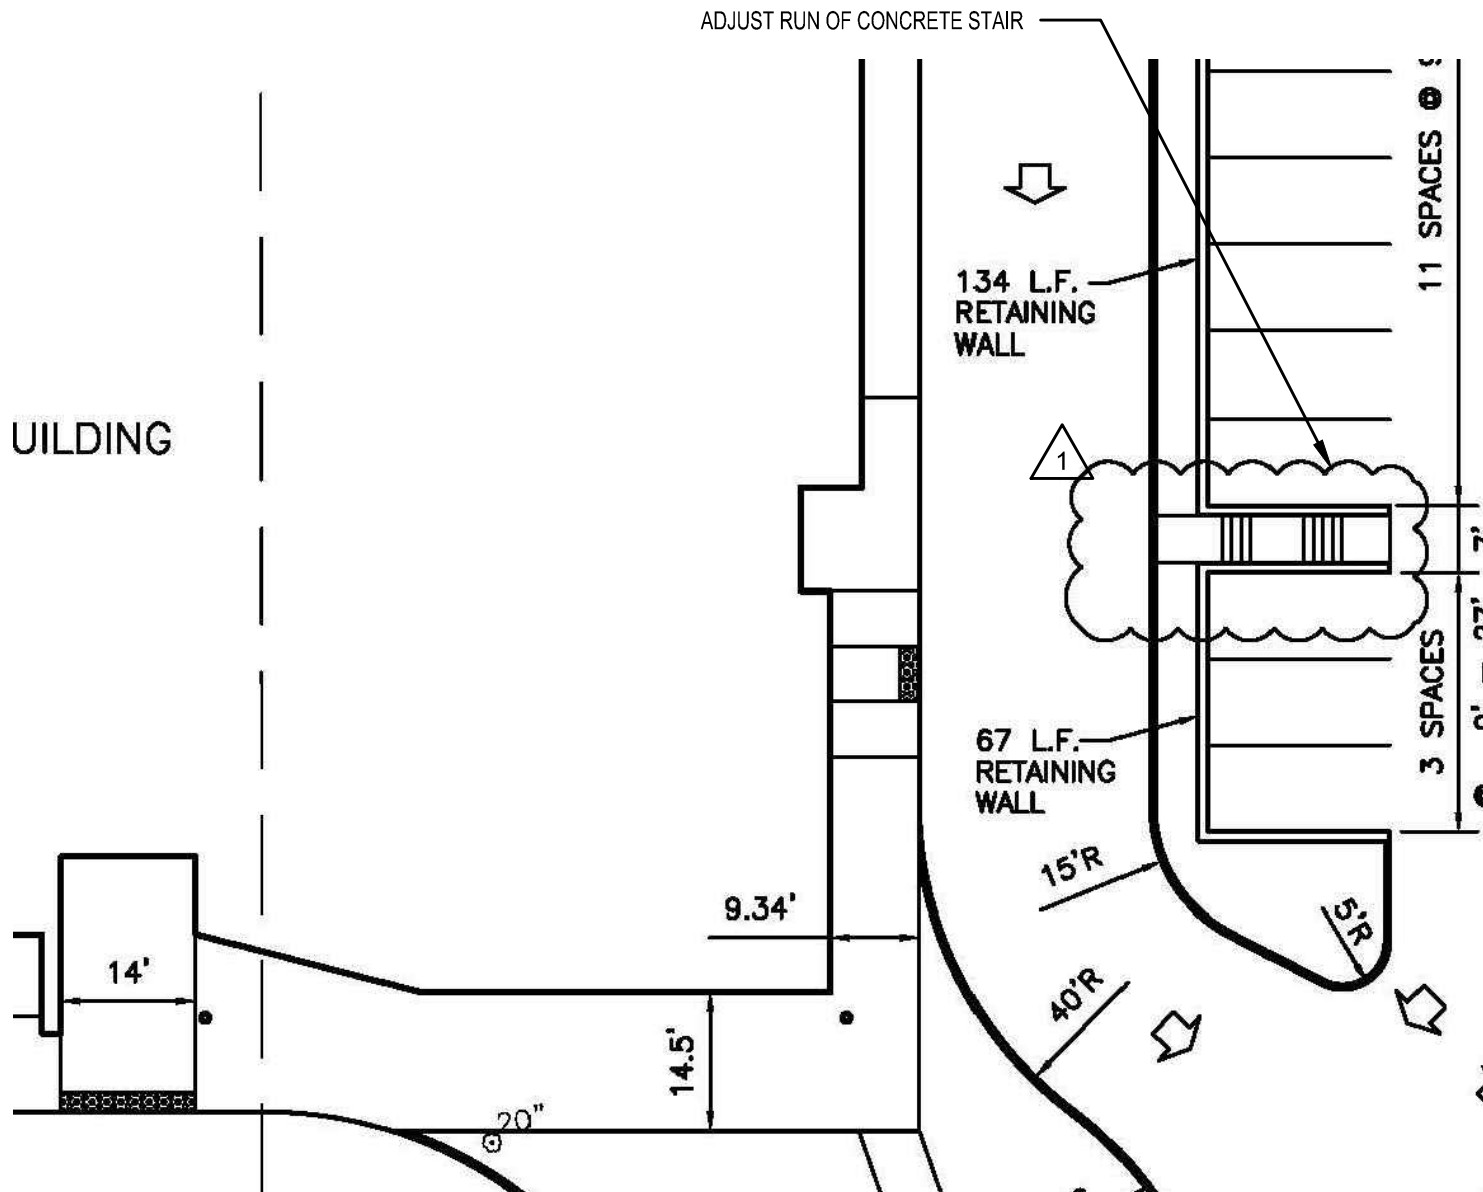

DRAWING REFERENCE: SECOND FLOOR ARCHITECTURAL FLOOR PLAN - C 3.0

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-C002 Bid Phase 1	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL			3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ				
		PROJ. NO.: 16-009,1	DATE: 9-2-16				

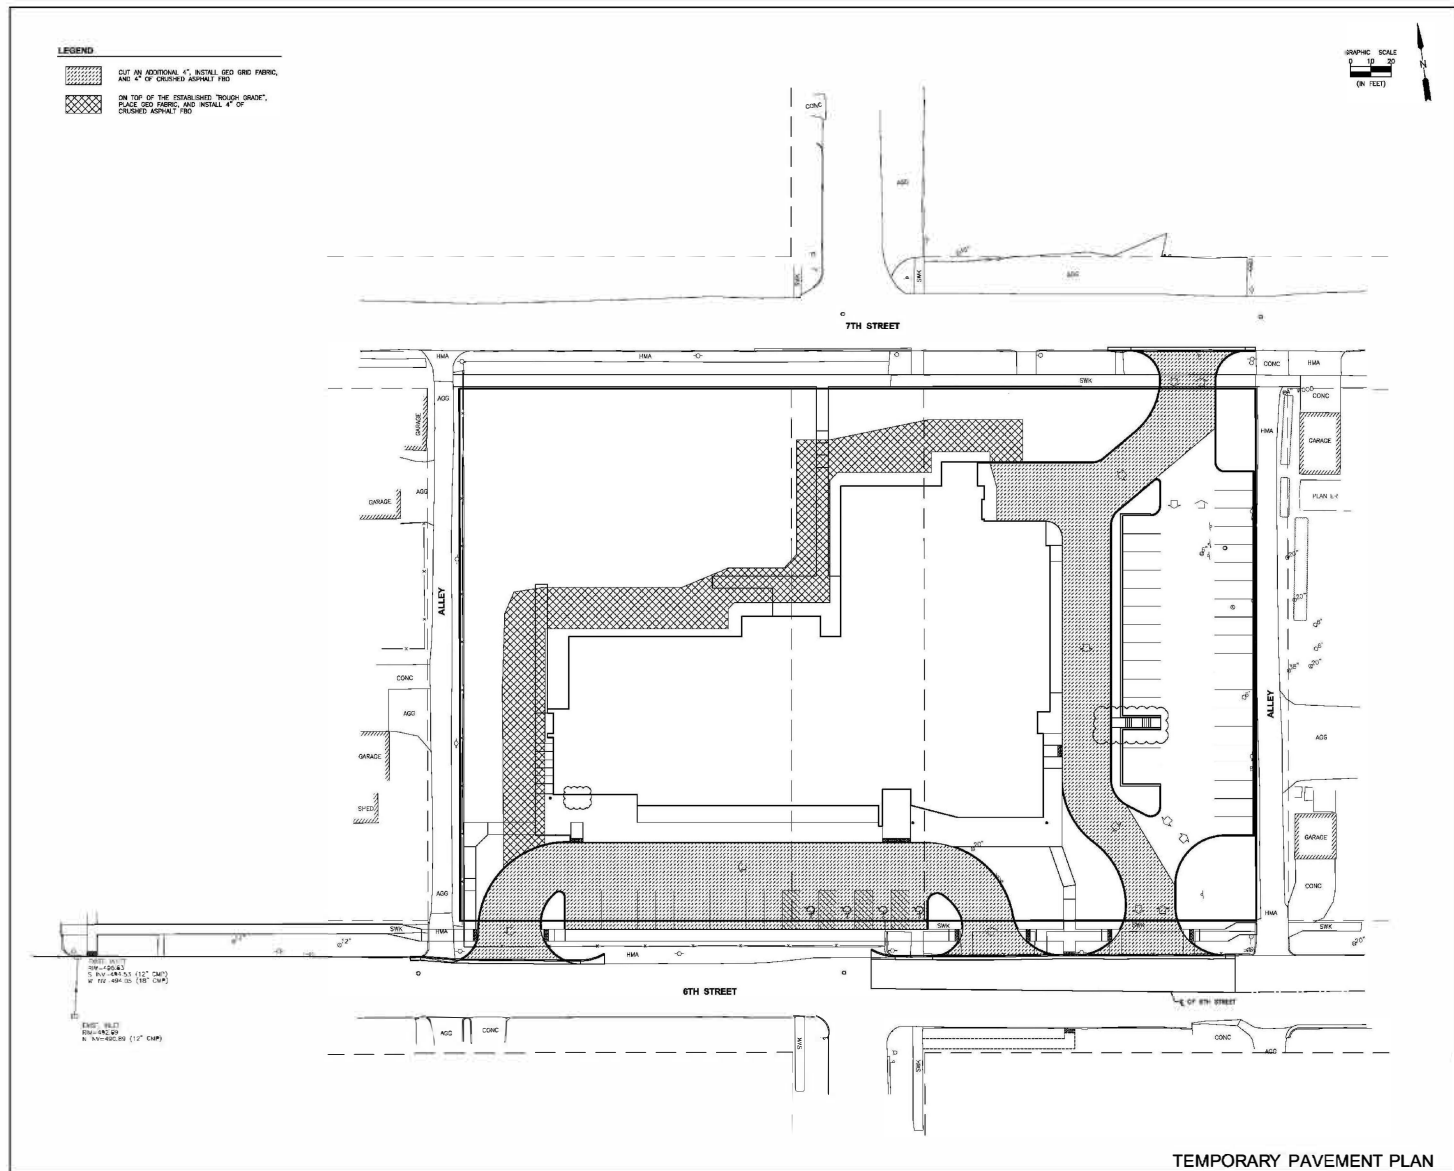

**MIDLAND ELEMENTARY SCHOOL
PROPOSED NEW SCHOOL**
LAOCN, ILLINOIS

CHAMLIN ASSOCIATES, INC.
PERU, ILLINOIS

CBJ + CGA
ARCHITECTS
PROFESSIONAL CORPORATION
COXGROUPARCHITECTS, LLC
1015 E. Tenth Avenue, Suite 200
Algonquin, IL 60102
P: 847-997-9838 F: 847-658-0095

REVISION	DATE	BY	CHKD
1	10/10/11	CBJ	CBJ

C-3.2


1

DRAWING REFERENCE: REFER TO ADDED TEMPORARY PAVEMENT PLAN SHEET - C 3.2

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-C003 Bid Phase 1	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	CHAMLIN ASSOCIATES, INC.	CBJ + CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: NTS	BY: CBJ				
		PROJ. NO.: 16-009.1	DATE: 9-2-16				

CLARIFICATION OF STAIR DIMENSION
AND REINFORCING

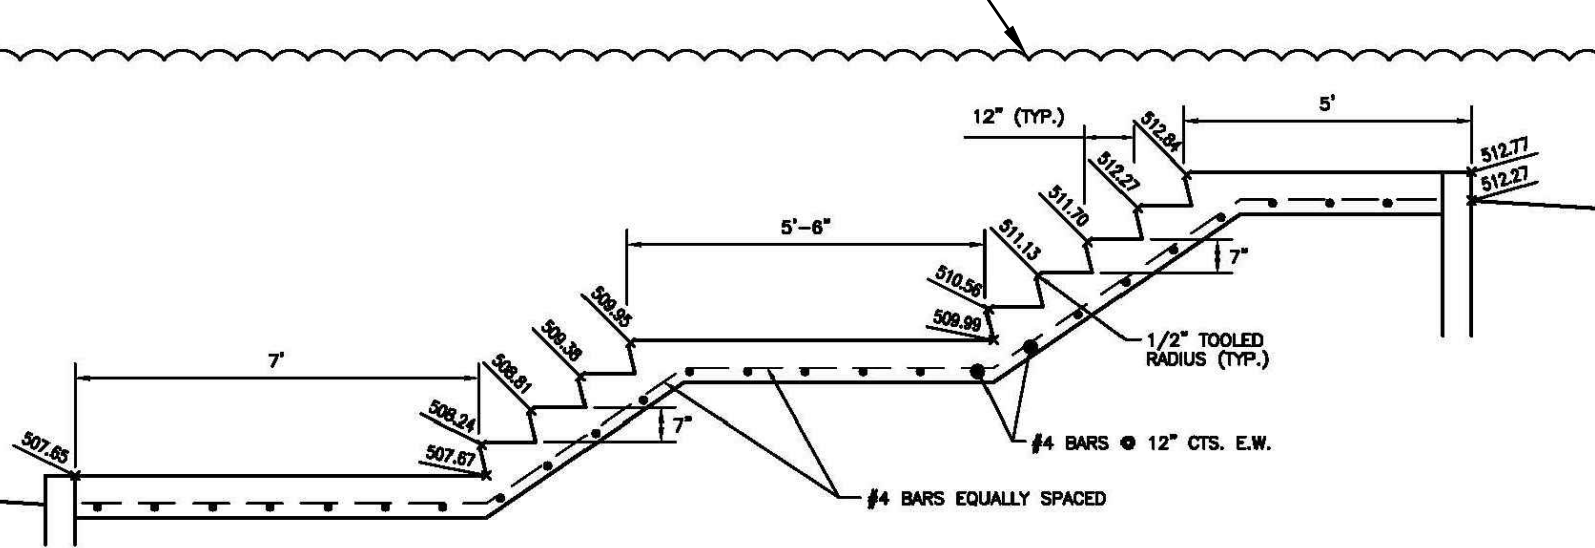


STAIR DETAIL #2
SOUTH EDGE OF STAIRS
N.T.S.


DRAWING REFERENCE: STAIR DETAIL #2 SHEET - C 4.0

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-C004 Bid Phase 1	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	 CHAMLIN ASSOCIATES, INC.	 CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ				
		PROJ. NO.: 16-009,1	DATE: 9-2-16				

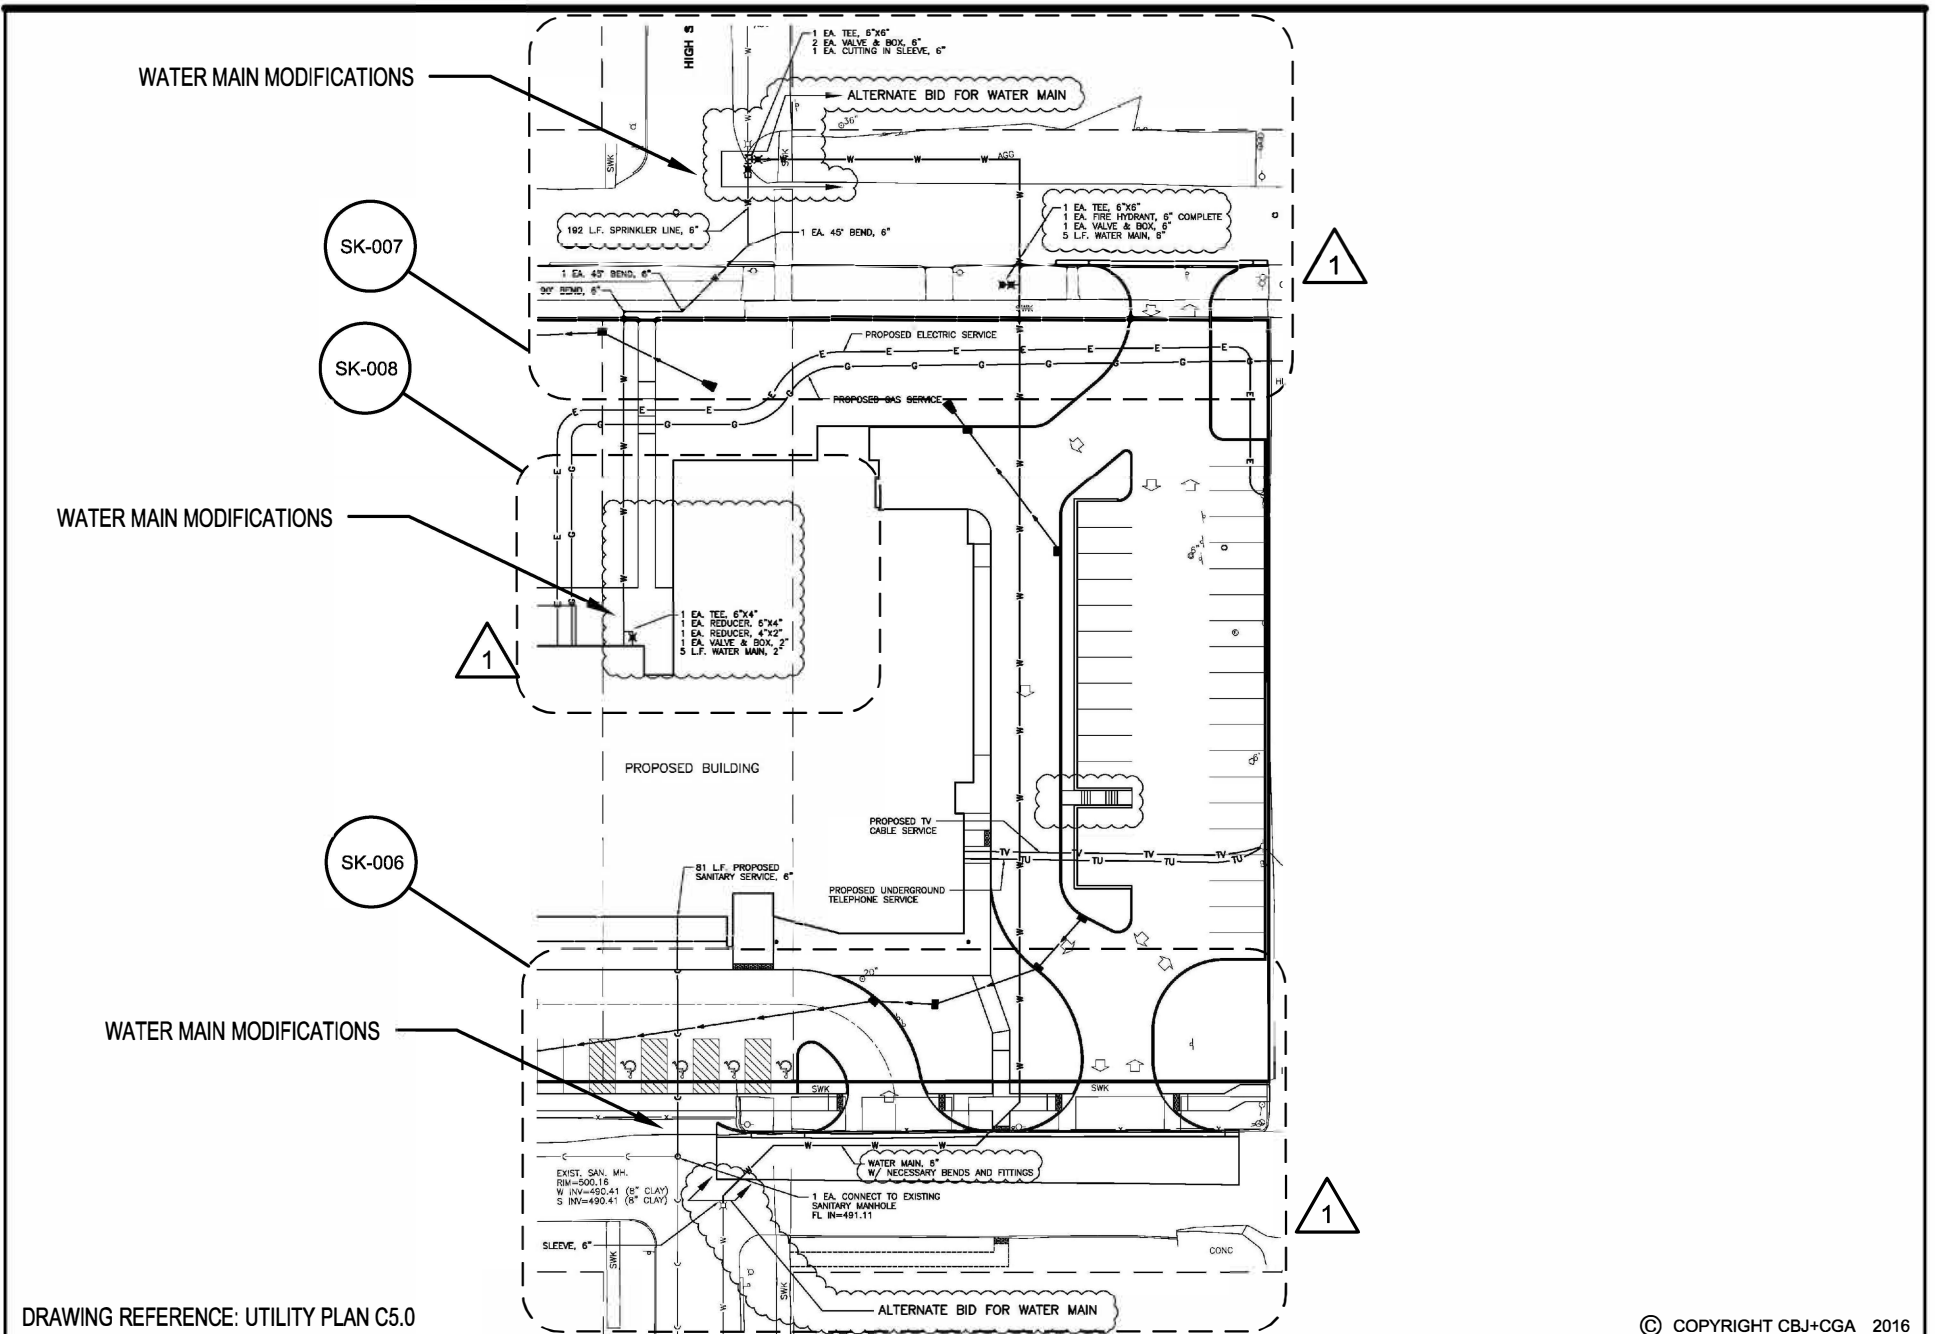


NORTH	SK-C005 Bid Phase 1	BID PHASE: 1 SCALE: NTS PROJ. NO.: 16-009.1 BY: CBJ DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	CHAMLIN ASSOCIATES, INC.	CBJ+CGA ARCHITECTS COXGROUPARCHITECTS	© COPYRIGHT CBJ+CGA 2016 3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
-------	------------------------	--	---	--------------------------	---------------------------------------	---

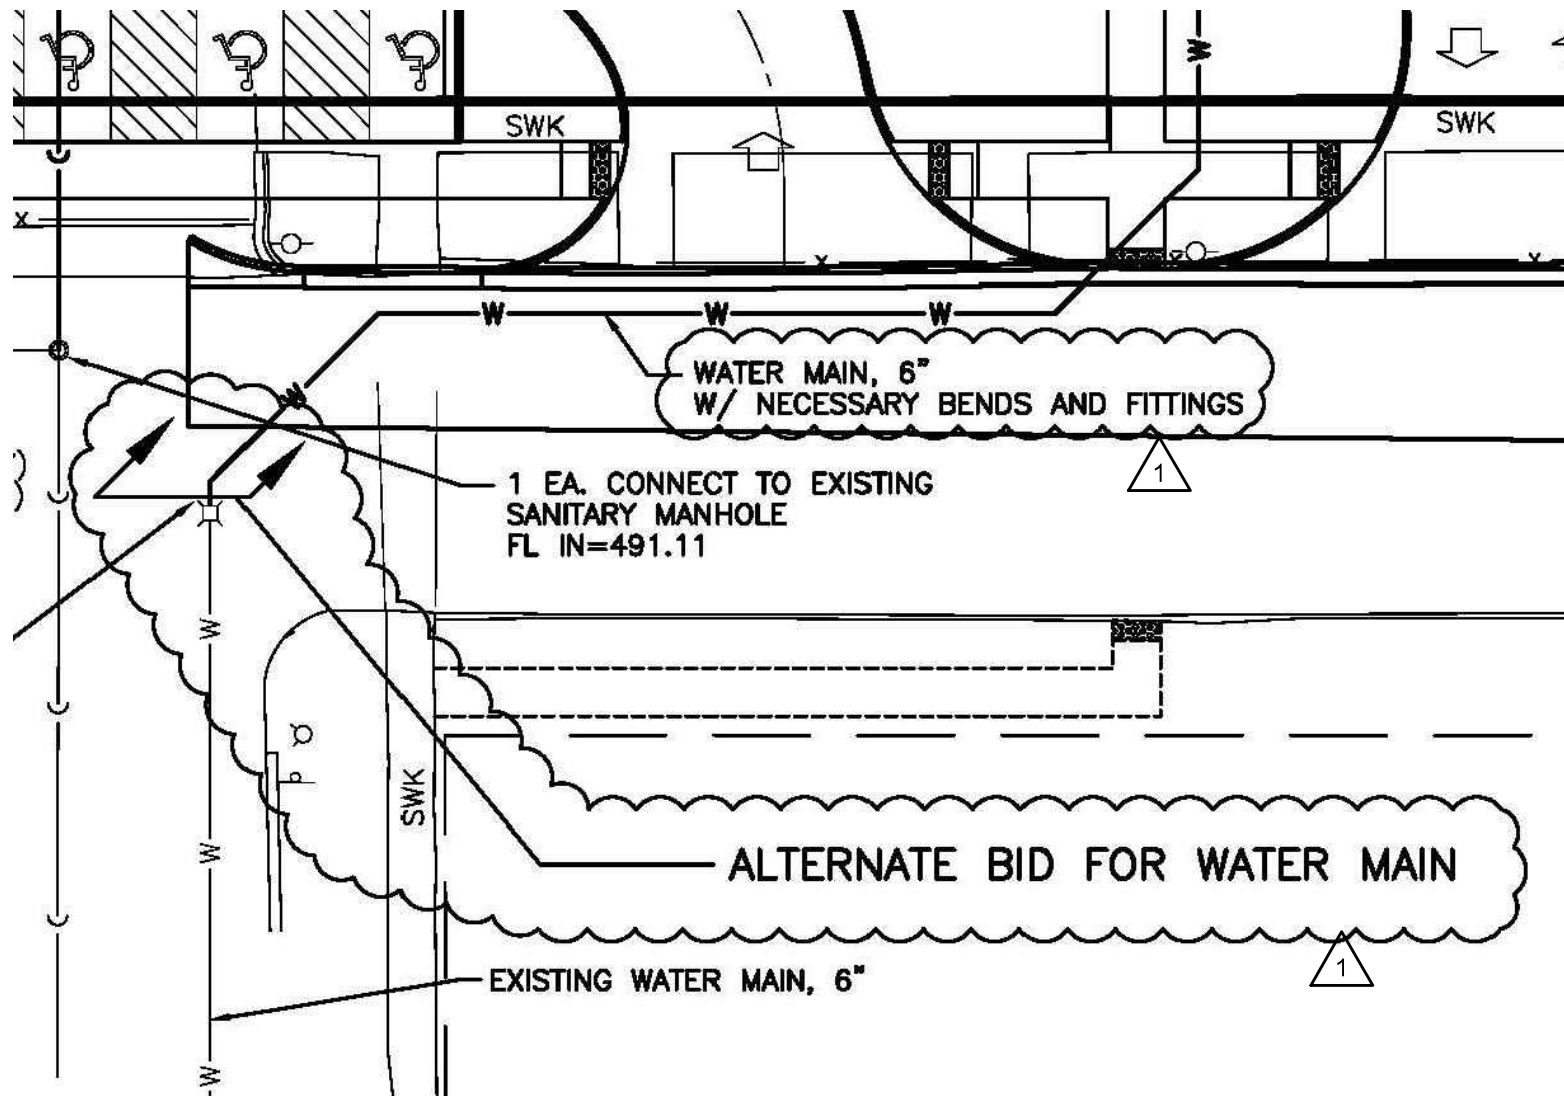

DRAWING REFERENCE: UTILITY PLAN C5.0

© COPYRIGHT CBJ+CGA 2016


NORTH	SK-C006 Bid Phase 1	BID PHASE: 1 SCALE: AS NOTED BY: CBJ PROJ. NO.: 16-009,1 DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	CHAMLIN ASSOCIATES, INC.	CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
--------------	--	---	---	--	--	--

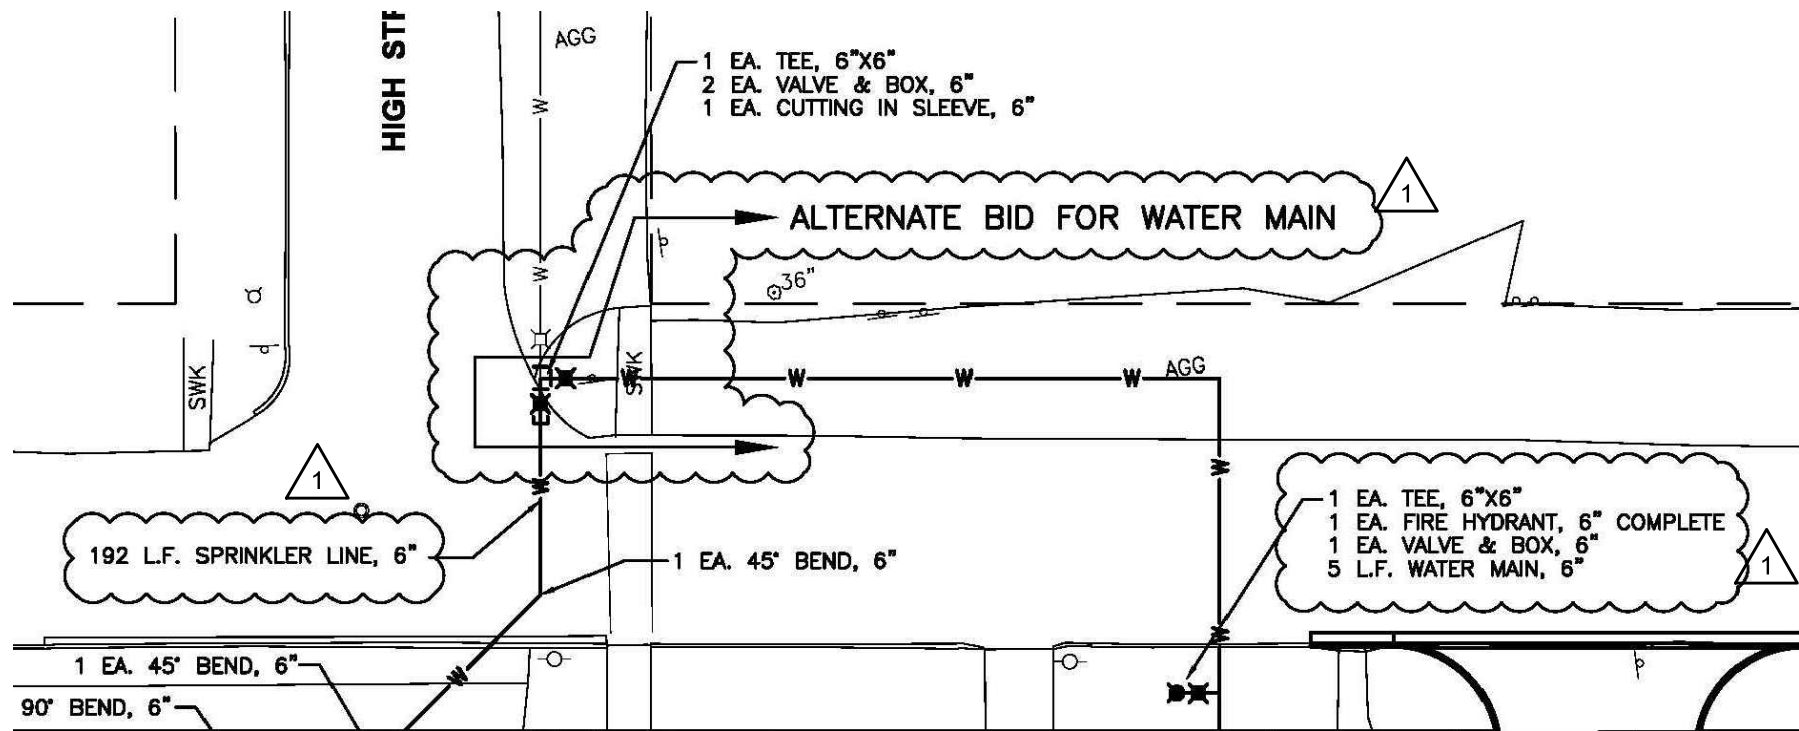

DRAWING REFERENCE: UTILITY PLAN C5.0

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-C007	BID PHASE: 1	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	CHAMLIN ASSOCIATES, INC.	CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
Bid Phase	1	SCALE: AS NOTED	BY: CBJ	PROJ. NO.: 16-009,1	DATE: 9-2-16	

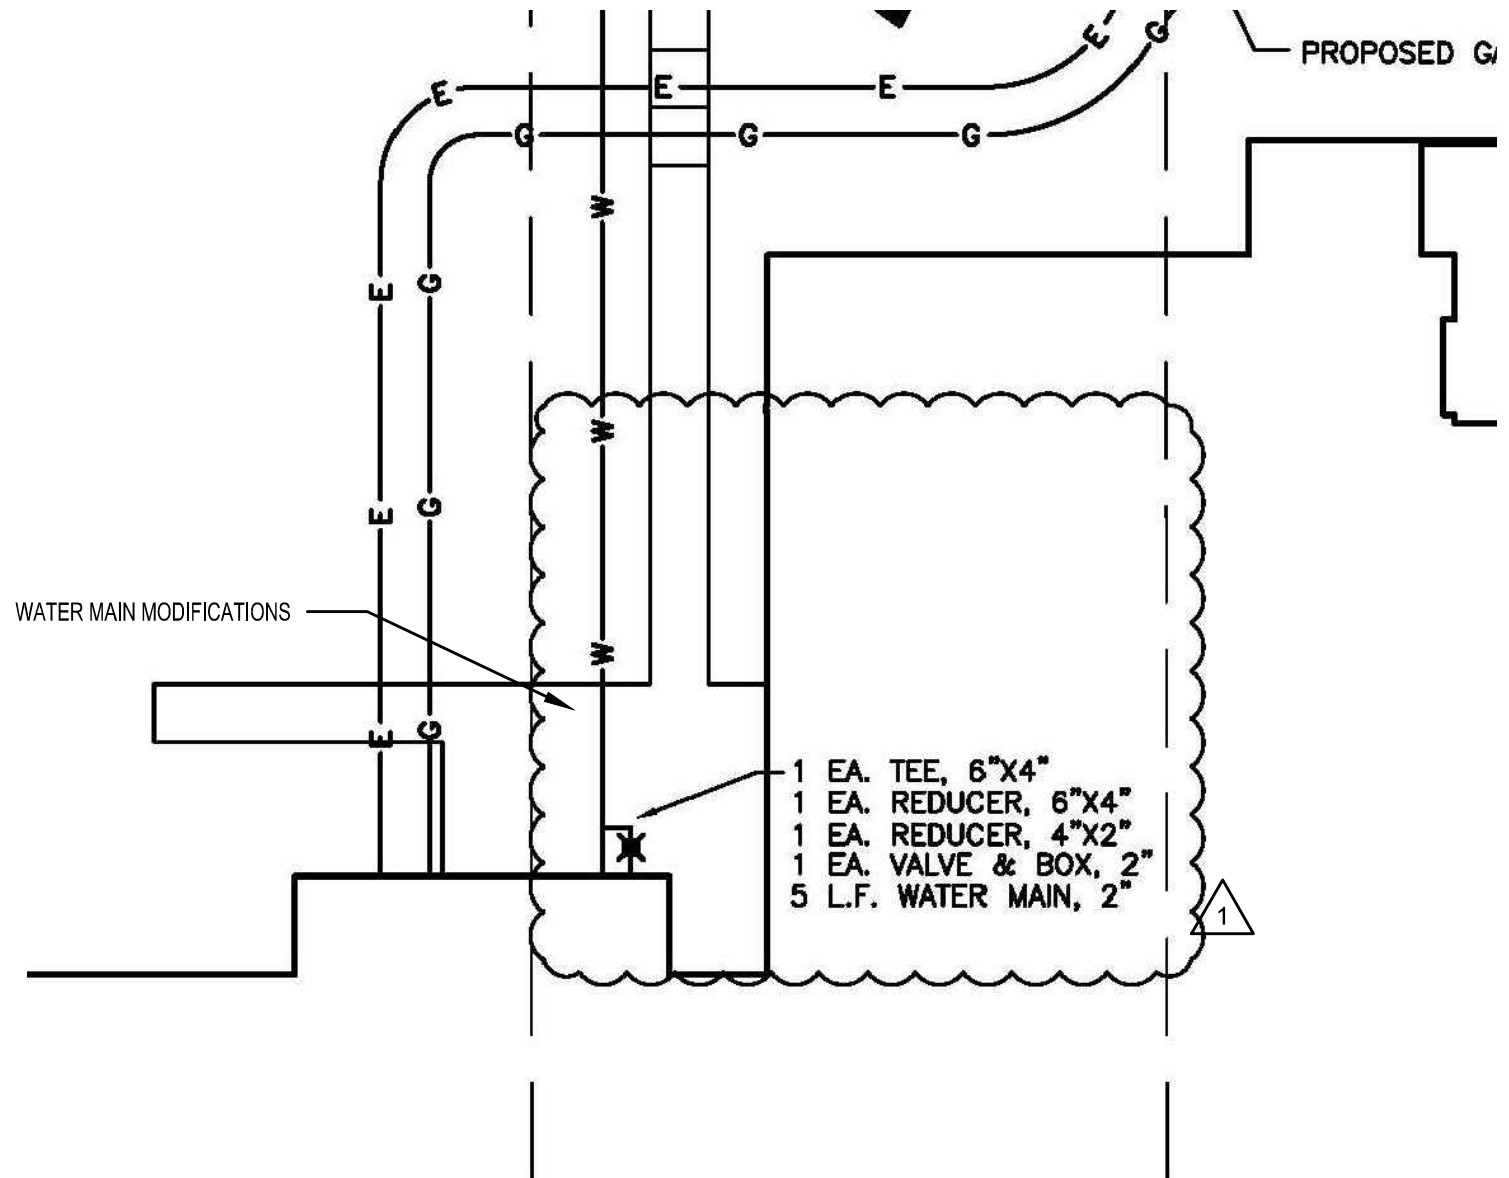


DRAWING REFERENCE: UTILITY PLAN C5.0

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-C008 Bid Phase 1	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL			3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ				
		PROJ. NO.: 16-009,1	DATE: 9-2-16				

FOR REFERENCE ONLY
NOT FOR CONSTRUCTION

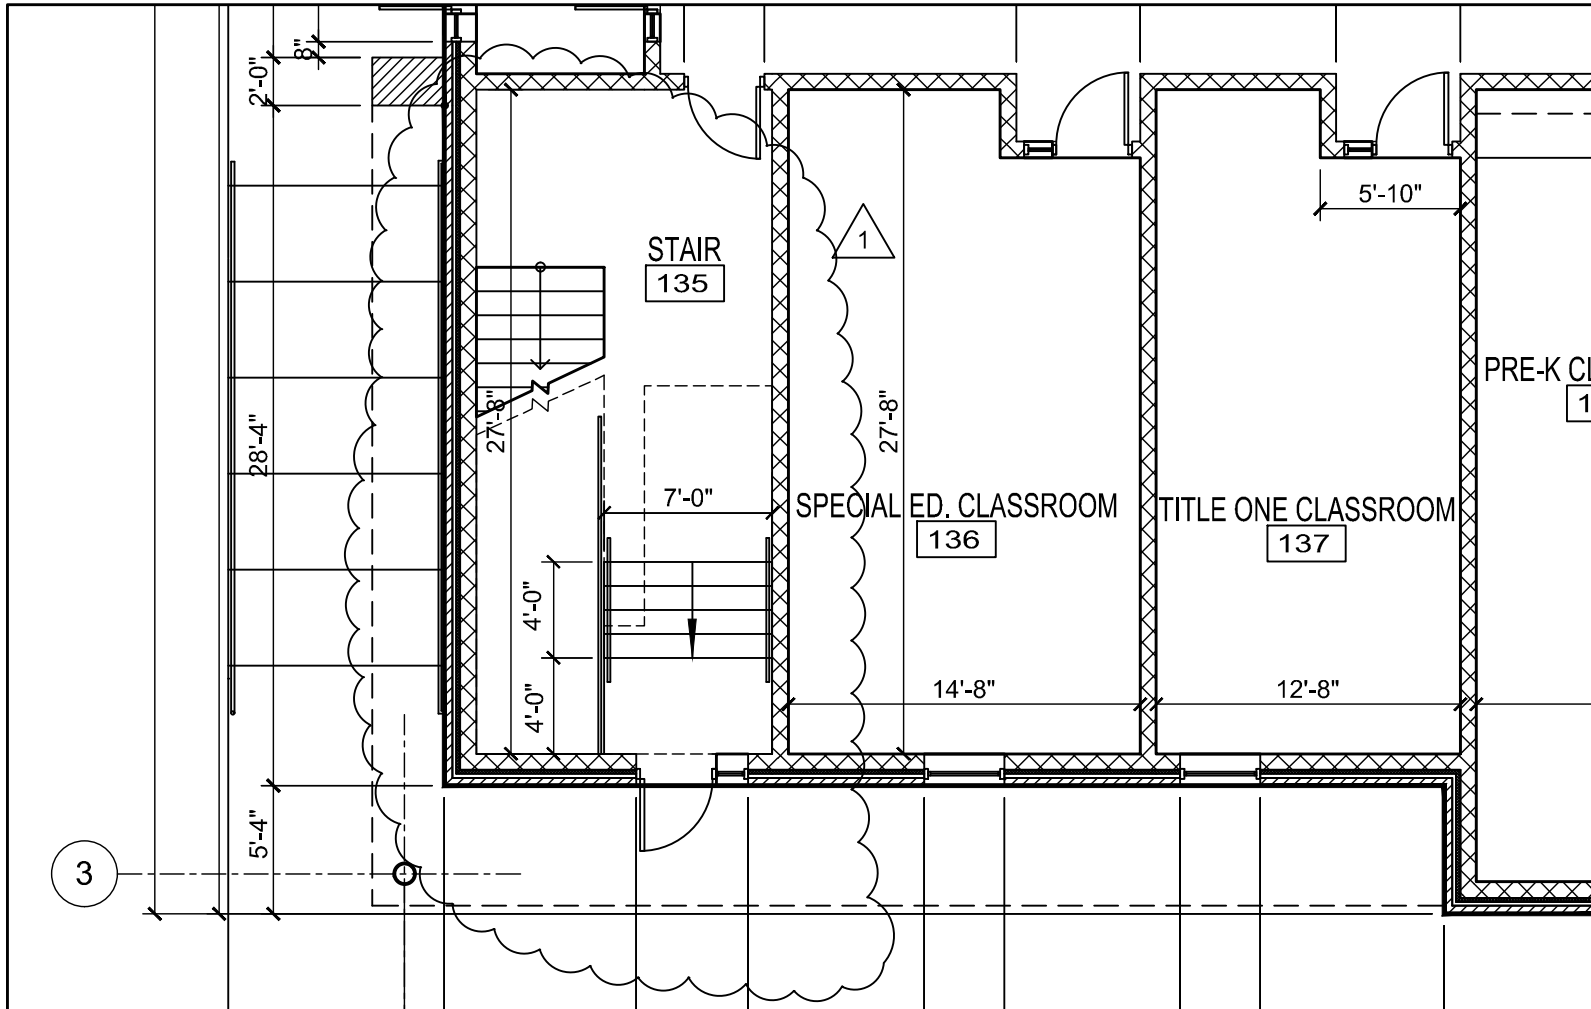


DRAWING REFERENCE: FIRST FLOOR ARCHITECTURAL FLOOR PLAN - A 2.1

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-A001	BID PHASE: 1	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL		CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
Bid Phase	1	SCALE: AS NOTED	BY: CBJ			
		PROJ. NO.: 16-009.1	DATE: 9-2-16			

FOR REFERENCE ONLY
NOT FOR CONSTRUCTION

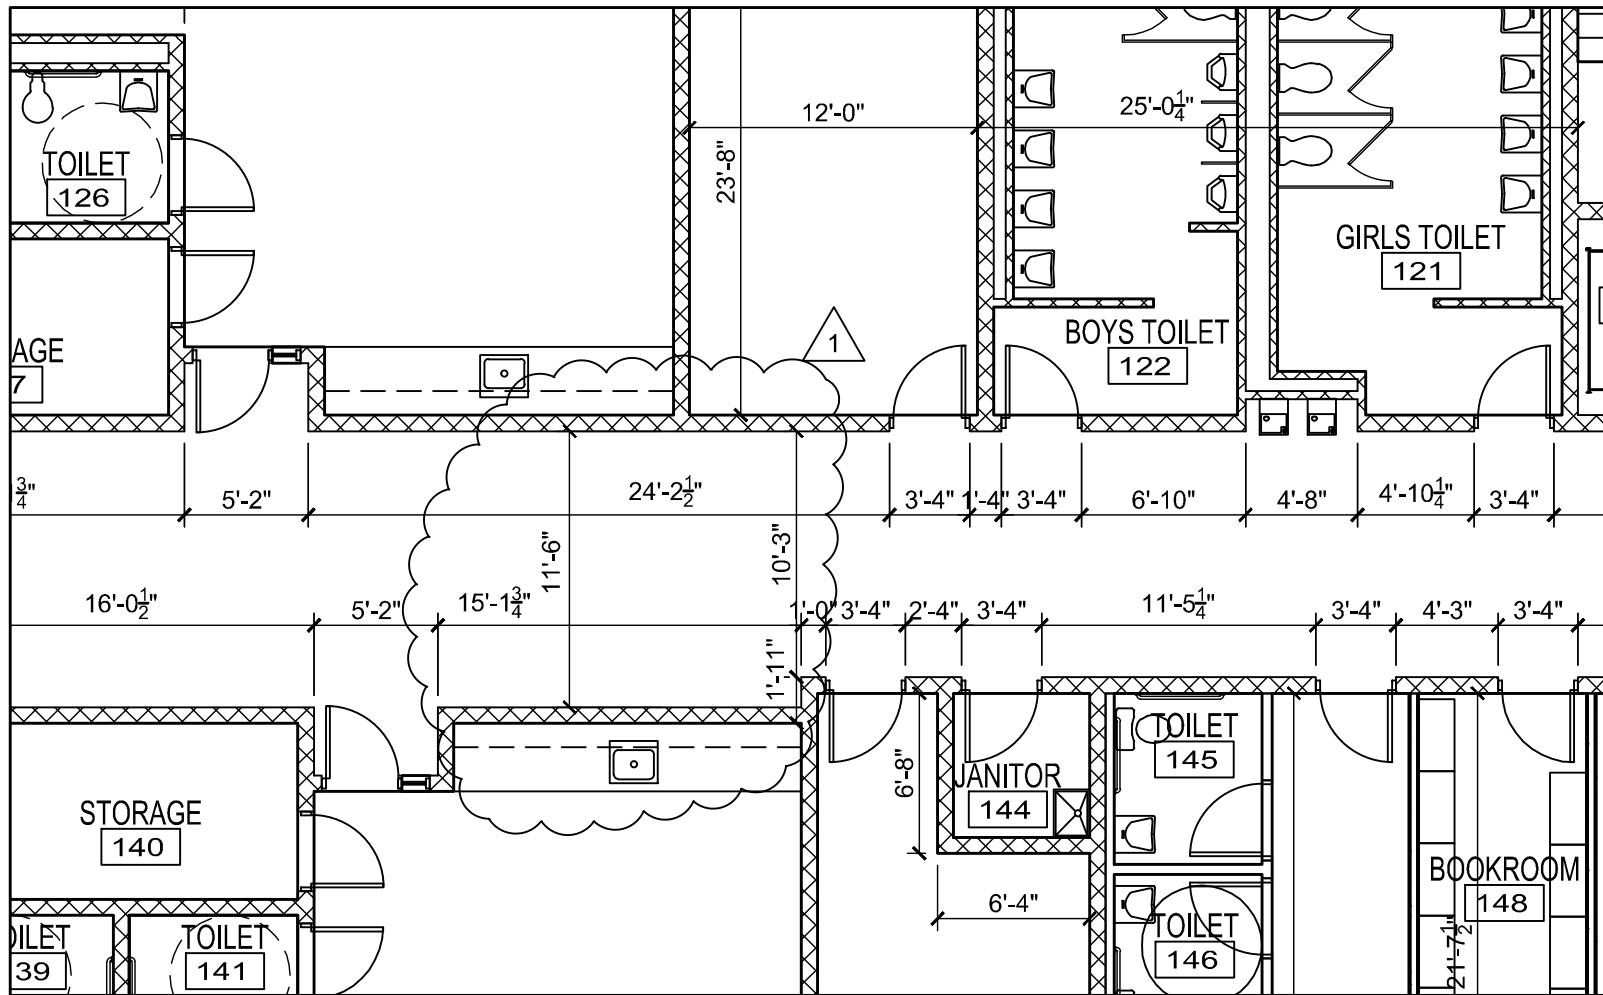


DRAWING REFERENCE: FIRST FLOOR ARCHITECTURAL FLOOR PLAN - A 2.1

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-A002 Bid Phase 1	BID PHASE: 1 SCALE: AS NOTED BY: CBJ PROJ. NO.: 16-009.1 DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL		CBJ+CGA ARCHITECTS COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
-------	------------------------	---	---	--	--	---

FOR REFERENCE ONLY
NOT FOR CONSTRUCTION

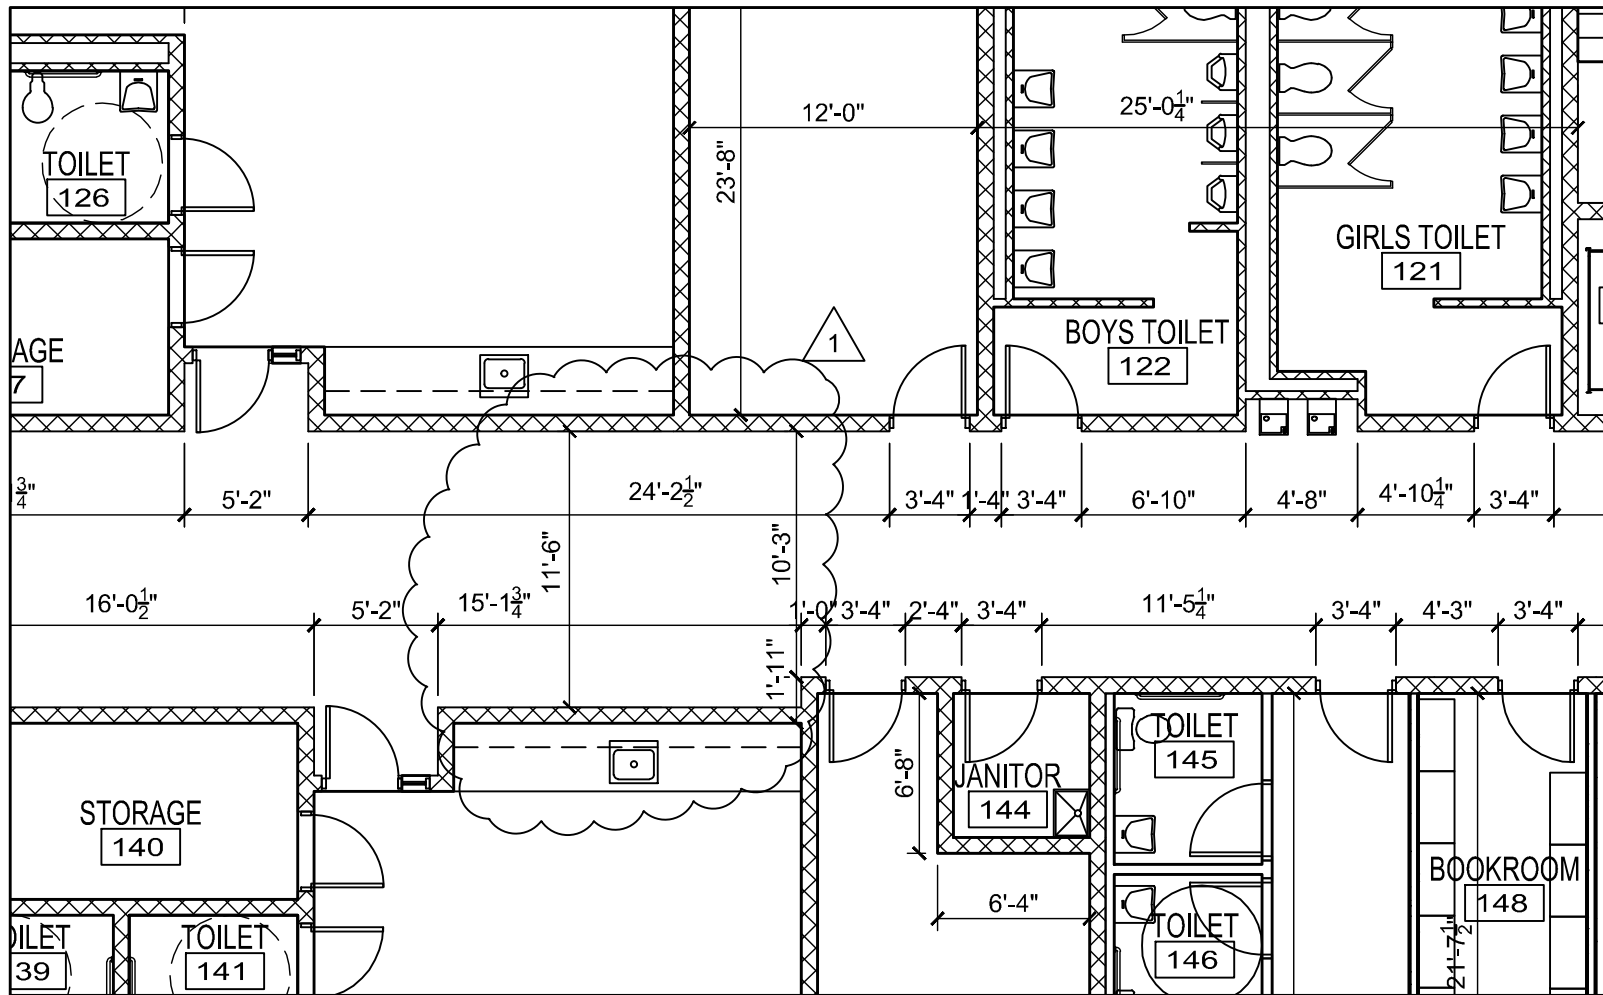


DRAWING REFERENCE: FIRST FLOOR ARCHITECTURAL FLOOR PLAN - A 2.1

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-A002 Bid Phase 1	BID PHASE: 1 SCALE: AS NOTED BY: CBJ PROJ. NO.: 16-009.1 DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL		CBJ+CGA ARCHITECTS COXGROUPARCHITECTS PROFESSIONAL CORPORATION	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
-------	------------------------	---	---	--	--	---

 CUT AN ADDITIONAL 4", INSTALL GEO GRID FABRIC, AND 4" OF CRUSHED ASPHALT FBO


 ON TOP OF THE ESTABLISHED "ROUGH GRADE", PLACE GEO FABRIC, AND INSTALL 4" OF CRUSHED ASPHALT FBO

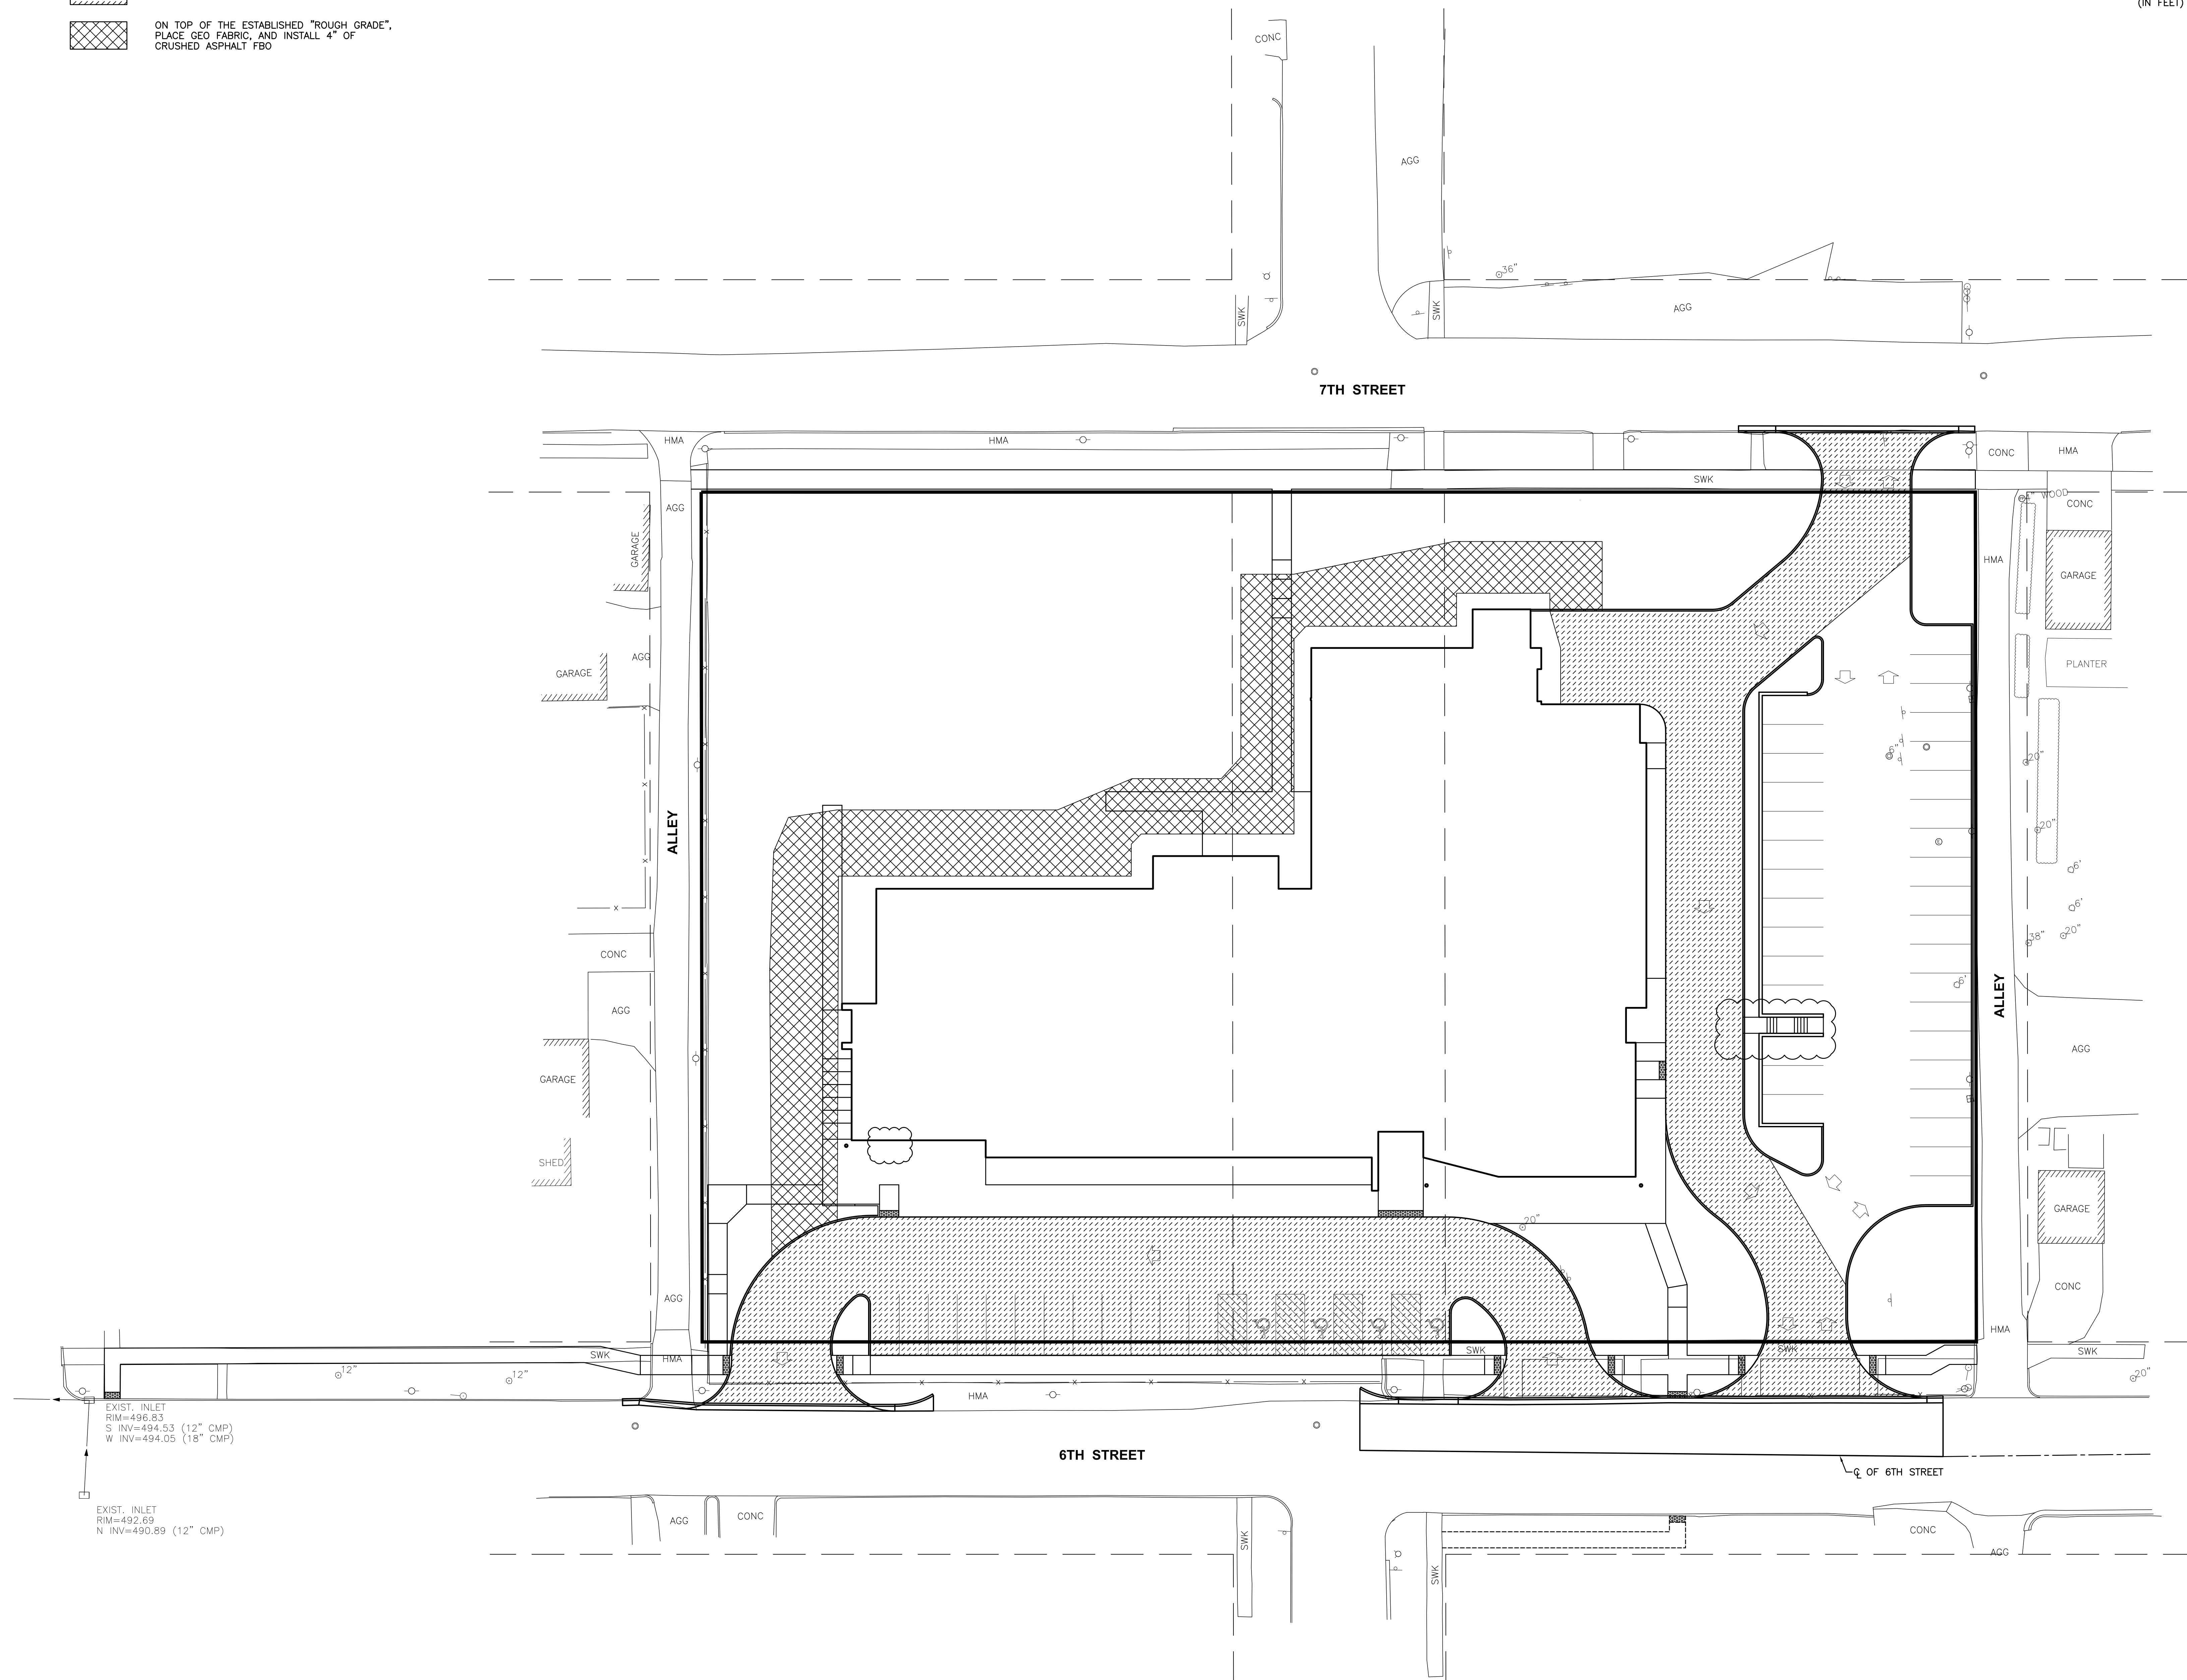

 COPYRIGHT CBU+CGA DATE

CHAMLIN
ASSOCIATES, INC.

MIDLAND ELEMENTARY SCHOOL
PROPOSED NEW SCHOOL
LACON, ILLINOIS



PROFESSIONAL CORPORATION
COX GROUP ARCHITECTS, LLC
2521 Wintergreen Ter.
Algonquin, IL 60102
P: 847-997-9838
2801 E. Enterprise Ave. #202
Appleton, WI 54913
P: 920-475-4088

JOB:	16-009.1	REVISION		
		NO.	DESCRIPTION	DATE
DATE:	8/19/16		R01 ISSUE	8/19/16
			ADDENDUM 1	9/01/16
SCALE:	1"=20'			
DRAWN:	NV			
CHECKED:	MSR			

SHEET NO.

C-3.2

Construction Docs

CONCRETE PIER SCHEDULE			
MARK	SIZE	REINFORCING	DETAIL
P1	1'-4"x1'-4"	(4) #6 VERTICAL & #3 TIES, TOP 3 @ 5" OC REMAINDER @ 12" OC	12 / S5.1
P2	1'-6"x1'-6"	(4) #6 VERTICAL & #3 TIES, TOP 3 @ 5" OC REMAINDER @ 12" OC	12 / S5.1
P3	2'-0"x2'-0"	(8) #6 VERTICAL & #3 TIES, TOP 3 @ 5" OC REMAINDER @ 12" OC	12 / S5.1
P4	1'-4"x2'-0"	(6) #8 VERTICAL & #3 TIES, TOP 3 @ 5" OC REMAINDER @ 12" OC	
P5	2'-0"x2'-8"	(8) #6 VERTICAL & #3 TIES, TOP 3 @ 5" OC REMAINDER @ 12" OC	
P6	0'-8"x4'-0"	(10) #6 VERTICAL & #3 TIES @ 8" OC	
P7	0'-8"x1'-4"	(4) #6 VERTICAL & #3 TIES @ 8" OC	




ADDED CONCRETE PIERS

DRAWING REFERENCE: S1.1, S2.1

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-S001	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	 Larson Engineering	 CBJ+CGA ARCHITECTS PROFESSIONAL CORPORATION COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ				
	Bid Phase 1	PROJ. NO.: 16-009.1	DATE: 9-2-16				



© COPYRIGHT CBJ+CGA 2016

Midland CUSD #7
New Elementary School
 206 N. High Street
 Lacon, IL

SCALE: AS NOTED	BY: CBJ
PROJ. NO.: 16-009.1	DATE: 9-2-16




Larson

Engineering



+CGA
COXGROUPARCHITECTS


3521 WINTERGREEN
ALGONQUIN, ILLINOIS 60102
P: 847-997-9838
F: 847-658-0095
cbjarchitect@comcast.net

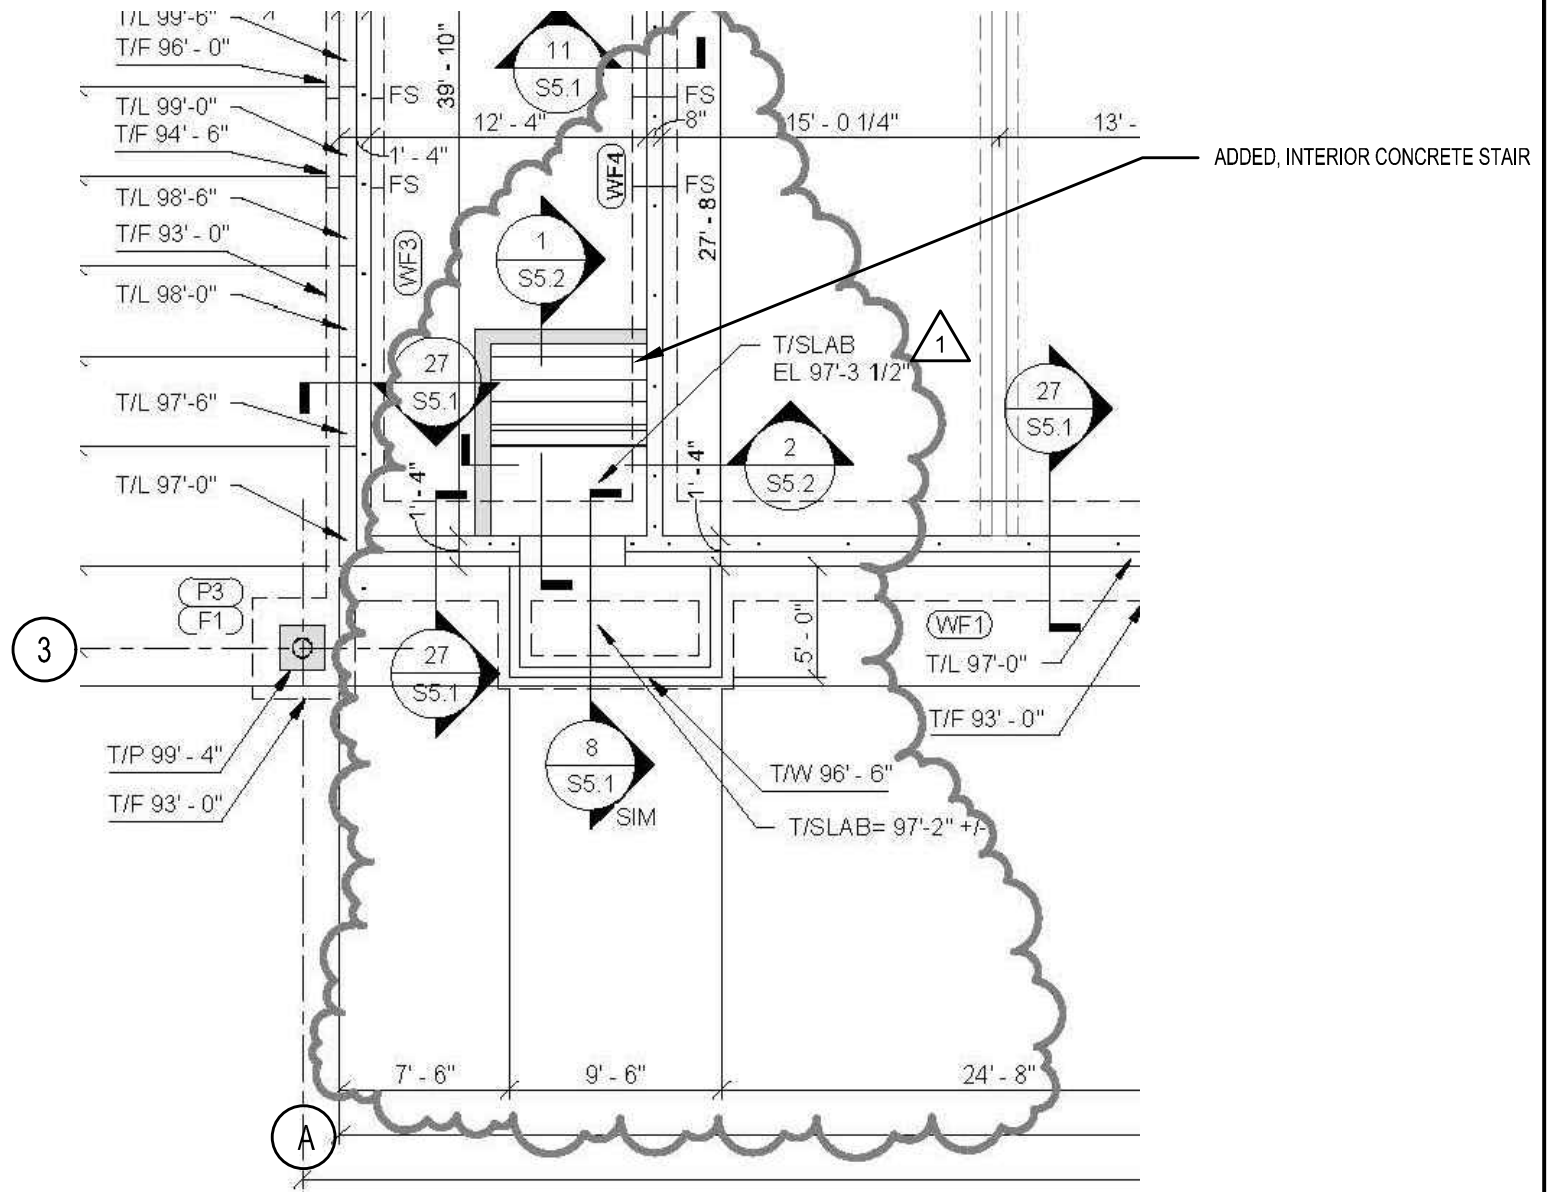

DRAWING REFERENCE: S2.1, S5.2INTERIOR STAIR ADDITION

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-S003 Bid Phase 1	BID PHASE: 1 SCALE: AS NOTED BY: CBJ PROJ. NO.: 16-009.1 DATE: 9-2-16	Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL	Larson Engineering	CBJ + CGA ARCHITECTS COXGROUPARCHITECTS	3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
--------------	-----------------------------------	--	--	---	---	--

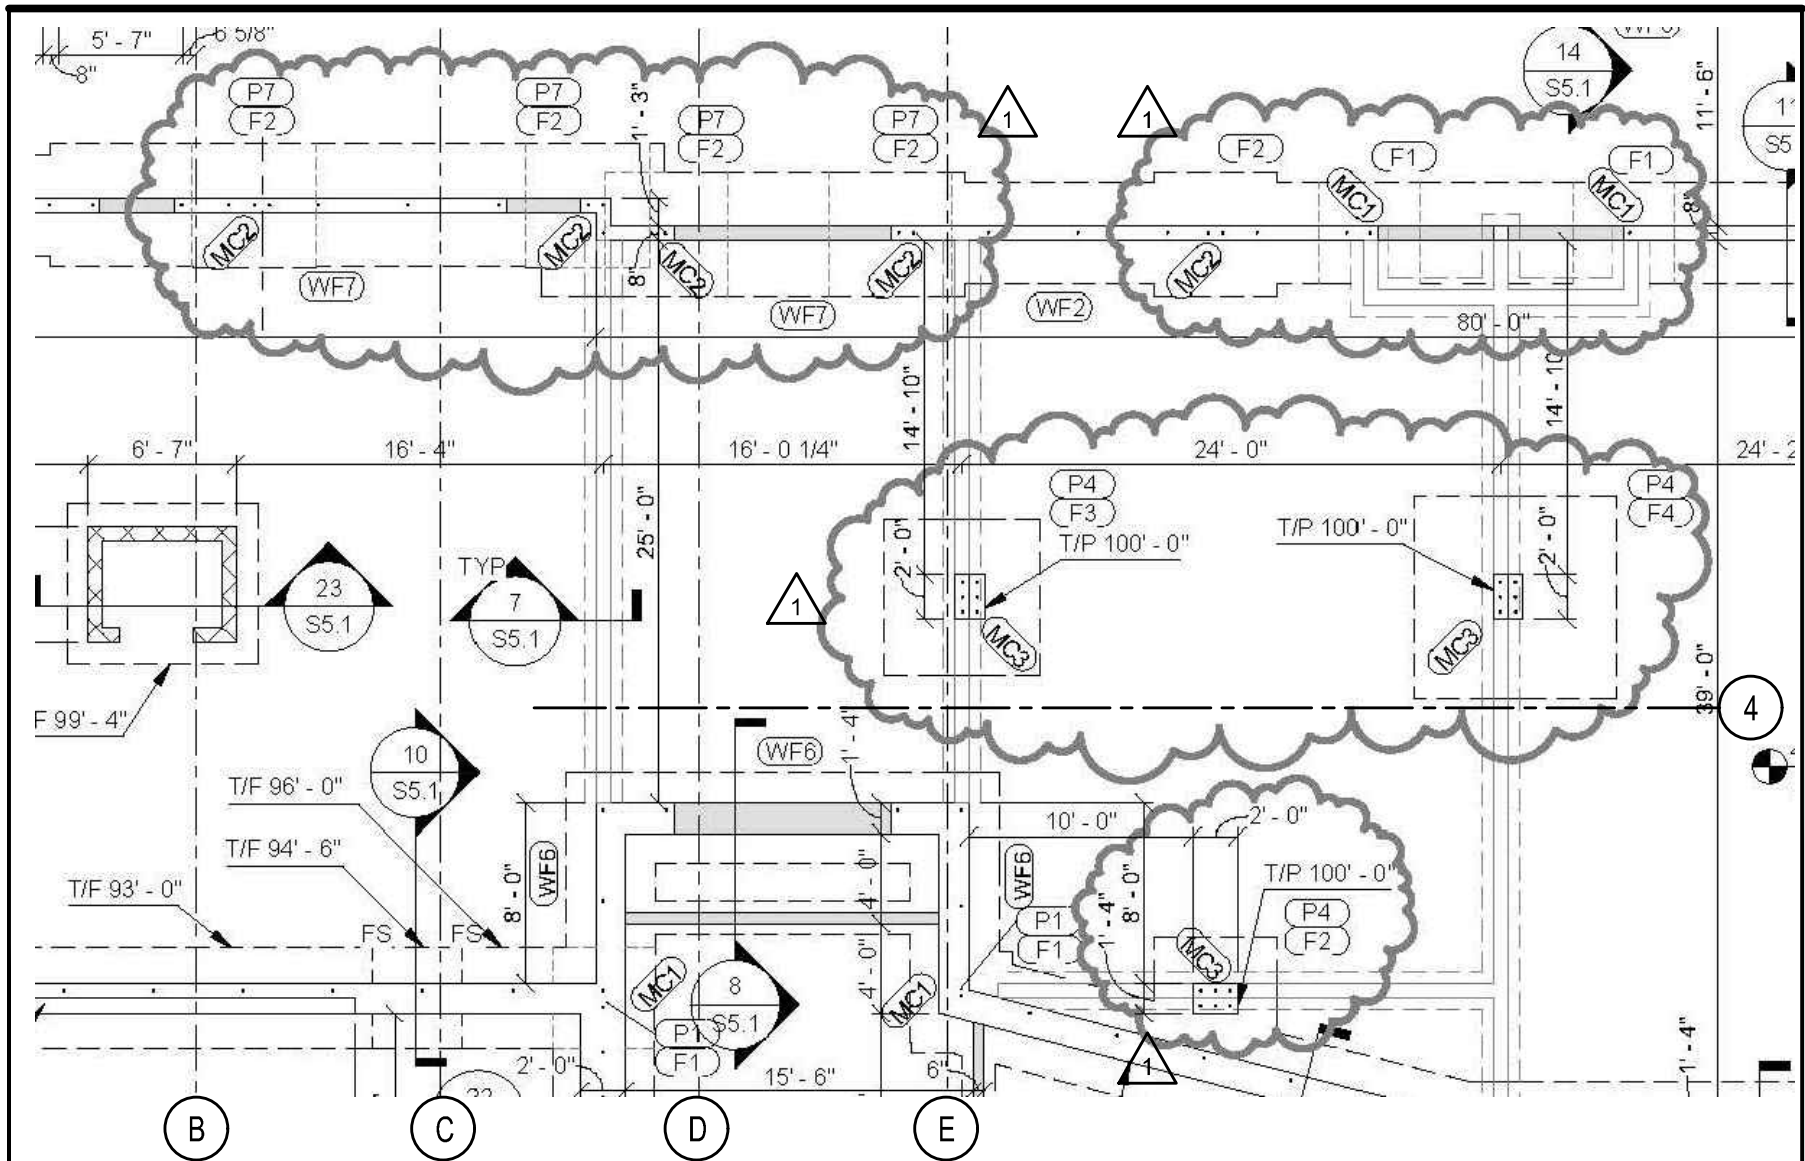

DRAWING REFERENCE: S2.1.....FOUNDATION MODIFICATIONS

© COPYRIGHT CBJ+CGA 2016

SK-S004

BID PHASE: 1

Midland CUSD #7
New Elementary School
206 N. High Street
Lacon, IL

SCALE: AS NOTED BY: CBJ
PROJ. NO.: 16-009.1 DATE: 9-2-16

NORTH

Bid Phase 1




Larson
Engineering

CBJ
ARCHITECTS
PROFESSIONAL CORPORATION

CGA
COXGROUPARCHITECTS

3521 WINTERGREEN
ALGONQUIN, ILLINOIS 60102
P: 847-997-9838
F: 847-658-0095
cbjarchitect@comcast.net

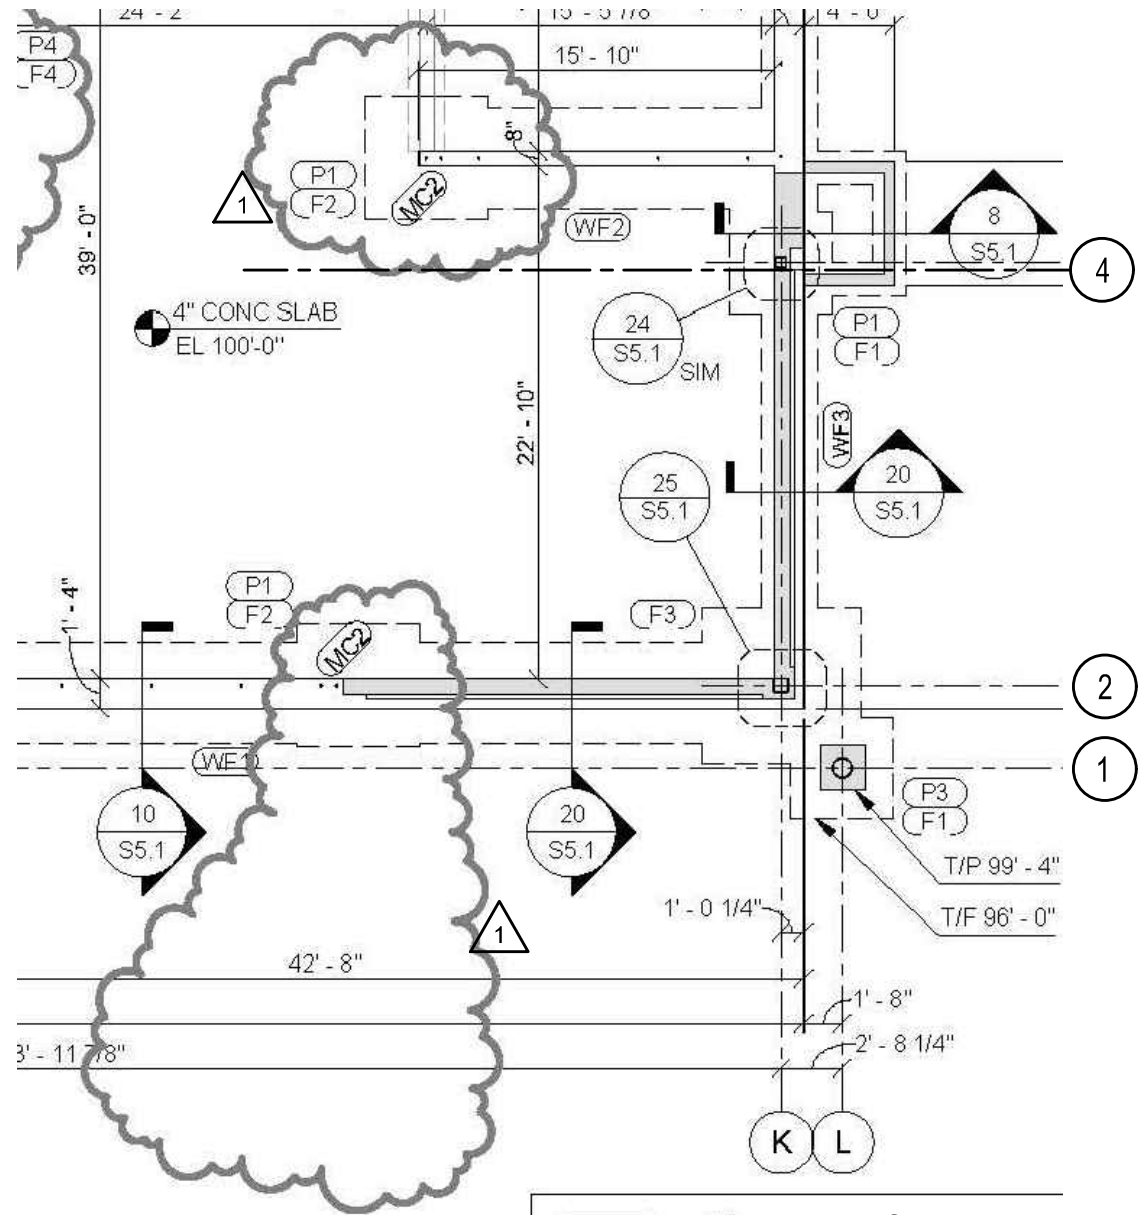

DRAWING REFERENCE: S2.1.....FOUNDATION MODIFICATIONS

© COPYRIGHT CBJ+CGA 2016

SK-S005

BID PHASE: 1

Midland CUSD #7
New Elementary School
206 N. High Street
Lacon, IL



Larson
Engineering



CBJ+CGA
ARCHITECTS
PROFESSIONAL CORPORATION
COXGROUPARCHITECTS


3521 WINTERGREEN
ALGONQUIN, ILLINOIS 60102
P: 847-997-9838
F: 847-658-0095
cbjarchitect@comcast.net

NORTH

Bid Phase 1

SCALE: AS NOTED
PROJ. NO.: 16-009.1

BY: CBJ
DATE: 9-2-16

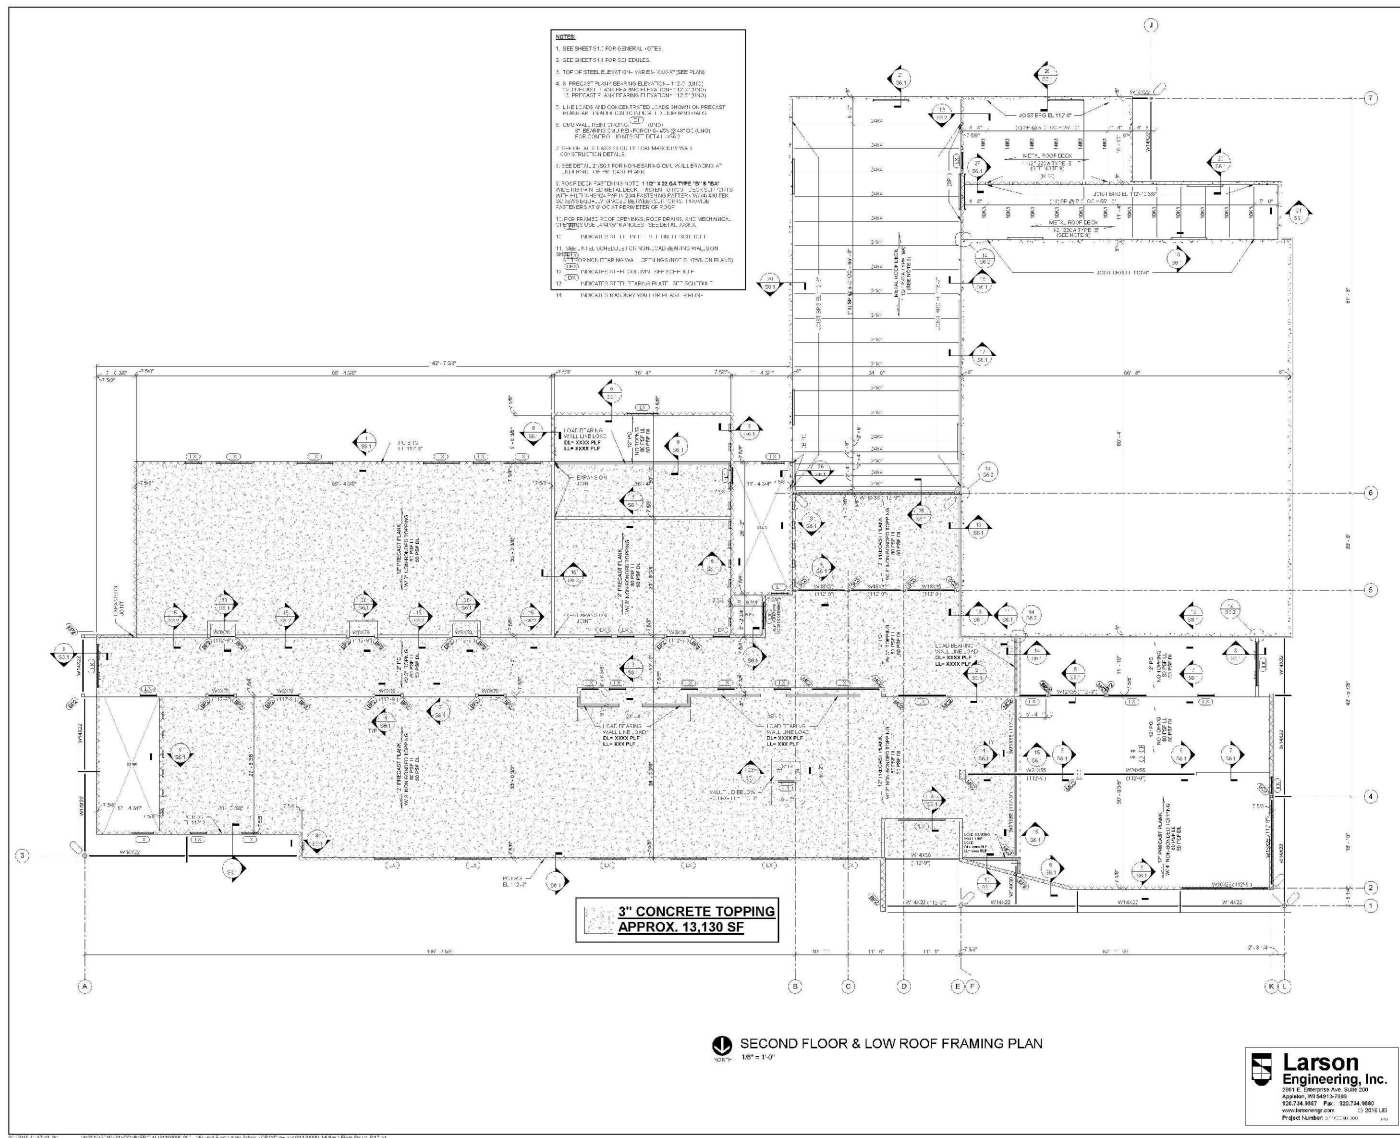

SECOND FLOOR & LOW ROOF FRAMING PLAN
1/8" = 1'-0"

Larson Engineering, Inc.
2001 E. University Ave. #200
Algonquin, IL 60110
P: 847-997-9838
F: 847-997-9838
Project Number: 16-009-1

PRELIMINARY
SECOND FLOOR & LOW ROOF
FRAMING PLAN

MIDLAND CUSD #7
New Elementary School
200 N. High Street
Lacon, IL

CBJ + CGA
ARCHITECTS
PROFESSIONAL CORPORATION
3000 E. University Ave. #200
Algonquin, IL 60110
P: 847-997-9838
F: 847-997-9838

REVISION	NO.	DESCRIPTION	DATE
1	1	ISSUED FOR PERMIT	9-2-16
2	2	ISSUED FOR PERMIT	9-2-16
3	3	ISSUED FOR PERMIT	9-2-16
4	4	ISSUED FOR PERMIT	9-2-16
5	5	ISSUED FOR PERMIT	9-2-16
6	6	ISSUED FOR PERMIT	9-2-16
7	7	ISSUED FOR PERMIT	9-2-16
8	8	ISSUED FOR PERMIT	9-2-16
9	9	ISSUED FOR PERMIT	9-2-16
10	10	ISSUED FOR PERMIT	9-2-16

S3.1

1

DRAWING REFERENCE: S3.1.....ADDED SHEET

© COPYRIGHT CBJ+CGA 2016

NORTH	SK-S006	BID PHASE: 1		Midland CUSD #7 New Elementary School 206 N. High Street Lacon, IL		Larson Engineering		3521 WINTERGREEN ALGONQUIN, ILLINOIS 60102 P: 847-997-9838 F: 847-658-0095 cbjarchitect@comcast.net
		SCALE: AS NOTED	BY: CBJ					
		PROJ. NO.: 16-009.1	DATE: 9-2-16					
Bid Phase 1								

1 SECTION
S5.2 1/2" = 1'-0"

2 SECTION
S5.2 1/2" = 1'-0"

DRAWING REFERENCE: S5.2.....ADDED DETAILS AT STAIR AND SHEET

© COPYRIGHT CBJ+CGA 2016

SK-S007

BID PHASE: 1

Midland CUSD #7
New Elementary School
 206 N. High Street
 Lacon, IL



Larson

Engineering



+ CGA
COXGROUPARCHITECT

3521 WINTERGREEN
ALGONQUIN, ILLINOIS 60102
P: 847-997-9838
F: 847-658-0095
cbjarchitect@comcast.net

NORTH

Bid Phase	1
-----------	---

SCALE: NTS

PROJ. NO.: 16-009.1

BY: CBJ
DATE: 9-2-16


PROJ. NO.: 16-009.1	DATE: 9-2-16
---------------------	--------------

The site plan for the Larson building shows a rectangular building footprint with a parking lot to the north and a landscaped area to the south. The building footprint is 145'-2 5/8" wide and 283'-8" deep. The parking lot is 120'-0" wide and 24'-8" deep. The landscaped area is 24'-8" wide and 9'-6" deep. The plan includes various annotations for construction and landscaping, including elevations, dimensions, and material callouts. Key features include:

- Building Footprint:** 145'-2 5/8" x 283'-8".
- Parking Lot:** 120'-0" x 24'-8".
- Landscaped Area:** 24'-8" x 9'-6".
- Annotations:**
 - 4" CONC SLAB EL 100'-0"** (multiple locations)
 - 4" CONC SLAB W/ 4% SLOPE**
 - 4" CONC SLAB W/ 2% SLOPE**
 - 4" CONC SLAB W/ 1% SLOPE**
 - 4" CONC SLAB W/ 0.5% SLOPE**
 - 4" CONC SLAB W/ 0.25% SLOPE**
 - 4" CONC SLAB W/ 0.125% SLOPE**
 - 4" CONC SLAB W/ 0.0625% SLOPE**
 - 4" CONC SLAB W/ 0.03125% SLOPE**
 - 4" CONC SLAB W/ 0.015625% SLOPE**
 - 4" CONC SLAB W/ 0.0078125% SLOPE**
 - 4" CONC SLAB W/ 0.00390625% SLOPE**
 - 4" CONC SLAB W/ 0.001953125% SLOPE**
 - 4" CONC SLAB W/ 0.0009765625% SLOPE**
 - 4" CONC SLAB W/ 0.00048828125% SLOPE**
 - 4" CONC SLAB W/ 0.000244140625% SLOPE**
 - 4" CONC SLAB W/ 0.0001220703125% SLOPE**
 - 4" CONC SLAB W/ 0.00006103515625% SLOPE**
 - 4" CONC SLAB W/ 0.000030517578125% SLOPE**
 - 4" CONC SLAB W/ 0.0000152587890625% SLOPE**
 - 4" CONC SLAB W/ 0.00000762939453125% SLOPE**
 - 4" CONC SLAB W/ 0.000003814697265625% SLOPE**
 - 4" CONC SLAB W/ 0.0000019073486328125% SLOPE**
 - 4" CONC SLAB W/ 0.00000095367431640625% SLOPE**
 - 4" CONC SLAB W/ 0.000000476837158203125% SLOPE**
 - 4" CONC SLAB W/ 0.0000002384185791015625% SLOPE**
 - 4" CONC SLAB W/ 0.00000011920928955078125% SLOPE**
 - 4" CONC SLAB W/ 0.000000059604644775390625% SLOPE**
 - 4" CONC SLAB W/ 0.0000000298023223876953125% SLOPE**
 - 4" CONC SLAB W/ 0.00000001490116119384765625% SLOPE**
 - 4" CONC SLAB W/ 0.000000007450580596923828125% SLOPE**
 - 4" CONC SLAB W/ 0.0000000037252902984619140625% SLOPE**
 - 4" CONC SLAB W/ 0.00000000186264514923095703125% SLOPE**
 - 4" CONC SLAB W/ 0.000000000931322574615478515625% SLOPE**
 - 4" CONC SLAB W/ 0.0000000004656612873077392578125% SLOPE**
 - 4" CONC SLAB W/ 0.00000000023283064365386962890625% SLOPE**
 - 4" CONC SLAB W/ 0.000000000116415321826934814453125% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000582076609134674071875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000002910383045673370359375% SLOPE**
 - 4" CONC SLAB W/ 0.000000000014551915228366851796875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000072759576141834258984375% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000363797880709171294921875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000001818989403545856474609375% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000009094947017729282373046875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000045474735088641191865234375% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000227373675443205959326171875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000001136868377216029796630859375% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000005684341886080148983154296875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000028421709430400744915771484375% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000142108547152003724578857221875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000710542735760018622894286109375% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000003552713678800093114471428546875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000177635683940004655723571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000008881784197000232786178571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000000444089209850011639308928571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000022204460492500581965446428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000001110223024625029098272321428546875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000000055511151231251454913610571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000277555756156257274556828571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000000013877787807812863727841428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000000693889390390643186392071428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000034694469519532159319603571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000000001734723475976607965980178571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000000086736173798830398299008928571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000004336808689941519914950446428571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.000000000000000000216840434497075995747522321428571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000001084202172485379978737610571428571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.00000000000000000005421010862426899893688053571428571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000000271050543121344994684402678571428571428571428546875% SLOPE**
 - 4" CONC SLAB W/ 0.0000000000000000000135525271560672497342201339285714285**

Architectural floor plan showing structural details and dimensions. The plan includes various rooms and corridors, with dimensions in feet and inches. Key annotations include:

- Slab Control Joints:** Indicated by dashed lines and labels such as "SLAB CONTROL JOINTS @ 10'-0\"/>

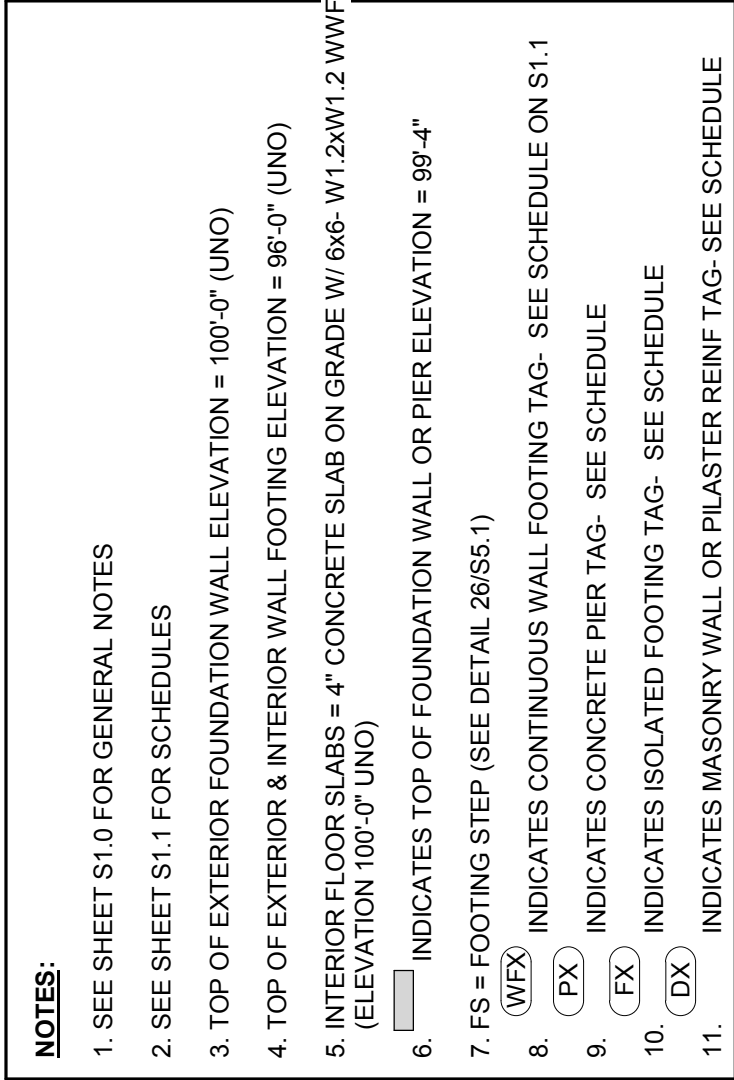


JOB:	16-009.1	NO.	1	ADENDUM 1	09-01-16
DATE:	8-19-16				
SCALE:					
DRAWN:	Author				
CHECKED:	Checker				

CBJ + **CGA**

MIDLAND CUSD #7
New Elementary School
206 N. High Street
Lacon, IL

DRAWINGS:
FOUNDATION DETAILS

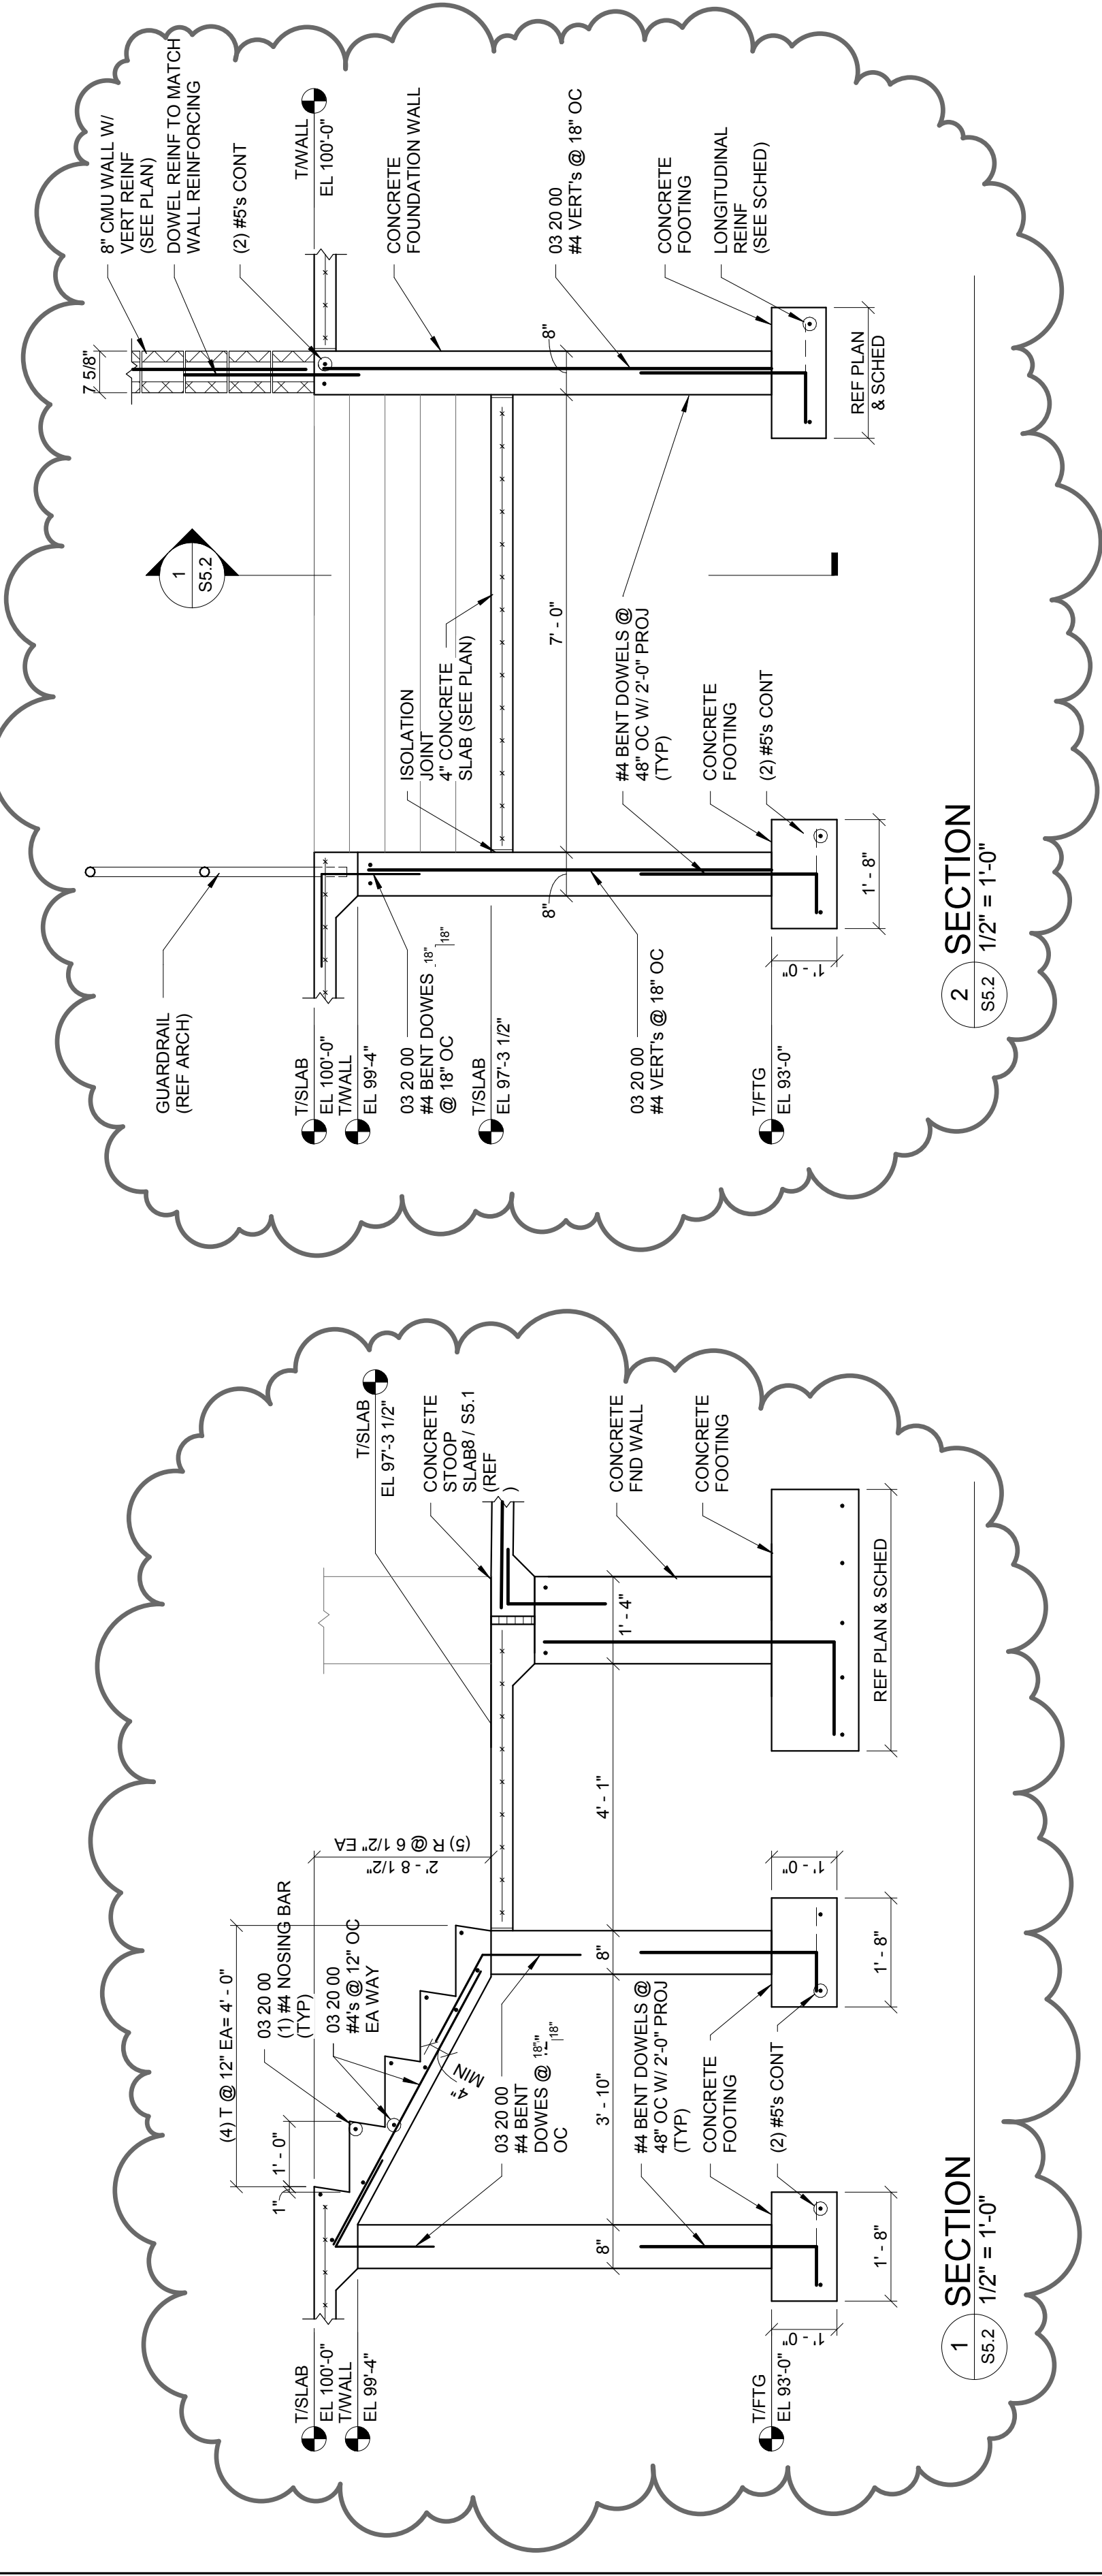

PROJECT MANUAL

August 19, 2016

Revised
September 2, 2016

Bid Phase #1

for a

New Elementary School

for the

Midland Community Unit School District #7

to be located at:
206 N. High Street
Lacon, IL 61540

ARCHITECTS:

CBJ ARCHITECTS P.C.
Algonquin, IL

COX GROUP ARCHITECTS
Appleton, WI

TABLE OF CONTENTS

DIVISION 00 - PROCUREMENT AND CONTRACTING REQUIREMENTS

00 2113	INSTRUCTIONS TO BIDDERS
00 4100	BID FORM
00 5000	CONTRACTING FORMS AND SUPPLEMENTS
00 5200	AGREEMENT FORM
00 7200	GENERAL CONDITIONS
00 7300	SUPPLEMENTARY CONDITIONS (NOT INCLUDED AT THIS TIME)

DIVISION 01 - GENERAL REQUIREMENTS

01 1000	SUMMARY
01 2000	PRICE AND PAYMENT PROCEDURES
01 2200	UNIT PRICES
01 2300	ALTERNATES
01 3000	ADMINISTRATIVE REQUIREMENTS
01 3216	CONSTRUCTION PROGRESS SCHEDULE
01 3553	SECURITY PROCEDURES
01 4000	QUALITY REQUIREMENTS
01 4100	REGULATORY REQUIREMENTS
01 4216	DEFINITIONS
01 5000	TEMPORARY FACILITIES AND CONTROLS
01 5100	TEMPORARY UTILITIES
01 5213	FIELD OFFICES AND SHEDS
01 5500	VEHICULAR ACCESS AND PARKING
01 5713	TEMPORARY EROSION AND SEDIMENT CONTROL
01 7000	EXECUTION AND CLOSEOUT REQUIREMENTS
01 7419	CONSTRUCTION WASTE MANAGEMENT AND DISPOSAL
01 7800	CLOSEOUT SUBMITTALS
01 7900	DEMONSTRATION AND TRAINING

DIVISION 03 - CONCRETE

03 2000	CONCRETE REINFORCING
03 3000	CAST-IN-PLACE CONCRETE

DIVISION 07 – THERMAL AND MOIDTURE PROTECTION

07 9200	JOINT SEALANTS
---------	----------------

DIVISION 31 - EARTHWORK

31 1000	SITE CLEARING
31 2200	GRADING
31 2316	EXCAVATION
31 2316.13	TRENCHING
31 2323	FILL

DIVISION 32 - EXTERIOR IMPROVEMENTS

32 1123	AGGREGATE BASE COURSES
32 1216	ASPHALT PAVING
32 1313	CONCRETE PAVING
32 1713	PARKING BUMPERS
32 1723.13	PAINTED PAVEMENT MARKINGS
32 1726	TACTILE WARNING SURFACING

DIVISION 33 - UTILITIES

33 0513	MANHOLES AND STRUCTURES
33 1116	SITE WATER UTILITY DISTRIBUTION PIPING
33 1300	DISINFECTING OF WATER UTILITY DISTRIBUTION
33 3111	SITE SANITARY UTILITY SEWERAGE PIPING
33 4111	SITE STORM UTILITY DRAINAGE PIPING
33 4600	SUBDRAINAGE
33 5111	SITE GAS DISTRIBUTION
33 7119	ELECTRICAL UNDERGROUND DUCTS AND MANHOLES

APPENDIX

SOILS REPORT

SECTION 00 2113
INSTRUCTIONS TO BIDDERS

PART 1 GENERAL

1.01 BID PACKAGES FOR BID PHASE #1

- A. BP #01 Earthwork and Storm Sewer
- B. BP #02 Site Sanitary Sewer and Site Water
- C. BP #03 Asphalt Paving
- D. BP #04 Site Concrete
- E. BP #05 Building Concrete

1.02 BID SUBMISSION

- A. Bids signed and sealed, executed, and dated will be received Tuesday, September 13, 2016 by 2:00 P.M. (CST) at the Midland Middle School located at 901 Hilltop Drive, Sparland, IL 61565.
- B. The front of the sealed envelope must be labeled as follows:
New Midland Elementary School
Bid Phase #1 - Bid Package # _____
(The bidder is to note the Bid Package # and description.)
Bidders Name and Address: _____
- C. Bidders shall be solely responsible for the delivery of their bids in the manner and time prescribed.
- D. Submit two copies of the executed offer on the Bid Forms provided, signed and sealed with the required bid security.
- E. Bids must be regular in every respect and no exclusions or special conditions shall be made or included on the bid form by the Bidder.
- F. Bidder's signature shall be construed as acceptance of, and willingness to comply with all provisions of the Illinois Revised Statutes, Prevailing Wage Laws as amended August 8, 1961. All laborers, workers, and mechanics engaged in construction will be paid not less than the "Prevailing Wage". Contractor agrees to abide by the current Prevailing Rate of Wages for Construction Workers in Marshall County.

1.03 BID INTENT

- A. The intent of this bid request is to obtain an offer to perform work to complete a the New Midland Elementary school located at 206 N. High Street, Lacon, Illinois, 61540.

1.04 WORK IDENTIFIED IN THE CONTRACT DOCUMENTS

- A. Construction work shall be performed in compliance with the requirements of all applicable local, state, and federal laws, regulations, and rules, and the requirements of the Construction Documents.
- B. Work shall not commence until all insurance and the Material-Payment bond requirements are met.

1.05 CONTRACT TIME

- A. Owner requires the work of this contract to be completed as quickly as possible and in accordance with the overall project schedule.

1.06 BID DOCUMENT AVAILABILITY AND EXAMINATION

A. Bid Documents will be available to view and download at the following locations:

Midland CUSD #7 website at the following link:

- http://www.midland-7.net/apps/pages/index.jsp?uREC_ID=413509&type=d&pREC_ID=950161

Submittal Exchange at the following link:

- <https://www.submittalexchange.com/bid/MidlandElementarySchool/Planroom>

Greater Peoria Contractors Association (309-692-5710)

Illinois Valley Contractors Association (815-223-0561)

B. All Bidders can contact Beth Huffman at MCP (309-291-0913) for assistance.

1.07 QUESTIONS AND ADDENDA

A. All questions are to be submitted in writing via email to Midwest Construction Professionals office to either beth@midconpro.com or chris@midconpro.com

B. Addenda will be issued during the bidding period and sent to all plan holders. All addenda will become part of the Bid Documents. Include the resultant cost in the Bid Amount.

C. Verbal answers or email answers are not binding on any party.

1.08 SITE ASSESSMENT

A. It is recommended that all Bidders visit the site prior to submitting their bid so they can each be aware of existing conditions, accessibility, etc. Conditions observed shall be correlated with the requirements of the Bid Documents. Existing conditions include, but are not limited to: the existing site, existing structures, obvious obstructions not detailed on the Bid Documents, etc. Failure to familiarize itself with the local conditions shall in no way relieve the Bidder from the responsibility for properly estimating the difficulty and or costs of successfully performing the work, and shall not be construed as a basis for subsequently initiating a change in the contract amount and/or time.

1.09 BID FORMAT AND BID INELIGIBILITY

A. This bid forms must be filled out in their entirety. If the form is not filled out, the bid may be considered as not responsive.

B. Bids that are unsigned, improperly signed or sealed, conditional, illegible, obscure, contain errors, alterations, or irregularities of any kind may, at the discretion of the Owner, be declared unacceptable.

C. Bid Forms, Appendices, and Enclosures that are improperly prepared may, at the discretion of the Owner, be declared unacceptable.

1.10 INSURANCE REQUIREMENTS

A. See the required insurance requirements in the project manual.

1.11 BID SECURITY

A. Bids shall be accompanied by a bid security as required in the Project Manual.

B. All Bidders will have to provide a Payment and Performance Bond.

C. All Bidders are to include any and all costs for their Bid Security as well as their Payment and Performance Bond in their Bid amount.

D. The security deposit will be returned after delivery to the Owner of the required Payment and Performance Bond by the accepted bidder.

E. If no contract is awarded, all security deposits will be returned.

1.12 SELECTION AND AWARD OF ALTERNATES

A. The Owner reserves the right to award bid based on base bid amounts or they may award bids on base bid amounts including one or more alternate bids.

1.13 DURATION OF OFFER

A. Bids shall remain open to acceptance and shall be irrevocable for a period of one hundred twenty (120) days after the bid opening.

1.14 ACCEPTANCE OF OFFER

A. The Owner reserves the right to accept or reject any and all bids.

1.15 GENERAL NOTES FOR ALL BID PACKAGES

A. GENERAL NOTES FOR ALL SCOPES OF WORK

1. Each Contractor is responsible for communicating project requirements to all employees associated with the project.
2. Project managers or the project foreman for each contractor are required to attend weekly project coordination meetings. Attendance is required within two weeks prior to starting their work, at all times during their work on site, and two weeks after their work is completed.
3. All contractor's personnel that enter the site are to be made aware of any and all safety conditions for the project. Each contractor is to provide the Construction Manager with copies of their weekly toolbox meeting minutes.
4. Foremen are to be supplied (by their own contractor) with a complete set of drawings, specifications, shop drawings, etc.
5. Contract price includes all escalation required for the project schedule.
6. All hoisting required, shall be provided by the individual contractor needing the hoisting.
7. Contractors are to provide scaffolding as required for the completion of their work.
8. Contractors are responsible to submit all shop drawings and submittals through Submittal Exchange as noted in the bidding documents. Each contractor is responsible to train their employees as needed to utilize Submittal Exchange efficiently and correctly throughout the duration of the project. Submittal Exchange does not charge for the training.
9. It is understood that all submittals and shop drawings submitted shall be in strict accordance with plans, specifications, and other contract documents. Substitutions will not be allowed unless prior approval from the owner, architect, and construction manager was obtained.

Any delays associated with submitting unspecified products will be the responsibility of the contractor.

10. Contractors are to provide a schedule of values within two weeks of receiving a signed contract.
11. Original Certificate of Insurance must be submitted and approved prior to the start of your work. If your insurance is not acceptable or has expired your crew will not be allowed on the job site. All trade contractors must provide and maintain insurance in accordance with the contract throughout the project.
12. Contractors are responsible for updating as-built drawings with any changes issued during construction.
13. Contractors are to coordinate their bid as well as their work with all drawings, architectural, civil, structural, fire protection, HVAC, plumbing, electrical, etc. that are part of the contract documents.
14. Contractors must receive a signed daily ticket from the Construction Manager to be reimbursed for any Time and Material work. Tickets will only be signed on the day the work takes place or the following business day. This is required even if the T & M task being performed is a multi-day task. Failure to provide a ticket on the day following the work will result in a rejection of the costs.
15. Approved tickets to be compiled and forwarded to the Construction Manager within three weeks of the ticket date. Failure to do so will result in the immediate rejection of the requested costs. Tickets to have a cover page with date, reference and brief description of the work performed along with a breakdown of labor, material, equipment, and OH&P costs. No trade contractor to provide additional work without authorization from the Construction Manager. Any work done without said authorization may not be paid.
16. Contractors shall allow sufficient time to inspect and accept the work of the previous contractor. Should any discrepancies be discovered, the Construction Manager shall be notified sufficiently in advance so that corrective action can be accomplished without affecting the progress of any other contractors. If the contractor proceeds without notifying the

Construction Manager of any discrepancies, it is understood the work of the preceding contractor was acceptable for the installation of this contractor's work.

17. Upon completion of their work, each contractor shall remove all marks, stains, smudges, chips, nicks, etc., regardless of origin, including removal of all manufacturing and shipping labels and tags.
18. Each contractor shall be responsible for all cutting that may be required in connection with his work. If their work was not coordinated and installed at the proper time, he will be responsible for the cost associated with patching.
19. Contractors are to staff the job to meet the project schedule. Work includes all staffing, supervision, and premium time required to meet this schedule.
20. Contractors are to work premium time to make up for any lost time due to contractor error (e.g. lack of material, workers, inaccurate ordering, etc.).
21. The contractor shall be responsible for the cost of expediting any deliveries in accordance with the project schedule.
22. Contractor's foreman and/or project managers' shall coordinate with the Construction Manager and Architect for all inspections required. This shall be done on an area-by-area basis. The contractors are responsible for personally ensuring that all work is complete and

in compliance. Any charges for re-inspections, etc. are to be paid by the responsible contractors.

23. All work to comply with both OSHA safety standards as well as the safety programs of each contractor. The more stringent of the two programs applies to each job task.
24. Contractors are to supply all safety equipment associated with their work.
25. It is mandatory that all contractors workers and staff on site wear hard hats and safety glasses at all times.
26. Contractors shall coordinate access for all equipment deliveries into the building. Failure to do so can result in a deductive change order for other trades to remove their work for equipment access.
27. Contractors shall clean up their own work and debris continuously as needed and at a minimum on a weekly basis. Backcharges will be sent to any contractors if the Construction Manager has to provide manpower to clean up for certain contractors.
28. All factory startups and training sessions are to be coordinated with the Construction Manager and Architect at least 2 weeks ahead of time.
29. Contractors are responsible for installing all owner-furnished items as indicated on the drawings, in the specifications, or in the scope of work.
30. Temporary power (inside and out) will include temporary lights and power for small tools. Each subcontractor must make his own arrangements (and pay) for any special temporary electric requirements beyond those outlined above (i.e. welders, special fans, etc...) The electrical contractor will be providing temporary lighting and power as needed to the building

site and within the building during construction. The Owner will be paying for the power usage.

31. Smoking is not allowed on the job site. This is school property and it is a state law. Any worker found smoking will be asked to leave the job site.
32. Contractors are responsible for weekly toolbox talks. Failure to comply can result in delayed payments. Toolbox talks, signed by attendants, are to be turned in on a weekly basis to the Construction Manager.
33. All traffic control required for deliveries, hoisting, scaffolding, etc., is the responsibility of the contractor. All deliveries must be coordinated with the Construction Manager.
34. All deliveries to be scheduled with the Construction Manager 48 hours in advance. Contractors are responsible for coordinating any special deliveries that affect other contractors. Contractors are responsible for all freight, and all unloading of material.
35. Contractors are responsible for layout and verification of their own work.
36. Storage of materials and equipment at the site shall be permitted only to the extent approved in advance by the Construction Manager, and if anything stored obstructs the progress of any portion of the work, it shall be promptly removed and relocated by the Contractor without reimbursement. Any damage or loss of items stored at the job site will be the responsibility of the contractor. Materials not being used on the job are to be removed immediately. Materials are to be supplied to the job on an "as needed" basis. If not removed or relocated within 24 hours, the Construction Manager will do so with its own forces and back-charge the responsible contractor.
 - i. Each contractor shall be responsible for the erection, dismantling, maintenance, hook-up of utilities, security, etc., that may be necessary in setting-up storage area.
37. Contractors are responsible for fire-safing any penetrations associated with their work in walls, floors, ceilings, etc...
38. Contractors are responsible for completing all punch-list items in the allotted times.
39. Contractors are responsible for all permits, fees, licenses, etc. for deliveries of material and equipment to the job site. This would include excess tonnage charges, oversized load

charges, etc. Any delays associated with improper coordination with the state or local governments are the responsibility of this contractor.

40. All contractors are responsible for providing one additional hard hat and safety glasses at the job for workers who forget or lose theirs.
41. Any incidental supporting angles, clips, brackets, hardware, etc., which is inherent to the installation or construction of any assembly, but is not shown on the documents, is to be included in the original contract of the contractor installing the assembly.
42. Each contractor will be required to maintain the streets and walks surrounding the project clean of debris and mud at all times. Each trade contractor is responsible for his or her suppliers and/or sub-trade contractors. All trucks leaving the site must be clean and free of debris.
43. Each contractor will be required to maintain first aid equipment on site at all times.
44. The cost of licenses and bonds required by the State or local governments are the responsibility of the contractor. Contractors must be licensed and bonded with per any city requirements prior to the start of your work.
45. Notwithstanding the dimensions given on the plan, specification, shop drawings, and other documents, it shall be the obligation and responsibility of each contractor or supplier to take

such filed measurements to ensure the proper matching and fitting of the contractor's work with the work of the other trades.

46. It is the subcontractor's responsibility to provide all necessary safety protection including any additional ventilation to maintain proper airflow and distribution.

47. Accounting Procedures

a. A Complete Billing Package is as follows:

- i. Due by the 25th of the month. Billing Cycle is through the 20th of the month. End of month projections are not allowed on this project.
- ii. G702CMA: Application for Payment
- iii. G703: Schedule of Values
- iv. Contractor's Affidavit
- v. Stored Material Documentation (if applicable): Bill of Sale, Evidence of Property Insurance, Bill of Lading from supplier (if applicable)
- vi. One (1) original copy and two (2) copies of a completed billing package are required.
- vii. Certified payroll reports to be included each month.

b. An Accurate Billing Package Includes:

- i. 10% retention will be held on all subcontracts.
- ii. When listing change orders on the G703 you must include the change order number and a brief description of the change order. Change orders must also be included in the "change order summary" located on the G702CMA form and be revised as needed.
- iii. Only "fully executed" change orders will be allowed to be included on pay applications.
- iv. A breakdown of costs listed on the G703 for review. List labor and material separately for each description.

1.17 PROJECT SCHEDULE & PUNCH LIST COMPLETION

1. Project Schedule

- a. The schedule dates are to be used as a guideline for bidding purposes to provide sufficient manpower, number of crews, equipment, and material to complete the work within the specified time frames. Neither the Construction Manager, Architect, nor Owner are responsible for assumptions made by the bidding Contractors. The Construction Manager has the right to act on behalf of the Owner to adjust and/or change the start or completion dates as required due to delay in gaining access to the site, weather delays, or another Contractor's performance within reason. The Contractors shall cooperate with the Construction Manager at all times and provide timely information as required to ensure coordination and timely completion of the work. After award of their contract, each Contractor is responsible to submit to the Construction Manager, detailed schedule information to meet the scheduled completion dates shown on the project schedule. This information will be coordinated with the other Contractors and the Construction Manager's schedule to develop an overall comprehensive project schedule to meet or exceed the original project schedule.

- b. All Contractors recognize the project completion is necessary for students to attend classes for the school year beginning in August of 2017. All contractors shall provide labor and equipment as necessary to meet the schedule dates provided within this project schedule.
- c. The activity durations included is preliminary and subject to revisions as necessary to meet the overall project completion date and critical milestone dates. All Contractors should be prepared to start any activity within any area at all times in order to the meet the project schedule.
- d. Provide expedited shop drawings and submittals to meet the project schedule.
- e. Work on site shall start immediately upon issuance of a Notice to Award, and submittal of acceptable Certificates of Insurance and Payment and Performance Bonds.

2. Project Punch List

- a. Contractors are required to complete all punchlist items to the Owner's satisfaction within thirty (30) days from the issuance of the punchlist. If punchlist items are not completed within this period, the Owner may utilize another Contractor to complete the work. Payment for this work shall be made from the original Contractor's retainage.
- b. All Contractors are required be proactive in the completion of all punchlist work. To accommodate phased turnover of building areas, Contractors will be required to perform punchlist work in phases. Contractors will be required to complete work on time and in a manner that will allow for punchlists to be developed, completed, and inspected so that the Owner move-in of the F.F. & E. and occupancy will not be affected. Any corrective work required in occupied areas must be done during off-hours and at no additional cost to the Owner. Punchlist efforts must not hinder the progress and completion of work in other areas.

END OF SECTION

SECTION 00 4100

BID FORM

BID FORM

THE PROJECT AND THE PARTIES

1.01 TO:

A. Owner

1. Board of Education
Midland Community Unit School District #7
1830 State Rt. 17
Varna, Illinois 61375

1.02 FOR:

A. New Elementary School

1.03 DATE: _____ (Bidder to enter date)

1.04 SUBMITTED BY: (Bidder to enter name and address)

A. Bidder's Full Name _____

1. Address _____

2. City, State, Zip _____

1.05 OFFER

The Undersigned Acknowledges:

1. Receipt of all Contract Documents prepared by CBJ Architects P.C. including but not limited to all drawings, specifications, and addenda.
2. The following Addenda have been received. The modifications to the Bid Documents noted below have been considered and all costs are included in the Bid Sum.

Addenda # _____ Dated _____.

Addenda # _____ Dated _____.

Addenda # _____ Dated _____.

Addenda # _____ Dated _____.

Addenda # _____ Dated _____.

3. Has received, read, understands, and accepts the terms and conditions outlined in the following Contract Documents, the Advertisement for Bid, Instruction to Bidders, Project Schedule, and Scopes of Work for ALL Bid Packages.
4. Has reviewed and is familiar with the site where the work is to be executed; and has become familiar with the local conditions as they might in any way affect the cost and/or execution of the Work.
5. Has carefully examined and understands the Contract and Bidding Documents and acknowledges that the Bid is in accordance with these documents.
6. In making this Bid the Bidder represents that:

SECTION 00 4100

BID FORM

- a. This Bid may not be modified, withdrawn, or cancelled until 120 calendar days after the Bid opening date, without consent of the Owner.
 - b. The right is reserved by the Owner to reject any or all Bids, to waive any or all informalities in connection therewith.
 - c. The bidder will enter into and execute a Contract with the Owner, if awarded on the basis of this Bid, and in connection therewith to:
 - i. Furnish all bonds and insurance required by the Bidding Documents.
 - ii. Commence with the Work within seven (7) days upon issuance of a Notice to Award, prosecute the Work regularly and diligently and complete the Work within the Time specified in Completion Dates and per the Project Schedule included in the Bid Documents.
 - iii. Accomplish the Work in accordance with the Contract and agrees to provide all labor, materials, plant, equipment, transportation, and other facilities as necessary and/or required for the complete and satisfactory execution of the Work.
7. Has notified a surety company of its Bid for work to be performed on the project. The surety company has agreed to issue Performance and Labor and Material Payment Bonds for the Work if the Bid is accepted.
8. Has checked all of the figures contained in this Bid and further understands that the Owner will not be responsible for any errors or omissions made therein by the undersigned.
9. Has complied and/or will comply with all requirements concerning licensing and with all other local, state, and national laws, and that no legal requirement has been or will be violated in making or accepting this Bid, in awarding the Contract and/or in the prosecution of the Work required thereunder.
10. Declares that the person(s) signing this Bid is/are fully authorized to sign on behalf of the named firm and to fully bind the named firm to all conditions and provisions thereof.
11. Declares that no person(s) or company other than the firm listed below or as otherwise indicated hereinafter has any interest whatsoever in this Bid or the Contract that may be entered into as a result thereof, and that in all respects the Bid is legal and fair, submitted in good faith, without collusion or fraud.
12. Will execute said Contract as soon as practical after the date of Notice of Award; or in any event, not later than ten (10) days from the date of such notification.
13. Provides the following applicable Base Bids and Alternate Bids:
 - a. If bidding more than one BID PACKAGE, submit a separate, complete, sealed bid for each bid package.

SECTION 00 4100

BID FORM

- b. If providing a Combination Bid for multiple Bid Packages, include a separate, sealed envelope containing the Combination Bid. Indicate the Bid Packages to be combined and the total Combined Base Bid amount.
- c. Include unit costs listed on the bid form.

Base Bid: Bid Package # _____ (Bid Package Name)

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

_____ Dollars (\$_____)

Combination Bid:

Bid Package # _____ (Bid Package Name)

Bid Package # _____ (Bid Package Name)

Bid Package # _____ (Bid Package Name)

Bid Package # _____ (Bid Package Name)

Bid Package # _____ (Bid Package Name)

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

_____ Dollars (\$_____)

Alternate Bid #1: Bid Package # 01 Earthwork and Storm Sewer
(Bid Package Name)

Provide 4" of crushed asphalt covering the parking lot drives and the south parking lot spaces. See plan showing the area issued in the addendum. The area is approximately 20,560 square feet. This alternate includes the necessary cut and/or fill to establish the rough grade at 4" below the bottom of the 10" of aggregate base for the asphalt paving. Provide a geo grid fabric and then place 4" of crushed asphalt/concrete that will be left on site by Iron Hustler Excavation during the building demolition. The material will be left in place.

****Please see Drawing C-3.2 Temporary Pavement Plan.**

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$_____)

SECTION 00 4100

BID FORM

Alternate Bid #2: Bid Package # 01 Earthwork and Storm Sewer
(Bid Package Name)

Provide 4" of crushed asphalt covering the established rough grade to the north and west of the new building as shown on the drawing provided in addendum. This area is approximately 16'-18' wide and covers approximately 8,400 square feet. This will be placed once the rough grade is established in these areas. Provide a geo grid fabric and then place 4" of crushed asphalt/concrete that will be left on site by Iron Hustler Excavation during the building demolition. The fabric and material will be removed by others at a later date.

*****Please see Drawing C-3.2 Temporary Pavement Plan.***

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$ _____)

Alternate Bid #3: Bid Package # 04 Site Concrete
(Bid Package Name)

Provide 6" of crushed asphalt/concrete as the granular base in lieu of the specified 6" of aggregate base course. The crushed asphalt/concrete will be left on site by Iron Hustler Excavation during the building demolition.

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$ _____)

Alternate Bid #4: Bid Package # 05 Building Concrete
(Bid Package Name)

Provide all winter conditions necessary to complete the **footings and foundations** throughout the building. Include providing and removing concrete blankets, etc. as needed to provide the adequate protection. Others will take care of temporary enclosures as well as providing fuel for temporary heat. The concrete contractor will have to provide heaters and hose if temporary heat is required over and beyond the blankets and other measures. Include changes to the concrete mix as needed for cold weather. Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$ _____)

SECTION 00 4100

BID FORM

Alternate Bid #5: Bid Package # 05 Building Concrete
(Bid Package Name)

Provide all winter conditions necessary to complete the slab on grade throughout the building. Include providing and removing concrete blankets, etc. as needed to provide the adequate protection. Others will take care of temporary enclosures as well as providing fuel for temporary heat. The concrete contractor will have to provide heaters and hose if temporary heat is required over and beyond the blankets and other measures. Include changes to the concrete mix as needed for cold weather. The Gym & Topping Slab are not to be included in this Alternate.

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$ _____)

Alternate Bid #6: Bid Package # 02 Site Sanitary & Site Water
(Bid Package Name)

Provide the installation of the 6" water main between 6th Street and 7th Street. Include excavation, backfill, and compaction as required. This will also include the furnishing and installation of the fire hydrant within the run of water main pipe.

Bidder agrees to perform all Work as set forth in the Bidding Documents for the sum of:

Add / Deduct _____
(Circle Add or Deduct)
_____ Dollars (\$ _____)

SECTION 00 4100**BID FORM****Unit Costs**

Refer to the Scopes of Work for unit costs to be provided. The unit costs are applicable for changes in Work, both additions and deletions. The unit costs are for Work complete and in place and include all costs such as material, labor, equipment, freight, taxes, insurance, fringe benefits, and overhead and profit. Also include costs for coordination with other trades where applicable. In the even the unit costs quoted exceed industry standards or fair market value, the Owner reserves the right to request pricing for changes at cost plus allowable mark-up for overhead and profit or a lump-sum under the terms of the agreement.

Unit Cost Description (Contractor Responsible to include all labor, material, equipment, overhead, & profit in the unit cost)	Unit Cost	Unit of Measure
<u>Footings, Foundations, or Slab on Grade:</u> For unsuitable soils discovered during your work, provide a Cubic Yard cost to remove and legally dispose of unsuitable soils off site, replace with an approved CA-6 material that is compacted as required.		Cubic Yard
<u>Earthwork, Site Concrete, or Asphalt Paving:</u> For unsuitable soils discovered during your work, provide a Cubic Yard cost to remove and legally dispose of unsuitable soils off site, replace with an approved CA-6 material that is compacted as required.		Cubic Yard
<u>Site Concrete:</u> Provide a Square Foot cost to provide <u>6'</u> wide sidewalks. Include excavation, compacted granular base, reinforcement, forming, and concrete complete.		Square Foot
<u>Site Concrete:</u> Provide a Square Foot cost to provide <u>5'</u> wide sidewalks. Include excavation, compacted granular base, reinforcement, forming, and concrete complete.		Square Foot
<u>Storm Sewer, Sanitary Sewer, or Water Main:</u> For unsuitable soils discovered during your work, provide a Cubic Yard cost to remove and legally dispose of unsuitable soils off site, replace with an approved CA-6 material that is compacted as required.		Cubic Yard
<u>Building Concrete:</u> Provide a square foot cost to provide Barrier One in the concrete slab on grade.		Square Foot

1.06 CHANGES TO THE WORK

- A. Each bidding contractor will be allowed the following overhead and profit for all change orders.:
1. Fifteen (15) percent overhead and profit on the net cost of our own Work;
 2. Five (5) percent on the cost of work done by any Subcontractor.

1.08 BID FORM SIGNATURE(S)

- A. See attached sheets. These must be signed and included with your sealed bid.

SECTION 00 4100

BID FORM

BIDDER ELIGIBILITY CERTIFICATION

The Criminal Code of 2012 requires that all the contractors bidding for public bodies or agencies in the State of Illinois certify that they are not barred from bidding on public contracts for bid rigging or bid rotation.

The following certification must be signed and submitted with bidder's bid proposal.
FAILURE TO DO SO WILL RESULT IN DISQUALIFICATION OF THE BIDDER.

Name of Bidder/Contractor _____
as part of its bid for the Board of Education of Midland Community Unit School District # 7, hereby certifies that the said contractor is not barred from bidding on the aforementioned contract as a result of a violation of either Section 33E-3 (bid rigging) or 33E-4 (bid rotating) of Article 33E of the Criminal Code of 2012 (20 ILCS 5/1-1 *et seq.*).

Firm Name: _____

By: _____
(Authorized Agent of Contractor)

Title: _____

Subscribed and sworn to before me

This _____ day of _____, 2016

Notary Public

SECTION 00 4100

BID FORM

CERTIFICATE OF COMPLIANCE WITH PREVAILING WAGE ACT

The undersigned Contractor hereby certifies to the Board of Education of Midland Community Unit School District # 7 that all work under this Contract shall comply with the Prevailing Wage Act of the State of Illinois, pursuant to 820 ILCS 130/0.01, *et. seq.*, and as amended, with rates to be paid that are in effect at the time work is performed. Contractors shall submit monthly certified payroll records to the District as set forth in 820 ILCS 130/5.

Firm Name _____

Address _____

Signature of Officer

Title

Subscribed and sworn to before me

This _____ day of _____, 2016

Notary Public

SECTION 00 4100

BID FORM

CERTIFICATE OF COMPLIANCE WITH ILLINOIS HUMAN RIGHTS ACT

All successful contractors must comply with the provisions of the Illinois Human Rights Act (ACT) dealing with the equal employment opportunities (Section 2-105, 775 ILCS 5/2-105) including equality of employment opportunity and the regulations of the Department of Human Rights of the State of Illinois and also must provide for the adoption and implementation of written Sexual Harassment Policies. The statutory provisions require that the written Sexual Harassment policy include, at the minimum, the following information: (i) the illegality of sexual harassment, (ii) the definition of sexual harassment under Illinois Law, (iii) a description of sexual harassment, utilizing examples; (iv) a vendor's internal compliant process including penalty; (v) the legal recourse, investigative and complaint process available through the Department of Human Rights Commission; (vi) protection against retaliation as provided by Section 6-101 of the Illinois Human Rights Act.

Firm Name _____

Address _____

Signature of Officer

Title

Subscribed and sworn to before me

This _____ day of _____, 2016

Notary Public

SECTION 00 4100

BID FORM

**CONTRACTOR'S CERTIFICATE OF COMPLIANCE WITH
ILLINOIS DRUG-FREE WORKPLACE ACT**

Pursuant to 30 ILCS 580/1 *et seq.* (the "Drug Free Workplace Act"), the undersigned Contractor hereby certifies to the Board of Education of Midland Community Unit School District #7 that it will provide a drug-free workplace by:

A. Publishing a statement:

1. Notifying employees that the unlawful manufacture, distribution, dispensation, possession, or use of a controlled substance, including cannabis, is prohibited in the contractor's workplace.
2. Specifying the actions that will be taken against employees for violations of such prohibition.
3. Notifying the employee that, as a condition of employment on such contract, the employee will:
 - a. Abide by the terms of the statement; and
 - b. Notify the employer of any criminal drug statute conviction for a violation occurring in the workplace no later than five (5) days after such conviction.

B. Establishing a drug-free awareness program to inform employees about:

1. The dangers of drug abuse in the workplace;
2. The contractor's policy of maintaining a drug-free workplace;
3. Any available drug counseling, rehabilitation, and employee assistance programs; and
4. The penalties that may be imposed upon employees for drug violations.

C. Making it a requirement to give a copy of the statement required by subsection "A" to each employee engaged in the performance of the contract and to post the statement in a prominent place in the workplace.

D. Notifying the contracting or granting agency within ten (10) days after receiving notice under part "b" of paragraph "3" of subsection "A" from an employee or otherwise receiving actual notice of such conviction.

BID FORM

- Failure to abide by this Contractor's Certificate of Compliance with Illinois Drug Free Workplace Act shall subject the individual to the penalties set forth in Section 6, 7 and 8 of the Drug Free Workplace Act.

Address _____

Print Name

Subscribed and sworn to before me

Notary Public _____

SECTION 00 4100

BID FORM

**INDIVIDUAL'S CERTIFICATE OF COMPLIANCE WITH
ILLINOIS DRUG-FREE WORKPLACE ACT**

Pursuant to 30 ILCS 580/1 *et. seq.* (the "Drug Free Workplace Act") the undersigned individual hereby certifies to the Board of Education of Midland Community Unit School District #7 that the individual will not engage in the unlawful manufacture, distribution, dispensation, possession, or use of a controlled substance in the performance of the contract.

Failure to abide by this Individual's Certificate of Compliance with Illinois Drug Free Workplace Act shall subject the individual to the penalties set forth in Section 6, 7 and 8 of the Drug Free Workplace Act.

NOTICE: This Individual's Certificate of Compliance with Illinois Drug Free Workplace Act is only to be completed by an *individual* directly responsible for the performance of a contract of \$5,000 or more with the School District.

Firm Name: _____

By: _____
(Signature of Individual)

(Print Name)

Subscribed and sworn to before me

This _____ day of _____, 2016

Notary Public

END OF BID FORM

CBJ Project No. 16-009

00 4100 - 12

BID FORM

Midland Elementary School Bid

Bid Phase #1

SECTION 00 5000
CONTRACTING FORMS AND SUPPLEMENTS

PART 1 GENERAL

1.01 AGREEMENT AND CONDITIONS OF THE CONTRACT

1.02 FORMS

- A. Use the following forms for the specified purposes unless otherwise indicated elsewhere in the Contract Documents.

PART 2 PRODUCTS - NOT USED

PART 3 EXECUTION - NOT USED

END OF SECTION

**SECTION 00 5200
AGREEMENT FORM**

PART 1 GENERAL

1.01 FORM OF AGREEMENT

1.02 THE AGREEMENT TO BE EXECUTED IS ATTACHED FOLLOWING THIS PAGE.

1.03 RELATED REQUIREMENTS

- A. Section 00 7200 - General Conditions.
- B. Section 00 7300 - Supplementary Conditions.
- C. Section 01 4216 - Definitions.

PART 2 PRODUCTS (NOT USED)

PART 3 EXECUTION (NOT USED)

END OF AGREEMENT FORM

AIA® Document A132™ – 2009

Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition

AGREEMENT made as of the day of in the year
(In words, indicate day, month and year.)

BETWEEN the Owner:
(Name, legal status, address and other information)

Midland Community Unit School District No. 7
1830 State Route 17
Varna, IL 61375

and the Contractor:
(Name, legal status, address and other information)

for the following Project:
(Name, location and detailed description)

Midland CUSD #7 New Elementary School
Lacon, IL
1.

The Construction Manager:
(Name, legal status, address and other information)

Midwest Construction Professionals
520 E. Highland
Morton, IL 61550

The Architect:
(Name, legal status, address and other information)

CBJ Architects, Professional Corporation

3521 Wintergreen
Algonquin, IL 60102
Telephone Number: 847-997-9838
Fax Number: 847-658-0095

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Documents A232™–2009, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition; B132™–2009, Standard Form of Agreement Between Owner and Architect, Construction Manager as Adviser Edition; and C132™–2009, Standard Form of Agreement Between Owner and Construction Manager as Adviser.

AIA Document A232™–2009 is adopted in this document by reference. Do not use with other general conditions unless this document is modified.

Init.

AIA Document A132™ – 2009 (formerly A101™ CMA – 1992). Copyright © 1975, 1980, 1992 and 2009 by The American Institute of Architects. **All rights reserved.** WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 12:48:06 on 08/24/2016 under Order No. 7834146880 which expires on 03/24/2017, and is not for resale.

User Notes:

(3B9ADA2E)

The Owner and Contractor agree as follows.



Init.

/

AIA Document A132™ – 2009 (formerly A101™ CMA – 1992). Copyright © 1975, 1980, 1992 and 2009 by The American Institute of Architects. **All rights reserved.** WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 12:48:06 on 08/24/2016 under Order No. 7834146880 which expires on 03/24/2017, and is not for resale.

User Notes:

(3B9ADA2E)

TABLE OF ARTICLES

- 1 THE CONTRACT DOCUMENTS
- 2 THE WORK OF THIS CONTRACT
- 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION
- 4 CONTRACT SUM
- 5 PAYMENTS
- 6 DISPUTE RESOLUTION
- 7 TERMINATION OR SUSPENSION
- 8 MISCELLANEOUS PROVISIONS
- 9 ENUMERATION OF CONTRACT DOCUMENTS
- 10 INSURANCE AND BONDS

EXHIBIT A DETERMINATION OF THE COST OF THE WORK

ARTICLE 1 THE CONTRACT DOCUMENTS

The Contract Documents consist of this Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of this Agreement, other documents listed in this Agreement and Modifications issued after execution of this Agreement, all of which form the Contract, and are as fully a part of the Contract as if attached to this Agreement or repeated herein. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations or agreements, either written or oral. An enumeration of the Contract Documents, other than Modifications, appears in Article 9.

ARTICLE 2 THE WORK OF THIS CONTRACT

The Contractor shall fully execute the Work described in the Contract Documents, except as specifically indicated in the Contract Documents to be the responsibility of others.

ARTICLE 3 DATE OF COMMENCEMENT AND SUBSTANTIAL COMPLETION

§ 3.1 The date of commencement of the Work shall be the date of this Agreement unless a different date is stated below or provision is made for the date to be fixed in a notice to proceed issued by the Owner.

(Insert the date of commencement, if it differs from the date of this Agreement or, if applicable, state that the date will be fixed in a notice to proceed.)

If, prior to the commencement of the Work, the Owner requires time to file mortgages, mechanics' liens and other security interests, the Owner's time requirement shall be as follows:

§ 3.2 The Contract Time shall be measured from the date of commencement.

§ 3.3 The Contractor shall achieve Substantial Completion of the entire Work not later than () days from the date of commencement, or as follows:

Init.

(Insert number of calendar days. Alternatively, a calendar date may be used when coordinated with the date of commencement. If appropriate, insert requirements for earlier Substantial Completion of certain portions of the Work.)

Portion of the Work

Substantial Completion Date

, subject to adjustments of this Contract Time as provided in the Contract Documents.

(Insert provisions, if any, for liquidated damages relating to failure to achieve Substantial Completion on time or for bonus payments for early completion of the Work.)

ARTICLE 4 CONTRACT SUM

§ 4.1 The Owner shall pay the Contractor the Contract Sum in current funds for the Contractor's performance of the Contract. The Contract Sum shall be one of the following:

(Check the appropriate box.)

- ☐ Stipulated Sum, in accordance with Section 4.2 below
- ☐ Cost of the Work plus the Contractor's Fee without a Guaranteed Maximum Price, in accordance with Section 4.3 below
- ☐ Cost of the Work plus the Contractor's Fee with a Guaranteed Maximum Price, in accordance with Section 4.4 below

(Based on the selection above, complete Section 4.2, 4.3 or 4.4 below. Based on the selection above, also complete either Section 5.1.4, 5.1.5 or 5.1.6 below.)

§ 4.2 Stipulated Sum

§ 4.2.1 The Stipulated Sum shall be (\$), subject to additions and deletions as provided in the Contract Documents.

§ 4.2.2 The Stipulated Sum is based on the following alternates, if any, which are described in the Contract Documents and are hereby accepted by the Owner:

(State the numbers or other identification of accepted alternates. If the bidding or proposal documents permit the Owner to accept other alternates subsequent to the execution of this Agreement, attach a schedule of such other alternates showing the amount for each and the date when that amount expires.)

§ 4.2.3 Unit prices, if any:

(Identify and state the unit price, and state the quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit (\$0.00)
------	-----------------------	-------------------------

§ 4.2.4 Allowances included in the Stipulated Sum, if any:

(Identify allowance and state exclusions, if any, from the allowance price.)

Item	Allowance
------	-----------

Init.

§ 4.3 Cost of the Work Plus Contractor's Fee without a Guaranteed Maximum Price

§ 4.3.1 The Contract Sum is the Cost of the Work as defined in Exhibit A, Determination of the Cost of the Work, plus the Contractor's Fee.

§ 4.3.2 The Contractor's Fee:

(State a lump sum, percentage of Cost of the Work or other provision for determining the Contractor's Fee.)

§ 4.3.3 The method of adjustment of the Contractor's Fee for changes in the Work:

§ 4.3.4 Limitations, if any, on a Subcontractor's overhead and profit for increases in the cost of its portion of the Work:

§ 4.3.5 Rental rates for Contractor-owned equipment shall not exceed percent (%) of the standard rate paid at the place of the Project.

§ 4.3.6 Unit prices, if any:

(Identify and state the unit price; state quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit (\$0.00)
------	-----------------------	-------------------------

§ 4.3.7 The Contractor shall prepare and submit to the Construction Manager for the Owner, in writing, a Control Estimate within 14 days of executing this Agreement. The Control Estimate shall include the items in Section A.1 of Exhibit A, Determination of the Cost of the Work.

§ 4.4 Cost of the Work Plus Contractor's Fee with a Guaranteed Maximum Price

§ 4.4.1 The Contract Sum is the Cost of the Work as defined in Exhibit A, Determination of the Cost of the Work, plus the Contractor's Fee.

§ 4.4.2 The Contractor's Fee:

(State a lump sum, percentage of Cost of the Work or other provision for determining the Contractor's Fee.)

§ 4.4.3 The method of adjustment of the Contractor's Fee for changes in the Work:

§ 4.4.4 Limitations, if any, on a Subcontractor's overhead and profit for increases in the cost of its portion of the Work:

§ 4.4.5 Rental rates for Contractor-owned equipment shall not exceed percent (%) of the standard rate paid at the place of the Project.

§ 4.4.6 Unit Prices, if any:

(Identify and state the unit price, and state the quantity limitations, if any, to which the unit price will be applicable.)

Item	Units and Limitations	Price per Unit (\$0.00)
------	-----------------------	-------------------------

Init.

§ 4.4.7 Guaranteed Maximum Price

§ 4.4.7.1 The sum of the Cost of the Work and the Contractor's Fee is guaranteed by the Contractor not to exceed (\$), subject to additions and deductions by changes in the Work as provided in the Contract Documents. Such maximum sum is referred to in the Contract Documents as the Guaranteed Maximum Price. Costs which would cause the Guaranteed Maximum Price to be exceeded shall be paid by the Contractor without reimbursement by the Owner.

(Insert specific provisions if the Contractor is to participate in any savings.)

§ 4.4.7.2 The Guaranteed Maximum Price is based on the following alternates, if any, which are described in the Contract Documents and are hereby accepted by the Owner:

§ 4.4.7.3 Allowances included in the Guaranteed Maximum Price, if any:

(Identify and state the amounts of any allowances, and state whether they include labor, materials, or both.)

Item	Allowance
------	-----------

§ 4.4.7.4 Assumptions, if any, on which the Guaranteed Maximum Price is based:

ARTICLE 5 PAYMENTS

§ 5.1 Progress Payments

§ 5.1.1 Based upon Applications for Payment submitted to the Construction Manager by the Contractor, and upon certification of the Project Application and Project Certificate for Payment or Application for Payment and Certificate for Payment by the Construction Manager and Architect and issuance by the Architect, the Owner shall make progress payments on account of the Contract Sum to the Contractor as provided below and elsewhere in the Contract Documents.

§ 5.1.2 The period covered by each Application for Payment shall be one calendar month ending on the last day of the month, or as follows:

§ 5.1.3 Provided that an Application for Payment is received by the Construction Manager not later than the day of a month, the Owner shall make payment of the certified amount in the Application for Payment to the Contractor not later than the day of the month. If an Application for Payment is received by the Construction Manager after the application date fixed above, payment shall be made by the Owner not later than () days after the Construction Manager receives the Application for Payment.

(Federal, state or local laws may require payment within a certain period of time.)

§ 5.1.4 Progress Payments Where the Contract Sum is Based on a Stipulated Sum

§ 5.1.4.1 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Contract Sum among the various portions of the Work and be prepared in such form and supported by such data to substantiate its accuracy as the Construction Manager and Architect may require. This schedule, unless objected to by the Construction Manager or Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.4.2 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment.

§ 5.1.4.3 Subject to the provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

- .1 Take that portion of the Contract Sum properly allocable to completed Work as determined by multiplying the percentage completion of each portion of the Work by the share of the total Contract Sum allocated to that portion of the Work in the schedule of values, less retainage of percent (%). Pending final determination of cost to the Owner of changes in the Work, amounts not in dispute may be included as provided in Section 7.3.9 of the General Conditions;
- .2 Add that portion of the Contract Sum properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the completed construction (or, if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing), less retainage of percent (%);
- .3 Subtract the aggregate of previous payments made by the Owner; and
- .4 Subtract amounts, if any, for which the Construction Manager or Architect has withheld or nullified a Certificate for Payment as provided in Section 9.5 of the General Conditions.

§ 5.1.4.4 The progress payment amount determined in accordance with Section 5.1.4.3 shall be further modified under the following circumstances:

- .1 Add, upon Substantial Completion of the Work, a sum sufficient to increase the total payments to percent (%) of the Contract Sum, less such amounts as the Construction Manager recommends and the Architect determines for incomplete Work and unsettled claims; and
- .2 Add, if final completion of the Work is thereafter materially delayed through no fault of the Contractor, any additional amounts payable in accordance with Section 9.10.3 of the General Conditions.

§ 5.1.4.5 Reduction or limitation of retainage, if any, shall be as follows:

(If it is intended, prior to Substantial Completion of the entire Work, to reduce or limit the retainage resulting from the percentages inserted in Sections 5.1.4.3.1 and 5.1.4.3.2 above, and this is not explained elsewhere in the Contract Documents, insert here provisions for such reduction or limitation.)

§ 5.1.5 Progress Payments Where the Contract Sum is Based on the Cost of the Work without a Guaranteed Maximum Price

§ 5.1.5.1 With each Application for Payment, the Contractor shall submit the cost control information required in Exhibit A, Determination of the Cost of the Work, along with payrolls, petty cash accounts, receipted invoices or invoices with check vouchers attached and any other evidence required by the Owner, Construction Manager or Architect to demonstrate that cash disbursements already made by the Contractor on account of the Cost of the Work equal or exceed (1) progress payments already received by the Contractor; less (2) that portion of those payments attributable to the Contractor's Fee; plus (3) payrolls for the period covered by the present Application for Payment.

§ 5.1.5.2 Applications for Payment shall show the Cost of the Work actually incurred by the Contractor through the end of the period covered by the Application for Payment and for which the Contractor has made or intends to make actual payment prior to the next Application for Payment.

§ 5.1.5.3 Subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

- .1 Take the Cost of the Work as described in Exhibit A, Determination of the Cost of the Work;
- .2 Add the Contractor's Fee, less retainage of percent (%). The Contractor's Fee shall be computed upon the Cost of the Work described in that Section at the rate stated in that Section; or if the Contractor's Fee is stated as a fixed sum, an amount which bears the same ratio to that fixed-sum Fee as the Cost of the Work bears to a reasonable estimate of the probable Cost of the Work upon its completion;
- .3 Subtract retainage of percent (%) from that portion of the Work that the Contractor self-performs;
- .4 Subtract the aggregate of previous payments made by the Owner;
- .5 Subtract the shortfall, if any, indicated by the Contractor in the documentation required by Article 5 or resulting from errors subsequently discovered by the Owner's auditors in such documentation; and

- .6 Subtract amounts, if any, for which the Construction Manager or Architect has withheld or withdrawn a Certificate for Payment as provided in Section 9.5 of AIA Document A232™–2009, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition.

§ 5.1.5.4 The Owner, Construction Manager and Contractor shall agree upon (1) a mutually acceptable procedure for review and approval of payments to Subcontractors and (2) the percentage of retainage held on Subcontracts, and the Contractor shall execute subcontracts in accordance with those agreements.

§ 5.1.5.5 In taking action on the Contractor's Applications for Payment, the Construction Manager and Architect shall be entitled to rely on the accuracy and completeness of the information furnished by the Contractor and shall not be deemed to represent that the Construction Manager and Architect have made a detailed examination, audit or arithmetic verification of the documentation submitted in accordance with Article 5 or other supporting data; that the Construction Manager and Architect have made exhaustive or continuous on-site inspections; or that the Construction Manager and Architect have made examinations to ascertain how or for what purposes the Contractor has used amounts previously paid on account of the Contract. Such examinations, audits and verifications, if required by the Owner, will be performed by the Owner's auditors acting in the sole interest of the Owner.

§ 5.1.5.6 Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.

§ 5.1.6 Progress Payments Where the Contract Sum is Based on the Cost of the Work with a Guaranteed Maximum Price

§ 5.1.6.1 With each Application for Payment, the Contractor shall submit payrolls, petty cash accounts, receipted invoices or invoices with check vouchers attached, and any other evidence required by the Owner or Architect to demonstrate that cash disbursements already made by the Contractor on account of the Cost of the Work equal or exceed (1) progress payments already received by the Contractor; less (2) that portion of those payments attributable to the Contractor's Fee; plus (3) payrolls for the period covered by the present Application for Payment.

§ 5.1.6.2 Each Application for Payment shall be based on the most recent schedule of values submitted by the Contractor in accordance with the Contract Documents. The schedule of values shall allocate the entire Contract Sum among the various portions of the Work and be prepared in such form and supported by such data to substantiate its accuracy as the Construction Manager and Architect may require. This schedule, unless objected to by the Construction Manager or Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment.

§ 5.1.6.3 Applications for Payment shall show the percentage of completion of each portion of the Work as of the end of the period covered by the Application for Payment. The percentage of completion shall be the lesser of (1) the percentage of that portion of the Work which has actually been completed; or (2) the percentage obtained by dividing (a) the expense that has actually been incurred by the Contractor on account of that portion of the Work for which the Contractor has made or intends to make actual payment prior to the next Application for Payment by (b) the share of the Guaranteed Maximum Price allocated to that portion of the Work in the schedule of values.

§ 5.1.6.4 Subject to other provisions of the Contract Documents, the amount of each progress payment shall be computed as follows:

- .1 Take that portion of the Guaranteed Maximum Price properly allocable to completed Work as determined by multiplying the percentage of completion of each portion of the Work by the share of the Guaranteed Maximum Price allocated to that portion of the Work in the schedule of values. Pending final determination of cost to the Owner of changes in the Work, amounts not in dispute shall be included as provided in Section 7.3.10 of AIA Document A232–2009;
- .2 Add that portion of the Guaranteed Maximum Price properly allocable to materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work, or if approved in advance by the Owner, suitably stored off the site at a location agreed upon in writing;
- .3 Add the Contractor's Fee, less retainage of percent (%). The Contractor's Fee shall be computed upon the Cost of the Work at the rate stated in Section 4.4.2 or, if the Contractor's Fee is stated as a fixed sum in that Section, shall be an amount that bears the same ratio to that fixed-sum fee as the Cost of the Work bears to a reasonable estimate of the probable Cost of the Work upon its completion;

- .4 Subtract retainage of percent (%) from that portion of the Work that the Contractor self-performs;
- .5 Subtract the aggregate of previous payments made by the Owner;
- .6 Subtract the shortfall, if any, indicated by the Contractor in the documentation required by Section 5.1.6.1 to substantiate prior Applications for Payment, or resulting from errors subsequently discovered by the Owner's auditors in such documentation; and
- .7 Subtract amounts, if any, for which the Construction Manager or Architect have withheld or nullified a Certificate for Payment as provided in Section 9.5 of AIA Document A232–2009.

§ 5.1.6.5 The Owner and the Contractor shall agree upon a (1) mutually acceptable procedure for review and approval of payments to Subcontractors and (2) the percentage of retainage held on Subcontracts, and the Contractor shall execute subcontracts in accordance with those agreements.

§ 5.1.6.6 In taking action on the Contractor's Applications for Payment, the Construction Manager and Architect shall be entitled to rely on the accuracy and completeness of the information furnished by the Contractor and shall not be deemed to represent that the Construction Manager or Architect have made a detailed examination, audit or arithmetic verification of the documentation submitted in accordance with Section 5.1.6.1 or other supporting data; that the Construction Manager or Architect have made exhaustive or continuous on-site inspections; or that the Construction Manager or Architect have made examinations to ascertain how or for what purposes the Contractor has used amounts previously paid on account of the Contract. Such examinations, audits and verifications, if required by the Owner, will be performed by the Owner's auditors acting in the sole interest of the Owner.

§ 5.1.6.7 Except with the Owner's prior approval, the Contractor shall not make advance payments to suppliers for materials or equipment which have not been delivered and stored at the site.

§ 5.2 Final Payment

§ 5.2.1 Final payment, constituting the entire unpaid balance of the Contract Sum, shall be made by the Owner to the Contractor when

- .1 the Contractor has fully performed the Contract except for the Contractor's responsibility to correct Work as provided in Section 12.2 of AIA Document A232–2009, and to satisfy other requirements, if any, which extend beyond final payment;
- .2 the Contractor has submitted a final accounting for the Cost of the Work, pursuant to Exhibit A, Determination of the Cost of the Work when payment is on the basis of the Cost of the Work, with or without a Guaranteed Maximum payment; and
- .3 a final Certificate for Payment or Project Certificate for Payment has been issued by the Architect; such final payment shall be made by the Owner not more than 30 days after the issuance of the final Certificate for Payment or Project Certificate for Payment, or as follows:

ARTICLE 6 DISPUTE RESOLUTION

§ 6.1 Initial Decision Maker

The Architect will serve as Initial Decision Maker pursuant to Section 15.2 of AIA Document A232–2009, unless the parties appoint below another individual, not a party to this Agreement, to serve as Initial Decision Maker.

(If the parties mutually agree, insert the name, address and other contact information of the Initial Decision Maker, if other than the Architect.)

§ 6.2 Binding Dispute Resolution

For any Claim subject to, but not resolved by, mediation pursuant to Section 15.3 of AIA Document A232–2009, the method of binding dispute resolution shall be as follows:

(Check the appropriate box. If the Owner and Contractor do not select a method of binding dispute resolution below, or do not subsequently agree in writing to a binding dispute resolution method other than litigation, Claims will be resolved by litigation in a court of competent jurisdiction.)

- [] Arbitration pursuant to Section 15.4 of AIA Document A232–2009.
- [] Litigation in a court of competent jurisdiction.
- [] Other: *(Specify)*

ARTICLE 7 TERMINATION OR SUSPENSION

§ 7.1 Where the Contract Sum is a Stipulated Sum

§ 7.1.1 The Contract may be terminated by the Owner or the Contractor as provided in Article 14 of AIA Document A232–2009.

§ 7.1.2 The Work may be suspended by the Owner as provided in Article 14 of AIA Document A232–2009.

§ 7.2 Where the Contract Sum is Based on the Cost of the Work with or without a Guaranteed Maximum Price

§ 7.2.1 Subject to the provisions of Section 7.2.2 below, the Contract may be terminated by the Owner or the Contractor as provided in Article 14 of AIA Document A232–2009.

§ 7.2.2 The Contract may be terminated by the Owner for cause as provided in Article 14 of AIA Document A232–2009; however, the Owner shall then only pay the Contractor an amount calculated as follows:

- .1 Take the Cost of the Work incurred by the Contractor to the date of termination;
- .2 Add the Contractor's Fee computed upon the Cost of the Work to the date of termination at the rate stated in Sections 4.3.2 or 4.4.2, as applicable, or, if the Contractor's Fee is stated as a fixed sum, an amount that bears the same ratio to that fixed-sum Fee as the Cost of the Work at the time of termination bears to a reasonable estimate of the probable Cost of the Work upon its completion; and
- .3 Subtract the aggregate of previous payments made by the Owner.

§ 7.2.3 If the Owner terminates the Contract for cause when the Contract Sum is based on the Cost of the Work with a Guaranteed Maximum Price, and as provided in Article 14 of AIA Document A232–2009, the amount, if any, to be paid to the Contractor under Section 14.2.4 of AIA Document A232–2009 shall not cause the Guaranteed Maximum Price to be exceeded, nor shall it exceed the amount calculated in Section 7.2.2.

§ 7.2.4 The Owner shall also pay the Contractor fair compensation, either by purchase or rental at the election of the Owner, for any equipment owned by the Contractor that the Owner elects to retain and that is not otherwise included in the Cost of the Work under Section 7.2.1. To the extent that the Owner elects to take legal assignment of subcontracts and purchase orders (including rental agreements), the Contractor shall, as a condition of receiving the payments referred to in this Article 7, execute and deliver all such papers and take all such steps, including the legal assignment of such subcontracts and other contractual rights of the Contractor, as the Owner may require for the purpose of fully vesting in the Owner the rights and benefits of the Contractor under such subcontracts or purchase orders.

§ 7.2.5 The Work may be suspended by the Owner as provided in Article 14 of AIA Document A232–2009; in such case, the Contract Sum and Contract Time shall be increased as provided in Section 14.3.2 of AIA Document A232–2009, except that the term 'profit' shall be understood to mean the Contractor's Fee as described in Sections 4.3.2 and 4.4.2 of this Agreement.

ARTICLE 8 MISCELLANEOUS PROVISIONS

§ 8.1 Where reference is made in this Agreement to a provision of AIA Document A232–2009 or another Contract Document, the reference refers to that provision as amended or supplemented by other provisions of the Contract Documents.

§ 8.2 Payments due and unpaid under the Contract shall bear interest from the date payment is due at the rate stated below, or in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

(Insert rate of interest agreed upon, if any.)

Init.

%

§ 8.3 The Owner's representative:
(Name, address and other information)

§ 8.4 The Contractor's representative:
(Name, address and other information)

§ 8.5 Neither the Owner's nor the Contractor's representative shall be changed without ten days written notice to the other party.

§ 8.6 Other provisions:

ARTICLE 9 ENUMERATION OF CONTRACT DOCUMENTS

§ 9.1 The Contract Documents, except for Modifications issued after execution of this Agreement, are enumerated in the sections below.

§ 9.1.1 The Agreement is this executed AIA Document A132–2009, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition.

§ 9.1.2 The General Conditions are AIA Document A232–2009, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition.

§ 9.1.3 The Supplementary and other Conditions of the Contract:

Document	Title	Date	Pages
----------	-------	------	-------

§ 9.1.4 The Specifications:
(Either list the Specifications here or refer to an exhibit attached to this Agreement.)

Section	Title	Date	Pages
---------	-------	------	-------

§ 9.1.5 The Drawings:
(Either list the Drawings here or refer to an exhibit attached to this Agreement.)

Init.

Number

Title

Date

§ 9.1.6 The Addenda, if any:

Number

Date

Pages

Portions of Addenda relating to bidding requirements are not part of the Contract Documents unless the bidding requirements are also enumerated in this Article 9.

§ 9.1.7 Additional documents, if any, forming part of the Contract Documents are:

.1 AIA Document A132™–2009, Exhibit A, Determination of the Cost of the Work, if applicable.

.2 AIA Document E201™–2007, Digital Data Protocol Exhibit, if completed, or the following:

.3 AIA Document E202™–2008, Building Information Modeling Protocol Exhibit, if completed, or the following:

.4 Other documents, if any, listed below:

(List here any additional documents which are intended to form part of the Contract Documents. AIA Document A232–2009 provides that bidding requirements such as advertisement or invitation to bid, Instructions to Bidders, sample forms and the Contractor's bid are not part of the Contract Documents unless enumerated in this Agreement. They should be listed here only if intended to be part of the Contract Documents.)

ARTICLE 10 INSURANCE AND BONDS

The Contractor shall purchase and maintain insurance and provide bonds as set forth in Article 11 of AIA Document A232–2009.

(State bonding requirements, if any, and limits of liability for insurance required in Article 11 of AIA Document A232–2009.)

Type of Insurance or Bond

Limit of Liability or Bond Amount (\$0.00)

This Agreement is entered into as of the day and year first written above.

OWNER (Signature)

CONTRACTOR (Signature)

(Printed name and title)

(Printed name and title)

Init.

AIA Document A132™ – 2009 (formerly A101™ CMA – 1992). Copyright © 1975, 1980, 1992 and 2009 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 12:48:06 on 08/24/2016 under Order No. 7834146880 which expires on 03/24/2017, and is not for resale.

User Notes:

(3B9ADA2E)

Additions and Deletions Report for

AIA® Document A132™ – 2009

This Additions and Deletions Report, as defined on page 1 of the associated document, reproduces below all text the author has added to the standard form AIA document in order to complete it, as well as any text the author may have added to or deleted from the original AIA text. Added text is shown underlined. Deleted text is indicated with a horizontal line through the original AIA text.

Note: This Additions and Deletions Report is provided for information purposes only and is not incorporated into or constitute any part of the associated AIA document. This Additions and Deletions Report and its associated document were generated simultaneously by AIA software at 12:48:06 on 08/24/2016.

PAGE 1

Midland Community Unit School District No. 7
1830 State Route 17
Varna, IL 61375

...

Midland CUSD #7 New Elementary School
Lacon, IL
I.

...

Midwest Construction Professionals
520 E. Highland
Morton, IL 61550

...

CBJ Architects, Professional Corporation
3521 Wintergreen
Algonquin, IL 60102
Telephone Number: 847-997-9838
Fax Number: 847-658-0095

Certification of Document's Authenticity

AIA® Document D401™ – 2003

I, , hereby certify, to the best of my knowledge, information and belief, that I created the attached final document simultaneously with its associated Additions and Deletions Report and this certification at 12:48:06 on 08/24/2016 under Order No. 7834146880 from AIA Contract Documents software and that in preparing the attached final document I made no changes to the original text of AIA® Document A132™ - 2009, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition, as published by the AIA in its software, other than those additions and deletions shown in the associated Additions and Deletions Report.

(Signed)

(Title)

(Dated)

**SECTION 00 7200
GENERAL CONDITIONS**

FORM OF GENERAL CONDITIONS

1.01 THE GENERAL CONDITIONS APPLICABLE TO THIS CONTRACT IS ATTACHED FOLLOWING THIS PAGE.

RELATED REQUIREMENTS

2.01 SECTION 00 7300 - SUPPLEMENTARY CONDITIONS.

2.02 SECTION 01 4216 - DEFINITIONS.

END OF SECTION

AIA® Document A232™ – 2009

General Conditions of the Contract for Construction, Construction Manager as Adviser Edition

for the following PROJECT:

(Name, and location or address)

Midland CUSD #7 New Elementary School
Lacon, IL

THE CONSTRUCTION MANAGER:

(Name, legal status and address)

Midwest Construction Professionals
520 E. Highland
Morton, IL 61550

THE OWNER:

(Name, legal status and address)

Midland Community Unit School District No. 7
1830 State Route 17
Varna, IL 61375

THE ARCHITECT:

(Name, legal status and address)

CBJ Architects, Professional Corporation
3521 Wintergreen
Algonquin, IL 60102

TABLE OF ARTICLES

- 1 GENERAL PROVISIONS**
- 2 OWNER**
- 3 CONTRACTOR**
- 4 ARCHITECT AND CONSTRUCTION MANAGER**
- 5 SUBCONTRACTORS**
- 6 CONSTRUCTION BY OWNER OR BY OTHER CONTRACTORS**
- 7 CHANGES IN THE WORK**
- 8 TIME**

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

This document is intended to be used in conjunction with AIA Documents A132™–2009, Standard Form of Agreement Between Owner and Contractor, Construction Manager as Adviser Edition; B132™–2009, Standard Form of Agreement Between Owner and Architect, Construction Manager as Adviser Edition; and C132™–2009, Standard Form of Agreement Between Owner and Construction Manager as Adviser.

Init.

AIA Document A232™ – 2009 (rev. 12/11) (formerly A201™ CMA – 1992). Copyright © 1992 and 2009 by The American Institute of Architects. **All rights reserved.** WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 12:24:07 on 08/24/2016 under Order No. 7834146880 which expires on 03/24/2017, and is not for resale.

User Notes:

(3B9ADA2A)

9 PAYMENTS AND COMPLETION

10 PROTECTION OF PERSONS AND PROPERTY

11 INSURANCE AND BONDS

12 UNCOVERING AND CORRECTION OF WORK

13 MISCELLANEOUS PROVISIONS

14 TERMINATION OR SUSPENSION OF THE CONTRACT

15 CLAIMS AND DISPUTES

Init.

/

AIA Document A232™ – 2009 (rev. 12/11) (formerly A201™ CMA – 1992). Copyright © 1992 and 2009 by The American Institute of Architects. All rights reserved. WARNING: This AIA® Document is protected by U.S. Copyright Law and International Treaties. Unauthorized reproduction or distribution of this AIA® Document, or any portion of it, may result in severe civil and criminal penalties, and will be prosecuted to the maximum extent possible under the law. This document was produced by AIA software at 12:24:07 on 08/24/2016 under Order No. 7834146880 which expires on 03/24/2017, and is not for resale.

User Notes:

(3B9ADA2A)

INDEX

(Topics and numbers in bold are section headings.)

- Acceptance of Nonconforming Work
 - 9.6.6, 9.9.3, 12.3
- Acceptance of Work
 - 9.6.6, 9.8.2, 9.9.3, 9.10.1, 9.10.3, 12.3
- Access to Work
 - 3.16, 6.2.1, 12.1
- Accident Prevention
 - 10
- Acts and Omissions
 - 3.2.1, 3.2.2, 3.3.2, 3.12.8, 3.18, 8.3.1, 9.5.1, 10.1, 10.2.5, 13.4.2, 13.7
- Addenda
 - 1.1.1, 3.11, 4.2.14
- Additional Costs, Claims for
 - 3.2.4, 3.7.4, 3.7.5, 6.1.1, 7.3, 9.10.3, 9.10.4, 10.3, 10.4, 15.1.4
- Additional Inspections and Testing
 - 4.2.8, 12.2.1, 13.5
- Additional Insured
 - 11.1.4
- Additional Time, Claims for
 - 3.7.4, 3.7.5, 6.1.1, 7.3, 8.3, 10.3
- Administration of the Contract
 - 3.10, 4.2
- Advertisement or Invitation to Bid
 - 1.1.1
- Aesthetic Effect
 - 4.2.19
- Allowances
 - 3.8, 7.3.8
- All-risk Insurance
 - 11.3.1, 11.3.1.1
- Applications for Payment
 - 4.2.7, 4.2.15, 7.3.9, 9.2, 9.3, 9.4, 9.5.1, 9.7, 9.8.3, 9.10.1, 9.10.3, 9.10.5, 11.1.3, 14.2.4
- Approvals
 - 2.1.1, 2.2.2, 2.4, 3.1.4, 3.10.1, 3.10.2, 3.12.4 through 3.12.10, 3.13.2, 3.15.2, 4.2.9, 9.3.2, 13.4.2, 13.5
- Arbitration
 - 8.3.1, 11.3.10, 13.1, 15.3.2, 15.4
- ARCHITECT
 - 4
- Architect, Certificates for Payment
 - 9.4
- Architect, Definition of
 - 4.1.1
- Architect, Extent of Authority
 - 5.2, 7.1.2, 7.3.7, 7.4, 9.3.1, 9.4, 9.5, 9.8.3, 9.8.4, 9.10.1, 9.10.3, 12.1, 12.2.1, 13.5.1, 13.5.2, 15.1.3, 15.2.1
- Architect, Limitations of Authority and Responsibility
 - 2.1.1, 3.12.8, 4.2.1, 4.2.2, 4.2.8, 4.2.13, 5.2.1, 9.6.4, 15.2
- Architect's Additional Services and Expenses
 - 2.4, 11.3.1.1, 12.2.1, 12.2.4, 13.5.2
- Architect's Administration of the Contract
 - 4.2, 9.4, 9.5, 15.2
- Architect's Approvals
 - 3.12.8
- Architect's Authority to Reject Work
 - 4.2.8, 12.1.2, 12.2.1
- Architect's Copyright
 - 1.5
- Architect's Decisions
 - 4.2.8, 7.3.9, 7.4, 8.1.3, 8.3.1, 9.2, 9.4, 9.5, 9.8.3, 9.9.2, 13.5.2, 14.2.2, 14.2.4, 15.2
- Architect's Inspections
 - 3.7.4, 4.2, 9.8.3, 9.9.2, 9.10.1, 13.5
- Architect's Instructions
 - 3.2.4, 7.4, 9.4
- Architect's Interpretations
 - 4.2.8, 4.2.17, 4.2.18
- Architect's On-Site Observations
 - 4.2.2, 9.4, 9.5.1, 9.10.1, 12.1.1, 12.1.2, 13.5
- Architect's Project Representative
 - 4.2.16
- Architect's Relationship with Contractor
 - 1.1.2, 1.5, 3.2.2, 3.2.3, 3.2.4, 3.3.1, 3.4.2, 3.5, 3.7.4, 3.9.2, 3.9.3, 3.10, 3.11, 3.12.8, 3.16, 3.18, 4.2, 5.2, 6.2.2, 8.2, 11.3.7, 12.1, 13.5
- Architect's Relationship with Construction Manager
 - 1.1.2, 9.3 through 9.10, 10.3, 13.5.1, 10.3, 11.3.7, 13.4.2, 13.5.4
- Architect's Relationship with Subcontractors
 - 1.1.2, 4.2.8, 5.3, 9.6.3, 9.6.4
- Architect's Representations
 - 9.4, 9.5, 9.10.1
- Architect's Site Visits
 - 4.2.2, 9.4, 9.5.1, 9.8.3, 9.9.2, 9.10.1, 13.5
- Asbestos
 - 10.3.1
- Attorneys' Fees
 - 3.18.1, 9.10.2, 10.3.3
- Award of Other Contracts
 - 6.1.1, 6.1.2
- Award of Subcontracts and Other Contracts for Portions of the Work
 - 5.2
- Basic Definitions
 - 1.1
- Bidding Requirements
 - 1.1.1, 5.2.1, 11.4.1
- Binding Dispute Resolution

9.7, 11.3.9, 11.3.10, 13.1, 15.2.5, 15.2.6.1, 15.3.1, 15.3.2, 15.4.1
 Boiler and Machinery Insurance
 11.3.2
 BONDS, INSURANCE AND
 11
 Bonds, Lien
 7.3.7.4, 9.10.3
 Bonds, Performance and Payment
 7.3.7.4, 9.6.7, 9.10.3, 11.3.9, 11.4
 Building Permit
 2.2.2, 3.7.1
 Capitalization
 1.3
 Certificate of Substantial Completion
 9.8.3, 9.8.4, 9.8.5
 Certificates for Payment
 4.2.2, 9.3.3, 9.4, 9.5, 9.6.1, 9.6.6, 9.7, 9.10.1, 9.10.3, 15.1.3
 Certificates of Inspection, Testing or Approval
 13.5.4
 Certificates of Insurance
 9.3.2, 9.10.2, 11.1.3
 Change Orders
 1.1.1, 2.4, 3.4.2, 3.7.4, 3.8.2, 3.11, 3.12.8, 4.2.12, 4.2.13, 4.2.14, 5.2.3, 7.1.1, 7.1.2, 7.2, 7.3.2, 7.3.4, 7.3.6, 7.3.9, 7.3.10, 8.3.1, 9.3.1.1, 9.10.3, 10.3.2, 11.3.1.2, 11.3.4, 11.3.9, 12.1.2, 15.1.3
 Change Orders, Definition of
 7.2
 Changes
 7.1
 CHANGES IN THE WORK
 2.2.1, 3.4.2, 3.11, 3.12.8, 4.2.13, 4.2.14, 7, 8.3.1, 9.3.1.1
 Claims, Definition of
 15.1.1
 CLAIMS AND DISPUTES
 1.1.8, 3.2.4, 3.7.5, 6.1.1, 7.3.9, 8.3.2, 9.3.3, 9.10.3, 9.10.4, 10.3.3, 15, 15.4
 Claims for Additional Cost
 3.2.4, 3.7.5, 6.1.1, 7.3.9, 9.10.3, 9.10.4, 10.3.2, 10.4, 15.1.4
 Claims for Additional Time
 3.2.4, 3.7.5, 7, 8.3.2, 10.4, 15.1.5
 Concealed or Unknown Conditions, Claims for
 3.7
 Claims for Damages
 3.2.4, 3.18, 6.1.1, 6.2.5, 8.3.2, 9.3.3, 9.5.1.2, 9.10.2, 9.10.5, 10.3.3, 11.1.1, 11.3.5, 11.3.7, 15.1.6
 Cleaning Up
 3.15, 6.3
 Commencement of Statutory Limitation Period
 13.7
 Commencement of the Work, Definition of
 8.1.2
 Communications, Owner to Architect

2.2.6
 Communications, Owner to Construction Manager
 2.2.6
 Communications, Owner to Contractor
 2.2.6
 Communications Facilitating Contract
 Administration
 3.9.1, 4.2.6
 COMPLETION, PAYMENTS AND
 9
 Completion, Substantial
 4.2.15, 8.1.1, 8.1.3, 8.2.3, 9.4.3.3, 9.8, 9.9.1, 9.10.3, 12.2.1, 12.2.2, 13.7
 Concealed or Unknown Conditions
 3.7.4, 4.2.8, 8.3.1, 10.3
 Conditions of the Contract
 1.1.1
 Consolidation or Joinder
 15.4.4
 CONSTRUCTION BY OWNER OR BY OTHER
 CONTRACTORS
 1.1.4, 6
 Construction Change Directive, Definition of
 7.3.1
 Construction Change Directives
 1.1.1, 3.4.2, 3.12.8, 4.2.12, 4.2.13, 7.1.1, 7.1.2, 7.1.3, 7.3, 9.3.1.1
 Construction Manager, Building Permits
 2.2.2
 Construction Manager, Communications through
 4.2.6
 Construction Manager, Construction Schedule
 3.10.1, 3.10.3
 CONSTRUCTION MANAGER
 4
 Construction Manager, Definition of
 4.1.2
 Construction Manager, Documents and Samples at
 the Site
 3.11
 Construction Manager, Extent of Authority
 3.12.7, 3.12.8, 4.1.3, 4.2.1, 4.2.4, 4.2.5, 4.2.9, 7.1.2, 7.2, 7.3.1, 8.3, 9.3.1, 9.4.1, 9.4.2, 9.4.3, 9.8.2, 9.8.3, 9.8.4, 9.9.1, 12.1, 12.2.1, 14.2.2, 14.2.4
 Construction Manager, Limitations of Authority and
 Responsibility
 4.2.5, 4.2.8, 13.4.2
 Construction Manager, Submittals
 4.2.9
 Construction Manager's Additional Services and
 Expenses
 12.2.1
 Construction Manager's Administration of the
 Contract
 4.2, 9.4, 9.5
 Construction Manager's Approval
 2.4, 3.10.1, 3.10.2

Construction Manager's Authority to Reject Work
4.2.8, 12.2.1

Construction Manager's Decisions
7.3.7, 7.3.9, 9.4.1, 9.5.1

Construction Manager's Inspections
4.2.8, 9.8.3, 9.9.2

Construction Manager's On-Site Observations
9.5.1

Construction Manager's Relationship with Architect
1.1.2, 4.2.1, 4.2.7, 4.2.8, 4.2.9, 4.2.13, 4.2.15, 4.2.16,
4.2.20, 9.2.1, 9.4.2, 9.5, 9.6.1, 9.6.3, 9.8.2, 9.8.3,
9.8.4, 9.9.1, 9.10.1, 9.10.2, 9.10.3, 11.1.3, 12.2.4,
13.5.1, 13.5.2, 13.5.4, 14.2.2, 14.2.4

Construction Manager's Relationship with Contractor
3.2.2, 3.2.3, 3.3.1, 3.5, 3.10.1, 3.10.2, 3.10.3, 3.11,
3.12.5, 3.12.6, 3.12.7, 3.12.8, 3.12.9, 3.12.10, 3.13.2,
3.14.2, 3.15.2, 3.16, 3.17, 3.18.1, 4.2.4, 4.2.5, 4.2.6,
4.2.9, 4.2.14, 4.2.17, 4.2.20, 5.2, 6.2.1, 6.2.2, 7.1.2,
7.2, 7.3.5, 7.3.7, 7.3.10, 8.3.1, 9.2, 9.3.1, 9.4.1, 9.4.2,
9.7, 9.8.2, 9.8.3, 9.8.4, 9.9.1, 9.10.1, 9.10.2, 9.10.3,
10.1, 10.3, 11.3.7, 12.1, 13.5.1, 13.5.2, 13.5.3, 13.5.4

Construction Manager's Relationship with Owner
2.2.2, 4.2.1, 10.3.2

Construction Manager's Relationship with Other
Contractors and Owner's Own Forces
4.2.4

Construction Manager's Relationship with
Subcontractors
4.2.8, 5.3, 9.6.3, 9.6.4

Construction Manager's Site Visits
9.5.1

Construction Schedules, Contractor's
3.10, 3.12.1, 3.12.2, 6.1.2, 15.1.5.2

Contingent Assignment of Subcontracts
5.4, 14.2.2.2

Continuing Contract Performance
15.1.3

Contract, Definition of
1.1.2

CONTRACT, TERMINATION OR SUSPENSION
OF THE
5.4.1.1, 11.3.9, 14

Contract Administration
3.1.3, 4.2, 9.4, 9.5

Contract Award and Execution, Conditions Relating
to
3.7.1, 3.10, 5.2, 6.1, 11.1.3, 11.3.6, 11.4.1

Contract Documents, Copies Furnished and Use of
1.5.2, 2.2.5, 5.3

Contract Documents, Definition of
1.1.1

Contract Performance During Arbitration
15.1.3

Contract Sum
3.7.4, 3.7.5, 3.8, 3.10.2, 5.2.3, 7.2, 7.3, 7.4, 9.1, 9.2,
9.5.1.4, 9.6.7, 9.7, 10.3.2, 11.3.1.1, 12.3, 14.2.4,
14.3.2, 15.1.4, 15.2.5

Contract Time
3.7.4, 3.7.5, 4, 3.10.2, 5.2.3, 7.2.3, 7.3.1, 7.3.5,
7.3.10, 7.4, 8.1.1, 8.2.1, 8.2.3, 8.3.1, 9.5.1, 9.7,
10.3.2, 12.1.1, 14.3.2, 15.1.5.1, 15.2.5

Contract Time, Definition of
8.1.1

CONTRACTOR
3

Contractor, Definition of
3.1.1

Contractor's Construction Schedules
3.10, 3.12.1, 3.12.2, 6.1.3, 15.1.5.2

Contractor's Employees
3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.2, 4.2.3, 4.2.6, 10.2, 10.3,
11.1.1, 11.3.7, 14.1, 14.2.1.1

Contractor's Liability Insurance
11.1

Contractor's Relationship with Other Contractors and
Owner's Own Forces
3.12.5, 3.14.2, 4.2.6, 6, 11.3, 12.1.2, 12.2.4

Contractor's Relationship with Subcontractors
1.2.2, 3.3.2, 3.18, 5, 9.6.2, 9.6.7, 9.10.2, 11.3.1.2,
11.3.7, 11.3.8, 14.2.1.2

Contractor's Relationship with the Architect
1.1.2, 1.5, 3.2.2, 3.2.3, 3.2.4, 3.4.2, 3.5, 3.7.4, 3.10.1,
3.11, 3.12, 3.16, 3.18, 5.2, 6.2.2, 7, 8.3.1, 9.2, 9.3,
9.4, 9.5, 9.7, 9.8, 9.9, 10.2.6, 10.3, 11.3.7, 12, 13.5,
15.1.2, 15.2.1

Contractor's Relationship with the Construction
Manager
1.1.2, 3.2.2, 3.2.3, 3.3.1, 3.5, 3.10.1, 3.10.2, 3.10.3,
3.11, 3.12.5, 3.12.7, 3.12.9, 3.12.10, 3.13.2, 3.14.2,
3.15.1, 3.16, 3.17, 3.18.1, 4.2.4, 4.2.5, 5.2, 6.2.1,
6.2.2, 7.1.2, 7.3.5, 7.3.7, 7.3.10, 8.3.1, 9.2, 9.3.1,
9.4.1, 9.4.2, 9.8.2, 9.9.1, 9.10.1, 9.10.2, 9.10.3, 10.1,
10.2.6, 10.3, 11.3.7, 12.1, 13.5.1, 13.5.2, 13.5.3,
13.5.4

Contractor's Representations
3.2.1, 3.2.2, 3.5, 3.12.6, 6.2.2, 8.2.1, 9.3.3, 9.8.2

Contractor's Responsibility for Those Performing the
Work
3.3.2, 3.18, 5.3, 6.1.3, 6.2, 9.5.1, 10.2.8

Contractor's Review of Contract Documents
3.2

Contractor's Right to Stop the Work
9.7

Contractor's Right to Terminate the Contract
14.1

Contractor's Submittals
3.10.2, 3.11, 3.12, 4.2.9, 9.2, 9.3, 9.8.2, 9.9.1, 9.10.2,
9.10.3, 11.1.3, 11.4.2

Contractor's Superintendent
3.9, 10.2.6

Contractor's Supervision and Construction
Procedures
1.2.2, 3.3, 3.4, 4.2.5, 4.2.7, 6.1, 6.2.4, 7.1.3, 7.3.5,
7.3.7, 8.2, 10, 12, 14, 15.1.3

Contractual Liability Insurance
11.1.1.8, 11.2, 11.3.1.5
Coordination and Correlation
1.2, 3.2, 3.3.1, 3.10, 3.12.6, 6.1.2, 6.2.1
Copies Furnished of Drawings and Specifications
1.5, 2.2.5, 3.11
Copyrights
1.5, 3.17
Correction of Work
2.3, 2.4, 9.4.1, 9.4.2, 9.8.2, 9.8.3, 9.9.1, 12.1.2, 12.2
Correlation and Intent of the Contract Documents
1.2
Costs
2.4, 3.2.4, 3.7.3, 3.8.2, 3.15.2, 5.4.2, 6.1.1, 6.2.3,
7.3.3.3, 7.3.6, 7.3.7, 7.3.8, 7.3.9, 11.3.1.2, 11.3.1.3,
11.3.4, 11.3.9, 12.1, 12.2.1, 13.5, 14
Cutting and Patching
3.14, 6.2.5
Damage to Construction of Owner or Other
Contractors
3.14.2, 6.2.4, 9.5.1.5, 10.2.1.2, 10.2.5, 10.4, 11.1.1,
11.3, 12.2.4
Damage to the Work
3.14.2, 9.9.1, 10.2.1.2, 10.2.5, 10.4, 11.3.1, 12.2.4
Damages, Claims for
3.2.4, 3.18, 6.1.1, 8.3.2, 10.3.3, 11.1.1, 11.3.5, 11.3.7,
14.2.4, 15.1.6
Damages for Delay
6.1.1, 8.3.3, 9.5.1.6, 9.7, 10.3.2, 15.1.5
Date of Commencement of the Work, Definition of
8.1.2
Date of Substantial Completion, Definition of
8.1.3
Day, Definition of
8.1.4
Decisions of the Architect
3.7.4, 4.2.7, 4.2.8, 4.2.10, 4.2.11, 4.2.13, 4.2.15,
4.2.16, 4.2.17, 4.2.18, 4.2.19, 4.2.20, 7.3.9, 8.1.3,
8.3.1, 9.2, 9.4, 9.5, 9.8.3, 9.8.4, 9.9.1, 10.1.2, 13.5.2,
14.2.2, 14.2.4, 15.1, 15.2
Decisions of the Construction Manager
7.3.7, 7.3.8, 7.3.9, 15.1, 15.2
Decisions to Withhold Certification
9.4.1, 9.5, 9.7, 14.1.1.3
Defective or Nonconforming Work, Acceptance,
Rejection and Correction of
2.3, 2.4, 3.5, 4.2.8, 6.2.5, 9.5.1, 9.6.6, 9.8.2, 9.9.3,
9.10.4, 12.2.1, 12.2.2
Definitions
1.1, 2.1.1, 3.1.1, 3.12.1, 3.12.2, 3.12.3, 4.1.1, 4.1.2,
7.2, 7.3.1, 8.1, 9.1, 9.8.1, 15.1.1
Delays and Extensions of Time
3.2, 3.7.4, 5.2.3, 7.2, 7.3.1, 7.4, 8.3, 9.5.1, 9.7, 10.3.2,
10.4, 14.3.2, 15.1.5, 15.2.5
Disputes
7.3.8, 7.3.9, 9.3, 15.1, 15.2
DISPUTES, CLAIMS AND

3.2.4, 6.1.1, 6.3, 7.3.9, 9.3.3, 15, 15.4
Documents and Samples at the Site
3.11
Drawings, Definition of
1.1.5
Drawings and Specifications, Ownership and Use
1.1.1, 1.5, 2.2.5, 3.11, 5.3
Duty to Review Contract Documents and Field
Conditions
3.2
Effective Date of Insurance
8.2.2, 11.1.2
Emergencies
10.4, 14.1.1.2, 15.1.4
Employees, Contractor's
3.3.2, 3.4.3, 3.8.1, 3.9, 3.18.1, 3.18.2, 4.2.3, 4.2.6,
10.2, 10.3.3, 11.1.1, 11.3.7, 14.1, 14.2.1.1
Equipment, Labor, Materials and or
1.1.3, 1.1.6, 3.4, 3.5, 3.8.2, 3.8.3, 3.12.2, 3.12.3,
3.13.1, 3.15.1, 4.2.8, 4.2.7, 5.2.1, 6.2.1, 7.3.7, 9.3.2,
9.3.3, 9.5.1.3, 9.10.2, 10.2.1, 10.2.4, 14.2.2
Execution and Progress of the Work
1.1.3, 1.2.1, 1.2.2, 2.2.3, 2.2.5, 3.1, 3.3.1, 3.4.1, 3.5,
3.7.1, 3.10.1, 3.12, 3.14, 4.2, 6.2.2, 7.1.3, 7.3.5, 8.2,
9.5.1, 9.9.1, 10.2, 10.3, 12.2, 14.2, 14.3.1, 15.1.3
Extensions of Time
3.2.4, 3.7.4, 5.2.3, 7.2.3, 7.4, 8.3, 9.5.1, 9.7, 10.3.2,
10.4, 14.3, 15.1.5, 15.2.5
Failure of Payment
9.5.1.3, 9.7, 13.6, 14.1.1.3, 14.1.3, 14.2.1.2, 15.1.4
Faulty Work (See Defective or Nonconforming
Work)
Final Completion and Final Payment
4.2.1, 4.2.15, 9.8.2, 9.10, 11.1.2, 11.1.3, 11.3.1,
11.3.5, 12.3, 15.2.1
Financial Arrangements, Owner's
2.2.1
GENERAL PROVISIONS
1
Governing Law
13.1
Guarantees (See Warranty and Warranties)
Hazardous Materials
10.2.4, 10.3
Identification of Contract Documents
1.2.1
Identification of Subcontractors and Suppliers
5.2.1
Indemnification
3.18, 9.10.2, 10.3.3, 10.3.5, 10.3.6, 11.3.1.2, 11.3.7
Information and Services Required of the Owner
2.1.2, 2.2, 4.2.6, 6.1.2, 6.2.5, 9.6.1, 9.6.4, 9.8, 9.9.1,
9.10.3, 10.3.2, 10.3.3, 11.2, 11.3.4, 13.5.1, 13.5.2,
14.1.1.4, 14.1.3, 15.1.2
Initial Decision
15.2
Initial Decision Maker, Definition of

1.1.8
Initial Decision Maker, Extent of Authority
14.2.2, 14.2.4, 15.1.3, 15.2.2, 15.2.3, 15.2.4, 15.2.5
Injury or Damage to Person or Property
3.18.1, 10.2.1, 10.2.2, 10.2.8, 10.3, 10.3.3, 10.4,
11.1.1
Inspections
3.1.3, 3.7.1, 4.2.2, 9.8.2, 9.9.2, 9.10.1, 13.5
Instructions to Bidders
1.1.1
Instructions to the Contractor
3.1.4, 3.3.3, 3.7.1, 4.2.4, 5.2.1, 7, 8.2.2, 12.1, 13.5.2
Instruments of Service, Definition of
1.1.7, 1.5, 1.6
Insurance
6.1.1, 7.3.7, 8.2.2, 9.3.2, 9.8.4, 9.9.1, 9.10.2, 10.2.5,
11
Insurance, Boiler and Machinery
11.3.2
Insurance, Contractor's Liability
11.1
Insurance, Effective Date of
8.2.2, 11.1.2
Insurance, Loss of Use
11.3.3
Insurance, Owner's Liability
11.2
Insurance, Property
10.2.5, 11.3
Insurance, Stored Materials
9.3.2, 11.3.1
INSURANCE AND BONDS
11
Insurance Companies, Consent to Partial Occupancy
9.9.1, 11.3.1.5
Insurance Companies, Settlement with
11.3.10
Intent of the Contract Documents
1.2, 4.2.18, 4.2.19, 7.4
Interest
9.7, 13.6
Interpretation
1.4, 4.2.8, 4.2.17, 4.2.18
Interpretations, Written
4.2.17, 4.2.18, 4.2.20
Joinder and Consolidation of Claims Required
15.4.4
Judgment on Final Award
15.4.2
Labor and Materials, Equipment
1.1.3, 1.1.6, 3.4, 3.8.2, 3.8.3, 3.12.2, 3.12.3, 3.12.6,
3.12.10, 3.13.1, 3.15.1, 5.2.1, 6.2.1, 7.3.7, 9.3.2,
9.3.3, 9.5.1.3, 9.6, 9.10.2, 10.2.1.2, 11.3.1, 14.2.1,
14.2.2
Labor Disputes
8.3.1
Laws and Regulations

3.2.3, 3.2.4, 3.7, 3.13.1, 10.2.2, 10.2.3, 13.5.1, 14.2.1
Liens
2.1.2, 9.3.3, 9.10.2, 9.10.4, 15.2.8
Limitation on Consolidation or Joinder
15.4.4
Limitations, Statutes of
15.4.1
Limitations of Authority
3.12.4, 4.1.3, 4.2.16
Limitations of Liability
9.6.7, 11.1.1, 12.2
Limitations of Time
3.10.1, 4.2.17, 4.2.20, 8.2.1, 9.3.3, 9.6.1, 9.8.4,
9.10.2, 10.2, 11.1.3, 12.1.1, 12.2.2.2, 12.2.5, 13.7,
14.1.1, 15.2.6.1
Loss of Use Insurance
11.3.3
Material Suppliers
1.5.1, 1.5.2, 3.12, 4.2.6, 4.2.8, 9.3.1, 9.3.1.2, 9.3.3,
9.5.3, 9.6.4, 9.6.5, 9.6.7, 9.10.5, 11.3.1
Materials, Hazardous
10.2.4, 10.3
Materials, Labor, Equipment and
1.1.3, 1.1.6, 1.5.1, 1.5.2, 3.4, 3.5, 3.8.2, 3.8.3, 3.12.2,
3.12.3, 3.12.6, 3.12.10, 3.13.1, 5.2.1, 6.2.1, 9.3.1,
9.3.2, 9.3.3, 9.5.1, 9.5.3, 9.6.4, 9.6.5, 9.6.7, 9.10.2,
9.10.5, 10.2.1, 10.2.4, 10.3
Means, Methods, Techniques, Sequences and
Procedures of Construction
3.3.1, 3.12.10, 4.2.5, 4.2.11
Mechanic's Lien
2.1.2, 15.2.8
Mediation
8.3.1, 10.3.5, 15.2.1, 15.2.5, 15.2.6, 15.3, 15.4.1
Minor Changes in the Work
1.1.1, 3.12.8, 4.2.13, 7.1, 7.4
MISCELLANEOUS PROVISIONS
13
Modifications, Definition of
1.1.1
Modifications to the Contract
1.1.1, 1.1.2, 3.11, 4.1.3, 4.2.14, 5.2.3, 7, 11.3.1
Mutual Responsibility
6.2
Nonconforming Work, Acceptance of
9.4.3, 9.8.3, 12.3
Nonconforming Work, Rejection and Correction of
2.3, 2.4, 3.2.3, 3.7.3, 9.4.3.3, 9.8.2, 9.8.3, 9.9.1,
11.1.1, 12.2.2.1, 12.2.3, 12.2.4, 12.2.5
Notice
1.5, 2.1.2, 2.2.1, 2.4, 3.2.4, 3.3.1, 3.7.1, 3.7.2, 3.7.5,
3.9.2, 3.12.9, 5.2.1, 6.3, 9.4.1, 9.7, 9.10.1, 9.10.2,
10.2.2, 10.2.6, 10.2.8, 10.3.2, 11.3.6, 12.2.2.1, 13.3,
13.5.1, 13.5.2, 14.1.2, 14.2.2, 14.4.2, 15.1.2, 15.1.4,
15.1.5.1, 15.2, 15.4.1
Notice of Claims
3.7.2, 10.2.8, 15.1.2, 15.4.1

Notice of Testing and Inspections

13.5.1, 13.5.2

Notices, Permits, Fees and

3.7, 7.3.7, 10.2.2

Observations, On-Site

3.2.1, 9.5.1, 12.1.1

Occupancy

2.2.2, 9.6.6, 9.9, 11.3.1.5

On-Site Inspections

4.2.2, 9.10.1, 9.4.4, 9.5.1

Orders, Written

4.2.7, 4.2.18, 4.2.20

Other Contracts and Contractors

1.1.4, 3.14.2, 4.2.9, 6, 11.3.7, 12.1.2

OWNER

2

Owner, Definition of

2.1.1

Owner, Information and Services Required of the

2.1.2, 2.2, 4.2, 6.1.2, 6.1.3, 6.2.5, 9.3.2, 9.6.1, 9.6.4,
9.9.2, 9.10.2, 10.3.3, 11.2, 11.3, 13.5.1, 13.5.2,
14.1.1, 14.1.3, 15.1.3

Owner's Authority

1.5, 2.1.1, 2.3, 2.4, 3.4.2, 3.12.10, 3.14.2, 4.1.2, 4.1.3,
4.2.8, 4.2.9, 5.2.1, 5.2.4, 5.4.1, 6.1, 6.3, 7.2, 7.3.1,
8.2.2, 9.3.1, 9.3.2, 9.5.1, 9.6.4, 9.9.1, 9.10.2, 10.3.2,
11.3.3, 11.3.10, 12.2.2.1, 12.3, 13.5.2, 14.2, 14.3.1,
14.4, 15.2.7

Owner's Financial Capability

2.2.1, 13.2.2, 14.1.1

Owner's Liability Insurance

11.2

Owner's Relationship with Subcontractors

1.1.2, 5.2.1, 5.3, 5.4.1, 9.6.4, 9.10.2, 14.2.2

Owner's Right to Carry Out the Work

2.4, 12.2.4, 14.2.2

Owner's Right to Clean Up

6.3

Owner's Right to Perform Construction with Own
Forces and to Award Other Contracts

6.1

Owner's Right to Stop the Work

2.3

Owner's Right to Suspend the Work

14.3

Owner's Right to Terminate the Contract

14.2

Ownership and Use of Drawings, Specifications and
Other Instruments of Service

1.1.1, 1.1.5, 1.5, 1.6, 3.11, 3.12.10, 3.17, 4.2.14,
4.2.18, 4.2.20

Partial Occupancy or Use

9.9, 11.3.1.5

Patching, Cutting and

3.14, 6.2.5

Patents and Copyrights, Royalties

3.17

Payment, Applications for

4.2.1, 4.2.7, 4.2.15, 7.3.9, 9.2, 9.3, 9.4, 9.5, 9.7,
9.10.1, 9.10.3, 9.10.5, 11.1.3

Payment, Certificates for

4.2.15, 7.3.9, 9.3, 9.4, 9.5, 9.6.1, 9.6.6, 9.7, 9.10.1,
9.10.3, 14.1.1.3, 15.1.3

Payment, Failure of

9.4.1, 9.5, 9.7, 14.1.1.3

Payment, Final

4.2.1, 9.8.2, 9.10, 11.1.2, 11.3.1, 11.3.5, 12.3, 15.2.1

Payment Bond, Performance Bond and

5.4.1, 7.3.7, 9.6.7, 9.10.2, 9.10.3, 11, 11.4

Payments, Progress

9.3.1, 9.4.2, 9.6

PAYMENTS AND COMPLETION

9, 14

Payments to Subcontractors

5.4.2, 9.3, 9.5.1.3, 9.5.3, 9.6.2, 9.6.3, 9.6.4, 9.6.7,
9.10.5, 14.2.1.2

PCB

10.3.1

Performance Bond and Payment Bond

5.4.1, 7.3.7, 9.6.7, 9.10.2, 9.10.3, 11, 11.4

Permits, Fees, Notices and Compliance with Laws

2.2.2, 3.7, 7.3.7.4, 10.2.2

PERSONS AND PROPERTY, PROTECTION OF

10

Polychlorinated Biphenyl

10.3.1

Product Data, Definition of

3.12.2

Product Data and Samples, Shop Drawings

3.11, 3.12, 4.2.9, 4.2.10, 4.2.14

Progress and Completion

8.2, 9.3.1, 9.4.2, 9.6, 9.8, 9.10, 14.2.4, 15.1.6

Progress Payments

9.3.1, 9.4.2, 9.6

Project, Definition of

1.1.4

Project Representatives

4.2.16

Property Insurance

10.2.5, 11.3

Project Schedule

3.10.1, 3.10.3, 3.10.4, 4.2.2, 4.2.3, 4.2.4

PROTECTION OF PERSONS AND PROPERTY

10

Regulations and Laws

1.5, 3.2.3, 3.6, 3.7, 3.12.10, 3.13, 4.1.1, 9.6.4, 9.9.1,
10.2.2, 11.1, 11.4, 13.1, 13.4, 13.5.1, 13.5.2, 13.6,
14.1.1, 14.2.1, 15.2.8, 15.4

Rejection of Work

3.5, 4.2.8, 12.2.1

Releases of and Waivers of and of Liens

9.10.2

Representations

Init.

1.3, 2.2.1, 3.5, 3.12, 6.2.2, 8.2.1, 9.3.3, 9.4.3, 9.5.1, 9.8.2, 9.10.1
 Representatives
 2.1.1, 3.1.1, 3.9, 4.1.1, 4.2.1, 4.2.2, 4.2.10, 5.1.1, 5.1.2, 13.2.1
 Requests for Information
 4.2.20
 Resolution of Claims and Disputes
 15
 Responsibility for Those Performing the Work
 3.3.2, 3.7.3, 3.12.8, 3.18, 4.2.2, 4.2.5, 4.2.8, 5.3, 6.1.2, 6.2, 6.3, 9.5.1, 9.8.2, 10
 Retainage
 9.3.1, 9.6.2, 9.8.5, 9.9.1, 9.10.2, 9.10.3
 Review of Contract Documents and Field Conditions by Contractor
 1.2.2, 3.2, 3.7.3, 3.12.7
 Review of Contractor's Submittals by Owner, Construction Manager and Architect
 3.10.1, 3.10.2, 3.11, 3.12, 4.2, 5.2, 5.2, 9.2, 9.8.2
 Review of Shop Drawings, Product Data and Samples by Contractor
 3.12.5
 Rights and Remedies
 1.1.2, 2.3, 2.4, 3.7.4, 3.15.2, 4.2.8, 5.3, 5.4, 6.1, 6.3, 7.3.1, 8.3, 9.5.1, 9.7, 10.2.5, 10.3, 12.2.2, 12.2.4, 13.4, 14, 15.4
 Royalties, Patents and Copyrights
 3.17
 Rules and Notices for Arbitration
 15.4
 Safety of Persons and Property
 10.2, 10.3, 10.4
 Safety Precautions and Programs
 3.3.1, 3.12, 4.2.5, 5.3, 10.1, 10.2, 10.3, 10.4
 Samples, Definition of
 3.12.3
 Samples, Shop Drawings, Product Data and
 3.11, 3.12, 4.2.9, 4.2.10
 Samples at the Site, Documents and
 3.11
 Schedule of Values
 9.2, 9.3.1
 Schedules, Construction
 3.10, 3.12.1, 3.12.2, 6.1.2, 15.1.5.2
 Separate Contracts and Contractors
 1.1.4, 3.12.5, 3.14.2, 4.2.6, 4.2.11, 6, 8.3.1, 12.1.2
 Shop Drawings, Definition of
 3.12.1
 Shop Drawings, Product Data and Samples
 3.11, 3.12, 4.2.9, 4.2.10, 4.2.14
 Site, Use of
 3.13, 6.1.1, 6.2.1
 Site Inspections
 3.2.2, 3.3.3, 3.7.1, 3.7.4, 4.2.2, 4.2.3, 4.2.15, 9.4.3.3, 9.8.3, 9.9.2, 9.10.1, 13.5
 Site Visits, Architect's

3.7.4, 4.2.2, 4.2.15, 9.8.3, 9.9.2, 9.10.1, 13.5
 Special Inspections and Testing
 4.2.8, 12.2.1, 13.5
 Specifications, Definition of
 1.1.6
 Specifications
 1.1.1, 1.1.6, 1.2.2, 1.5, 3.11, 3.12.10, 3.17, 4.2.14
 Staffing Plan
 4.2.3
 Statute of Limitations
 12.2.5, 13.7, 15.4.1.1
 Stopping the Work
 2.3, 9.7, 10.3, 14.1
 Stored Materials
 6.2.1, 9.3.2, 10.2.1.2, 10.2.4
 Subcontractor, Definition of
 5.1.1
 SUBCONTRACTORS
 5
 Subcontractors, Work by
 1.2.2, 3.3.2, 3.12.1, 4.2.5, 5.2.3, 5.3, 5.4, 9.3.1.2, 9.6.7
 Subcontractual Relations
 5.3, 5.4, 9.3.1.2, 9.6.2, 9.6.3, 9.10, 10.2.1, 14.1, 14.2
 Submittals
 3.2.3, 3.10, 3.11, 3.12, 4.2.9, 4.2.10, 4.2.11, 5.2.1, 5.2.3, 7.3.7, 9.2, 9.3, 9.8, 9.9.1, 9.10.2, 9.10.3, 11.1.3
 Submittal Schedule
 3.10.2, 3.12.5, 4.2.9, 4.2.10
 Subrogation, Waivers of
 6.1.1, 11.3.7
 Substantial Completion
 8.1.1, 8.1.3, 8.2.3, 9.4.3.3, 9.8, 9.9.1, 9.10.3, 12.2.1, 12.2.2, 13.7
 Substantial Completion, Definition of
 9.8.1
 Substitution of Subcontractors
 5.2.3, 5.2.4
 Substitution of Architect
 4.1.4
 Substitution of Construction Manager
 4.1.4
 Substitutions of Materials
 3.4.2, 3.5, 7.3.8
 Sub-subcontractor, Definition of
 5.1.2
 Subsurface Conditions
 3.7.4
 Successors and Assigns
 13.2
 Superintendent
 3.9, 10.2.6
 Supervision and Construction Procedures
 1.2.2, 3.3, 3.4, 3.12.10, 4.2.2, 4.2.3, 4.2.5, 4.2.8, 4.2.9, 4.2.10, 4.2.11, 6.1.3, 6.2.4, 7.1.3, 7.3.7, 8.2, 8.3.1, 9.4.3.3, 10, 12, 14, 15.1.3
 Surety

5.4.1.2, 9.8.5, 9.10.2, 9.10.3, 14.2.2, 15.2.7
 Surety, Consent of
 9.10.2, 9.10.3
 Surveys
 1.1.7, 2.2.3
 Suspension by the Owner for Convenience
 14.3
 Suspension of the Work
 5.4.2, 14.3
 Suspension or Termination of the Contract
 5.4.1.1, 14
 Taxes
 3.6, 3.8.2.1, 7.3.7.4
 Termination by the Contractor
 14.1, 15.1.6
 Termination by the Owner for Cause
 5.4.1.1, 14.2, 15.1.6
 Termination by the Owner for Convenience
 14.4
 Termination of the Contractor
 14.2.2
 TERMINATION OR SUSPENSION OF THE
 CONTRACT
 14
 Tests and Inspections
 3.1.4, 3.3.3, 4.2.2, 4.2.6, 4.2.8, 9.4.3.3, 9.8.3, 9.9.2,
 9.10.1, 10.3.2, 12.2.1, 13.5
 TIME
 8
 Time, Delays and Extensions of
 3.2.4, 3.7.4, 5.2.3, 7.2, 7.3.1, 7.4, 8.3, 9.5.1, 10.3.2,
 14.3.2, 15.1.5, 15.2.5
 Time Limits
 2.1.2, 2.2, 2.4, 3.2.2, 3.10, 3.11, 3.12.5, 3.15.1, 4.2.1,
 5.2, 5.3, 5.4, 6.2.4, 7.3, 7.4, 8.2, 9.2, 9.3.1, 9.3.3,
 9.4.1, 9.4.2, 9.5, 9.6, 9.7, 9.8, 9.9, 9.10, 11.1.3, 11.4,
 12.2, 13.5, 13.7, 14, 15
 Time Limits on Claims
 3.7.4, 10.2.8, 13.7, 15.1.2
 Title to Work
 9.3.2, 9.3.3
 Transmission of Data in Digital Form
 1.6
 UNCOVERING AND CORRECTION OF WORK
 12

Uncovering of Work
 12.1
 Unforeseen Conditions, Concealed or Unknown
 3.7.4, 8.3.1, 10.3
 Unit Prices
 7.3.3.2, 7.3.4
 Use of Documents
 1.1.1, 1.5, 2.2.5, 3.12.6, 5.3
 Use of Site
 3.13, 6.1.1, 6.2.1
 Values, Schedule of
 9.2, 9.3.1
 Waiver of Claims by the Architect
 13.4.2
 Waiver of Claims by the Construction Manager
 13.4.2
 Waiver of Claims by the Contractor
 9.10.5, 13.4.2, 15.1.6
 Waiver of Claims by the Owner
 9.9.3, 9.10.3, 9.10.4, 12.2.2.1, 13.4.2, 14.2.4, 15.1.6
 Waiver of Consequential Damages
 14.2.4, 15.1.6
 Waiver of Liens
 9.10.2, 9.10.4
 Waivers of Subrogation
 6.1.1, 11.3.7
 Warranty
 3.5, 4.2.15, 9.3.3, 9.8.4, 9.9.1, 9.10.4, 12.2.2
 Weather Delays
 15.1.5.2
 Work, Definition of
 1.1.3
 Written Consent
 1.5.2, 3.4.2, 3.7.4, 3.12.8, 3.14.2, 4.1.3, 9.3.2, 9.8.5,
 9.9.1, 9.10.2, 9.10.3, 10.3.2, 11.4.1, 13.2, 13.4.2,
 15.4.4.2
 Written Interpretations
 4.2.17, 4.2.18
 Written Notice
 2.3, 2.4, 3.3.1, 3.9, 3.12.9, 3.12.10, 5.2.1, 5.3, 5.4.1.1,
 8.2.2, 9.4, 9.5.1, 9.7, 9.10, 10.2.2, 10.3, 11.1.3,
 12.2.2, 12.2.4, 13.3, 13.5.2, 14, 15.4.1
 Written Orders
 1.1.1, 2.3, 3.9, 7, 8.2.2, 12.1, 12.2, 13.5.2, 14.3.1,
 15.1.2

ARTICLE 1 GENERAL PROVISIONS

§ 1.1 Basic Definitions

§ 1.1.1 The Contract Documents. The Contract Documents are enumerated in the Agreement between the Owner and Contractor (hereinafter the Agreement), and consist of the Agreement, Conditions of the Contract (General, Supplementary and other Conditions), Drawings, Specifications, Addenda issued prior to execution of the Contract, other documents listed in the Agreement and Modifications issued after execution of the Contract. A Modification is (1) a written amendment to the Contract signed by both parties, (2) a Change Order, (3) a Construction Change Directive or (4) a written order for a minor change in the Work issued by the Architect. Unless specifically enumerated in the Agreement, the Contract Documents do not include the advertisement or invitation to bid, Instructions to Bidders, sample forms, other information furnished by the Owner in anticipation of receiving bids or proposals, the Contractor's bid or proposal, or portions of addenda relating to bidding requirements).

§ 1.1.2 The Contract. The Contract Documents form the Contract for Construction. The Contract represents the entire and integrated agreement between the parties hereto and supersedes prior negotiations, representations or agreements, either written or oral. The Contract may be amended or modified only by a Modification. The Contract Documents shall not be construed to create a contractual relationship of any kind (1) between the Contractor and the Architect or the Architect's consultants, (2) between the Owner and the Construction Manager or the Construction Manager's consultants, (3) between the Owner and the Architect or the Architect's consultants, (4) between the Contractor and the Construction Manager or the Construction Manager's consultants, (5) between the Owner and a Subcontractor or Sub-subcontractor (6) between the Construction Manager and the Architect, or (7) between any persons or entities other than the Owner and Contractor. The Construction Manager and Architect shall, however, be entitled to performance and enforcement of obligations under the Contract intended to facilitate performance of their duties.

§ 1.1.3 The Work. The term "Work" means the construction and services required by the Contract Documents, whether completed or partially completed, and includes all other labor, materials, equipment and services provided or to be provided by the Contractor to fulfill the Contractor's obligations. The Work may constitute the whole or a part of the Project.

§ 1.1.4 The Project. The Project is the total construction of which the Work performed under the Contract Documents may be the whole or a part and which may include construction by other Multiple Prime Contractors and by the Owner's own forces, including persons or entities under separate contracts not administered by the Construction Manager.

§ 1.1.5 The Drawings. The Drawings are the graphic and pictorial portions of the Contract Documents showing the design, location and dimensions of the Work, generally including plans, elevations, sections, details, schedules and diagrams.

§ 1.1.6 The Specifications. The Specifications are that portion of the Contract Documents consisting of the written requirements for materials, equipment, systems, standards and workmanship for the Work, and performance of related services.

§ 1.1.7 Instruments of Service. Instruments of Service are representations, in any medium of expression now known or later developed, of the tangible and intangible creative work performed by the Architect and the Architect's consultants under their respective professional services agreements. Instruments of Service may include, without limitation, studies, surveys, models, sketches, drawings, specifications, and other similar materials.

§ 1.1.8 Initial Decision Maker. The Initial Decision Maker is the person identified in the Agreement to render initial decisions on Claims in accordance with Section 15.2 and certify termination of the Agreement under Section 14.2.2.

§ 1.2 Correlation and Intent of the Contract Documents

§ 1.2.1 The intent of the Contract Documents is to include all items necessary for the proper execution and completion of the Work by the Contractor. The Contract Documents are complementary, and what is required by one shall be as binding as if required by all; performance by the Contractor shall be required only to the extent consistent with the Contract Documents and reasonably inferable from them as being necessary to produce the indicated results.

§ 1.2.2 Organization of the Specifications into divisions, sections and articles, and arrangement of Drawings shall not control the Contractor in dividing the Work among Subcontractors or in establishing the extent of Work to be performed by any trade.

§ 1.2.3 Unless otherwise stated in the Contract Documents, words that have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings.

§ 1.3 Capitalization

Terms capitalized in these General Conditions include those that are (1) specifically defined, (2) the titles of numbered articles or (3) the titles of other documents published by the American Institute of Architects.

§ 1.4 Interpretation

In the interest of brevity the Contract Documents frequently omit modifying words such as “all” and “any” and articles such as “the” and “an,” but the fact that a modifier or an article is absent from one statement and appears in another is not intended to affect the interpretation of either statement.

§ 1.5 Ownership and Use of Drawings, Specifications and Other Instruments of Service

§ 1.5.1 The Architect and the Architect’s consultants shall be deemed the authors and owners of their respective Instruments of Service, including the Drawings and Specifications, and will retain all common law, statutory and other reserved rights, including copyrights. The Contractor, Subcontractors, sub-subcontractors, and material or equipment suppliers shall not own or claim a copyright in the Instruments of Service. Submittal or distribution to meet official regulatory requirements or for other purposes in connection with this Project is not to be construed as publication in derogation of the Architect, or Architect’s consultants’ reserved rights.

§ 1.5.2 The Contractor, Subcontractors, Sub-subcontractors, and material or equipment suppliers are authorized to use and reproduce the Instruments of Service provided to them solely and exclusively for execution of the Work. All copies made under this authorization shall bear the copyright notice, if any, shown on the Instruments of Service. The Contractor, Subcontractors, Sub-subcontractors, and material or equipment suppliers may not use the Instruments of Service on other projects or for additions to this Project outside the scope of the Work without the specific written consent of the Owner, Architect and the Architect’s consultants.

§ 1.6 Transmission of Data in Digital Form

If the parties intend to transmit Instruments of Service or any other information or documentation in digital form, they shall endeavor to establish necessary protocols governing such transmissions, unless otherwise already provided in the Agreement or the Contract Documents.

ARTICLE 2 OWNER

§ 2.1 General

§ 2.1.1 The Owner is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Owner shall designate in writing a representative who shall have express authority to bind the Owner with respect to all matters requiring the Owner’s approval or authorization. Except as otherwise provided in Article 4, the Construction Manager and the Architect do not have such authority. The term “Owner” means the Owner or the Owner’s authorized representative.

§ 2.1.2 The Owner shall furnish to the Contractor within fifteen days after receipt of a written request, information necessary and relevant for the Contractor to evaluate, give notice of or enforce mechanic’s lien rights. Such information shall include a correct statement of the record legal title to the property on which the Project is located, usually referred to as the site, and the Owner’s interest therein.

§ 2.2 Information and Services Required of the Owner

§ 2.2.1 Prior to commencement of the Work, the Contractor may request in writing that the Owner provide reasonable evidence that the Owner has made financial arrangements to fulfill the Owner’s obligations under the Contract. Thereafter, the Contractor may only request such evidence if (1) the Owner fails to make payments to the Contractor as the Contract Documents require; (2) a change in the Work materially changes the Contract Sum; or (3) the Contractor identifies in writing a reasonable concern regarding the Owner’s ability to make payment when due. The Owner shall furnish such evidence as a condition precedent to commencement or continuation of the Work or

the portion of the Work affected by a material change. After the Owner furnishes the evidence, the Owner shall not materially vary such financial arrangements without prior notice to the Contractor.

§ 2.2.2 Except for permits and fees that are the responsibility of the Contractor under the Contract Documents, including those required under Section 3.7.1, the Owner shall secure and pay for necessary approvals, easements, assessments and charges required for construction, use or occupancy of permanent structures or for permanent changes in existing facilities. Unless otherwise provided under the Contract Documents, the Owner, through the Construction Manager, shall secure and pay for the building permit.

§ 2.2.3 The Owner shall furnish surveys describing physical characteristics, legal limitations and utility locations for the site of the Project, and a legal description of the site. The Contractor shall be entitled to rely on the accuracy of information furnished by the Owner but shall exercise proper precautions relating to the safe performance of the Work.

§ 2.2.4 The Owner shall furnish information or services required of the Owner by the Contract Documents with reasonable promptness. The Owner shall also furnish any other information or services under the Owner's control and relevant to the Contractor's performance of the Work with reasonable promptness after receiving the Contractor's written request for such information or services.

§ 2.2.5 Unless otherwise provided in the Contract Documents, the Owner shall furnish to the Contractor one copy of the Contract Documents for purposes of making reproductions pursuant to Section 1.5.2.

§ 2.2.6 The Owner shall endeavor to forward all communications to the Contractor through the Construction Manager and shall contemporaneously provide the same communications to the Architect about matters arising out of or relating to the Contract Documents.

§ 2.3 Owner's Right to Stop the Work

If the Contractor fails to correct Work that is not in accordance with the requirements of the Contract Documents as required by Section 12.2 or repeatedly fails to carry out Work in accordance with the Contract Documents, the Owner may issue a written order to the Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, the right of the Owner to stop the Work shall not give rise to a duty on the part of the Owner to exercise this right for the benefit of the Contractor or any other person or entity, except to the extent required by Section 6.1.3.

§ 2.4 Owner's Right to Carry Out the Work

If the Contractor defaults or neglects to carry out the Work in accordance with the Contract Documents and fails within a ten-day period after receipt of written notice from the Owner to commence and continue correction of such default or neglect with diligence and promptness, the Owner may, without prejudice to other remedies the Owner may have, correct such deficiencies. In such case an appropriate Change Order shall be issued deducting from payments then or thereafter due the Contractor the reasonable cost of correcting such deficiencies, including Owner's expenses and compensation for the Construction Manager's and Architect's and their respective consultants' additional services made necessary by such default, neglect or failure. Such action by the Owner and amounts charged to the Contractor are both subject to prior approval of the Architect, after consultation with the Construction Manager. If payments then or thereafter due the Contractor are not sufficient to cover such amounts, the Contractor shall pay the difference to the Owner.

ARTICLE 3 CONTRACTOR

§ 3.1 General

§ 3.1.1 The Contractor is the person or entity identified as such in the Agreement and is referred to throughout the Contract Documents as if singular in number. The Contractor shall be lawfully licensed, if required in the jurisdiction where the Project is located. The Contractor shall designate in writing a representative who shall have express authority to bind the Contractor with respect to all matters under this Contract. The term "Contractor" means the Contractor or the Contractor's authorized representative.

§ 3.1.2 The plural term "Multiple Prime Contractors" refers to persons or entities who perform construction under contracts with the Owner that are administered by the Construction Manager. The term does not include the Owner's own forces, including persons or entities under separate contracts not administered by the Construction Manager.

§ 3.1.3 The Contractor shall perform the Work in accordance with the Contract Documents.

§ 3.1.4 The Contractor shall not be relieved of obligations to perform the Work in accordance with the Contract Documents either by activities or duties of the Construction Manager or Architect in their administration of the Contract, or by tests, inspections or approvals required or performed by persons or entities other than the Contractor.

§ 3.2 Review of Contract Documents and Field Conditions by Contractor

§ 3.2.1 Execution of the Contract by the Contractor is a representation that the Contractor has visited the site, become generally familiar with local conditions under which the Work is to be performed and correlated personal observations with requirements of the Contract Documents.

§ 3.2.2 Because the Contract Documents are complementary, the Contractor shall, before starting each portion of the Work, carefully study and compare the various Contract Documents relative to that portion of the Work, as well as the information furnished by the Owner pursuant to Section 2.2.3, shall take field measurements of any existing conditions related to that portion of the Work, and shall observe any conditions at the site affecting it. These obligations are for the purpose of facilitating coordination and construction by the Contractor and are not for the purpose of discovering errors, omissions, or inconsistencies in the Contract Documents; however, the Contractor shall promptly report to the Construction Manager and Architect any errors, inconsistencies or omissions discovered by or made known to the Contractor as a request for information submitted to the Construction Manager in such form as the Construction Manager and Architect may require. It is recognized that the Contractor's review is made in the Contractor's capacity as a contractor and not as a licensed design professional, unless otherwise specifically provided in the Contract Documents.

§ 3.2.3 The Contractor is not required to ascertain that the Contract Documents are in accordance with applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, but the Contractor shall promptly report to the Construction Manager and Architect any nonconformity discovered by or made known to the Contractor as a request for information submitted to Construction Manager in such form as the Construction Manager and Architect may require.

§ 3.2.4 If the Contractor believes that additional cost or time is involved because of clarifications or instructions the Architect issues in response to the Contractor's notices or requests for information pursuant to Sections 3.2.2 or 3.2.3, the Contractor shall make Claims as provided in Article 15. If the Contractor fails to perform the obligations of Sections 3.2.2 or 3.2.3, the Contractor shall pay such costs and damages to the Owner as would have been avoided if the Contractor had performed such obligations. If the Contractor performs those obligations, the Contractor shall not be liable to the Owner or Architect for damages resulting from errors, inconsistencies or omissions in the Contract Documents, for differences between field measurements or conditions and the Contract Documents, or for nonconformities of the Contract Documents to applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities.

§ 3.3 Supervision and Construction Procedures

§ 3.3.1 The Contractor shall supervise and direct the Work, using the Contractor's best skill and attention. The Contractor shall be solely responsible for, and have control over, construction means, methods, techniques, sequences and procedures and for coordinating all portions of the Work under the Contract, unless the Contract Documents give other specific instruction concerning these matters. If the Contract Documents give specific instructions concerning construction means, methods, techniques, sequences or procedures, the Contractor shall evaluate the jobsite safety thereof and, except as stated below, shall be fully and solely responsible for the jobsite safety of such means, methods, techniques, sequences or procedures. If the Contractor determines that such means, methods, techniques, sequences or procedures may not be safe, the Contractor shall give timely written notice to the Owner, the Construction Manager, and the Architect and shall not proceed with that portion of the Work without further written instructions from the Architect, through the Construction Manager. If the Contractor is then instructed to proceed with the required means, methods, techniques, sequences or procedures without acceptance of changes proposed by the Contractor, the Owner shall be solely responsible for any loss or damage arising solely from those Owner-required means, methods, techniques, sequences or procedures.

§ 3.3.2 The Contractor shall be responsible to the Owner for acts and omissions of the Contractor's employees, Subcontractors and their agents and employees, and other persons performing portions of the Work for, or on behalf of, the Contractor or any of its Subcontractors.

§ 3.3.3 The Contractor shall be responsible for inspection of portions of the Project already performed to determine that such portions are in proper condition to receive subsequent Work.

§ 3.4 Labor and Materials

§ 3.4.1 Unless otherwise provided in the Contract Documents, the Contractor shall provide and pay for labor, materials, equipment, tools, construction equipment and machinery, water, heat, utilities, transportation, and other facilities and services necessary for proper execution and completion of the Work, whether temporary or permanent and whether or not incorporated or to be incorporated in the Work.

§ 3.4.2 Except in the case of minor changes in the Work authorized by the Architect in accordance with Sections 3.12.8 or 7.4, the Contractor may make substitutions only with the consent of the Owner, after evaluation by the Architect, in consultation with the Construction Manager, and in accordance with a Change Order or Construction Change Directive.

§ 3.4.3 The Contractor shall enforce strict discipline and good order among the Contractor's employees and other persons carrying out the Work. The Contractor shall not permit employment of unfit persons or persons not properly skilled in tasks assigned to them.

§ 3.5 Warranty

The Contractor warrants to the Owner, Construction Manager, and Architect that materials and equipment furnished under the Contract will be of good quality and new unless the Contract Documents require or permit otherwise. The Contractor further warrants that the Work will conform with the requirements of the Contract Documents and will be free from defects, except for those inherent in the quality of the Work the Contract Documents require or permit. Work, materials, or equipment not conforming to these requirements may be considered defective. The Contractor's warranty excludes remedy for damage or defect caused by abuse, alterations to the Work not executed by the Contractor, improper or insufficient maintenance, improper operation, or normal wear and tear and normal usage. If required by the Construction Manager or Architect, the Contractor shall furnish satisfactory evidence as to the kind and quality of materials and equipment.

§ 3.6 Taxes

The Contractor shall pay sales, consumer, use and similar taxes for the Work or portions thereof provided by the Contractor that are legally enacted when bids are received or negotiations concluded, whether or not yet effective or merely scheduled to go into effect.

§ 3.7 Permits, Fees, Notices, and Compliance with Laws

§ 3.7.1 Unless otherwise provided in the Contract Documents, the Owner, through the Construction Manager, shall secure and pay for the building permit. The Contractor shall secure and pay for other permits, fees, licenses and inspections by government agencies necessary for proper execution and completion of the Work that are customarily secured after execution of the Contract and legally required at the time bids are received or negotiations concluded.

§ 3.7.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities applicable to performance of the Work.

§ 3.7.3 If the Contractor performs Work knowing it to be contrary to applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of public authorities, the Contractor shall assume appropriate responsibility for such Work and shall bear the costs attributable to correction.

§ 3.7.4 Concealed or Unknown Conditions. If the Contractor encounters conditions at the site that are (1) subsurface or otherwise concealed physical conditions that differ materially from those indicated in the Contract Documents or (2) unknown physical conditions of an unusual nature that differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, the Contractor shall promptly provide notice to the Owner, Construction Manager, and the Architect before conditions are disturbed and in no event later than 21 days after first observance of the conditions. The Architect and

Construction Manager will promptly investigate such conditions and, if the Architect, in consultation with the Construction Manager, determines that they differ materially and cause an increase or decrease in the Contractor's cost of, or time required for, performance of any part of the Work, will recommend an equitable adjustment in the Contract Sum or Contract Time, or both. If the Architect, in consultation with the Construction Manager, determines that the conditions at the site are not materially different from those indicated in the Contract Documents and that no change in the terms of the Contract is justified, the Architect shall promptly notify the Owner, Construction Manager, and Contractor in writing, stating the reasons. If the Owner or Contractor disputes the Architect's determination or recommendation, either party may proceed as provided in Article 15.

§ 3.7.5 If, in the course of the Work, the Contractor encounters human remains or recognizes the existence of burial markers, archaeological sites or wetlands not indicated in the Contract Documents, the Contractor shall immediately suspend any operations that would affect them and shall notify the Owner, Construction Manager, and Architect. Upon receipt of such notice, the Owner shall promptly take any action necessary to obtain governmental authorization required to resume the operations. The Contractor shall continue to suspend such operations until otherwise instructed by the Owner but shall continue with all other operations that do not affect those remains or features. Requests for adjustments in the Contract Sum and Contract Time arising from the existence of such remains or features may be made as provided in Article 15.

§ 3.8 Allowances

§ 3.8.1 The Contractor shall include in the Contract Sum all allowances stated in the Contract Documents. Items covered by allowances shall be supplied for such amounts and by such persons or entities as the Owner may direct, but the Contractor shall not be required to employ persons or entities to whom the Contractor has reasonable objection.

§ 3.8.2 Unless otherwise provided in the Contract Documents:

- .1 Allowances shall cover the cost to the Contractor of materials and equipment delivered at the site and all required taxes, less applicable trade discounts;
- .2 Contractor's costs for unloading and handling at the site, labor, installation costs, overhead, profit and other expenses contemplated for stated allowance amounts shall be included in the Contract Sum but not in the allowances; and
- .3 Whenever costs are more than or less than allowances, the Contract Sum shall be adjusted accordingly by Change Order. The amount of the Change Order shall reflect (1) the difference between actual costs and the allowances under Section 3.8.2.1 and (2) changes in Contractor's costs under Section 3.8.2.2.

§ 3.8.3 Materials and equipment under an allowance shall be selected by the Owner with reasonable promptness.

§ 3.9 Superintendent

§ 3.9.1 The Contractor shall employ a competent superintendent and necessary assistants who shall be in attendance at the Project site during performance of the Work. The superintendent shall represent the Contractor, and communications given to the superintendent shall be as binding as if given to the Contractor.

§ 3.9.2 The Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Owner and Architect through the Construction Manager, the name and qualifications of a proposed superintendent. The Construction Manager may reply within 14 days to the Contractor in writing stating (1) whether the Owner, the Construction Manager, or the Architect has reasonable objection to the proposed superintendent or (2) that any of them require additional time to review. Failure of the Construction Manager to reply within the 14 day period shall constitute notice of no reasonable objection.

§ 3.9.3 The Contractor shall not employ a proposed superintendent to whom the Owner, Construction Manager or Architect has made reasonable and timely objection. The Contractor shall not change the superintendent without the Owner's consent, which shall not unreasonably be withheld or delayed.

§ 3.10 Contractor's Construction Schedules

§ 3.10.1 The Contractor, promptly after being awarded the Contract, shall prepare and submit for the Owner's and Architect's information and the Construction Manager's approval a Contractor's construction schedule for the Work. The schedule shall not exceed time limits current under the Contract Documents, shall be revised at

appropriate intervals as required by the conditions of the Work and Project, shall be related to the entire Project schedule to the extent required by the Contract Documents, and shall provide for expeditious and practicable execution of the Work. The Contractor shall cooperate with the Construction Manager in scheduling and performing the Contractor's Work to avoid conflict with, and as to cause no delay in, the work or activities of other Multiple Prime Contractors or the construction or operations of the Owner's own forces.

§ 3.10.2 The Contractor shall prepare a submittal schedule, promptly after being awarded the Contract and thereafter update it as necessary to maintain a current submittal schedule, and shall submit the schedule(s) for the Construction Manager's and Architect's approval. The Architect and Construction Manager's approval shall not unreasonably be delayed or withheld. The submittal schedule shall (1) be coordinated with the Contractor's construction schedule, and (2) allow the Construction Manager and Architect reasonable time to review submittals. If the Contractor fails to submit a submittal schedule, the Contractor shall not be entitled to any increase in Contract Sum or extension of Contract Time based on the time required for review of submittals.

§ 3.10.3 The Contractor shall participate with other Contractors, the Construction Manager and Owner in reviewing and coordinating all schedules for incorporation into the Project schedule that is prepared by the Construction Manager. The Contractor shall make revisions to the construction schedule and submittal schedule as deemed necessary by the Construction Manager to conform to the Project schedule.

§ 3.10.4 The Contractor shall perform the Work in general accordance with the most recent schedules submitted to the Owner, Construction Manager and Architect and incorporated into the approved Project schedule.

§ 3.11 Documents and Samples at the Site

The Contractor shall maintain at the site for the Owner one copy of the Drawings, Specifications, Addenda, Change Orders and other Modifications, in good order and marked currently to indicate field changes and selections made during construction, and one copy of approved Shop Drawings, Product Data, Samples and similar required submittals. These documents shall be available to the Architect and delivered to the Construction Manager for submittal to the Owner upon completion of the Work as a record of the Work as constructed.

§ 3.12 Shop Drawings, Product Data and Samples

§ 3.12.1 Shop Drawings are drawings, diagrams, schedules and other data specially prepared for the Work by the Contractor or a Subcontractor, Sub-subcontractor, manufacturer, supplier or distributor to illustrate some portion of the Work.

§ 3.12.2 Product Data are illustrations, standard schedules, performance charts, instructions, brochures, diagrams and other information furnished by the Contractor to illustrate materials or equipment for some portion of the Work.

§ 3.12.3 Samples are physical examples that illustrate materials, equipment or workmanship and establish standards by which the Work will be judged.

§ 3.12.4 Shop Drawings, Product Data, Samples and similar submittals are not Contract Documents. Their purpose is to demonstrate the way by which the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents for those portions of the Work for which the Contract Documents require submittals. Review by the Architect and Construction Manager is subject to the limitations of Sections 4.2.9 through 4.2.11. Informational submittals upon which the Construction Manager and Architect are not expected to take responsive action may be so identified in the Contract Documents. Submittals that are not required by the Contract Documents may be returned by the Construction Manager or Architect without action.

§ 3.12.5 The Contractor shall review for compliance with the Contract Documents, approve and submit to the Construction Manager Shop Drawings, Product Data, Samples and similar submittals required by the Contract Documents in accordance with the Project submittal schedule approved by the Construction Manager and Architect, or in the absence of an approved Project submittal schedule, with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of other Multiple Prime Contractors or the Owner's own forces. The Contractor shall cooperate with the Construction Manager in the coordination of the Contractor's Shop Drawings, Product Data, Samples and similar submittals with related documents submitted by other Multiple Prime Contractors.

§ 3.12.6 By submitting Shop Drawings, Product Data, Samples and similar submittals, the Contractor represents to the Owner, Construction Manager, and Architect, that the Contractor has (1) reviewed and approved them, (2) determined and verified materials, field measurements and field construction criteria related thereto, or will do so and (3) checked and coordinated the information contained within such submittals with the requirements of the Work and of the Contract Documents.

§ 3.12.7 The Contractor shall perform no portion of the Work for which the Contract Documents require submittal and review of Shop Drawings, Product Data, Samples or similar submittals until the respective submittal has been reviewed and approved by the Architect.

§ 3.12.8 The Work shall be in accordance with approved submittals except that the Contractor shall not be relieved of responsibility for deviations from requirements of the Contract Documents by the Architect's approval of Shop Drawings, Product Data, Samples or similar submittals unless the Contractor has specifically informed the Construction Manager and Architect in writing of such deviation at the time of submittal and (1) the Architect has given written approval to the specific deviation as a minor change in the Work, or (2) a Change Order or Construction Change Directive has been issued authorizing the deviation. The Contractor shall not be relieved of responsibility for errors or omissions in Shop Drawings, Product Data, Samples or similar submittals by the Architect's approval thereof.

§ 3.12.9 The Contractor shall direct specific attention, in writing or on resubmitted Shop Drawings, Product Data, Samples or similar submittals, to revisions other than those requested by the Construction Manager and Architect on previous submittals. In the absence of such written notice, the Architect's approval of a resubmission shall not apply to such revisions.

§ 3.12.10 The Contractor shall not be required to provide professional services that constitute the practice of architecture or engineering unless such services are specifically required by the Contract Documents for a portion of the Work or unless the Contractor needs to provide such services in order to carry out the Contractor's responsibilities for construction means, methods, techniques, sequences and procedures. The Contractor shall not be required to provide professional services in violation of applicable law. If professional design services or certifications by a design professional related to systems, materials or equipment are specifically required of the Contractor by the Contract Documents, the Owner and the Architect will specify all performance and design criteria that such services must satisfy. The Contractor shall cause such services or certifications to be provided by a properly licensed design professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, Shop Drawings and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to the Architect. The Owner and the Architect shall be entitled to rely upon the adequacy, accuracy and completeness of the services, certifications and approvals performed or provided by such design professionals, provided the Owner and Architect have specified to the Contractor all performance and design criteria that such services must satisfy. Pursuant to this Section 3.12.10, the Architect will review, approve or take other appropriate action on submittals only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Contractor shall not be responsible for the adequacy of the performance and design criteria specified in the Contract Documents.

§ 3.13 Use of Site

§ 3.13.1 The Contractor shall confine operations at the site to areas permitted by applicable laws, statutes, ordinances, codes, rules and regulations, and lawful orders of public authorities and the Contract Documents and shall not unreasonably encumber the site with materials or equipment.

§ 3.13.2 The Contractor shall coordinate the Contractor's operations with, and secure the approval of, the Construction Manager before using any portion of the site.

§ 3.14 Cutting and Patching

§ 3.14.1 The Contractor shall be responsible for cutting, fitting or patching required to complete the Work or to make its parts fit together properly. All areas requiring cutting, fitting and patching shall be restored to the condition existing prior to the cutting, fitting and patching, unless otherwise required by the Contract Documents.

§ 3.14.2 The Contractor shall not damage or endanger a portion of the Work or fully or partially completed construction of the Owner's own forces or of other Multiple Prime Contractors by cutting, patching, or otherwise altering such construction, or by excavation. The Contractor shall not cut or otherwise alter such construction by the Owner's own forces or by other Multiple Prime Contractors except with written consent of the Construction Manager, Owner and such other Multiple Prime Contractors; such consent shall not be unreasonably withheld. The Contractor shall not unreasonably withhold from the other Multiple Prime Contractors or the Owner the Contractor's consent to cutting or otherwise altering the Work.

§ 3.15 Cleaning Up

§ 3.15.1 The Contractor shall keep the premises and surrounding area free from accumulation of waste materials or rubbish caused by operations under the Contract. At completion of the Work the Contractor shall remove waste materials, rubbish, the Contractor's tools, construction equipment, machinery and surplus materials from and about the Project.

§ 3.15.2 If the Contractor fails to clean up as provided in the Contract Documents, the Owner, or Construction Manager with the Owner's approval, may do so and the Owner shall be entitled to reimbursement from the Contractor.

§ 3.16 Access to Work

The Contractor shall provide the Owner, Construction Manager and Architect access to the Work in preparation and progress wherever located.

§ 3.17 Royalties, Patents and Copyrights

The Contractor shall pay all royalties and license fees. The Contractor shall defend suits or claims for infringement of copyrights and patent rights and shall hold the Owner, Construction Manager and Architect harmless from loss on account thereof, but shall not be responsible for such defense or loss when a particular design, process or product of a particular manufacturer or manufacturers is required by the Contract Documents or where the copyright violations are contained in Drawings, Specifications or other documents prepared by the Owner, Architect, or Construction Manager. However, if the Contractor has reason to believe that the required design, process or product is an infringement of a copyright or a patent, the Contractor shall be responsible for such loss unless such information is promptly furnished to the Architect through the Construction Manager.

§ 3.18 Indemnification

§ 3.18.1 To the fullest extent permitted by law, the Contractor shall indemnify and hold harmless the Owner, Construction Manager, Architect, Construction Manager's and Architect's consultants, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself) but only to the extent caused by the negligent acts or omissions of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, regardless of whether or not such claim, damage, loss or expense is caused in part by a party indemnified hereunder. Such obligation shall not be construed to negate, abridge or reduce other rights or obligations of indemnity that would otherwise exist as to a party or person described in this Section 3.18.

§ 3.18.2 In claims against any person or entity indemnified under this Section 3.18 by an employee of the Contractor, a Subcontractor, anyone directly or indirectly employed by them or anyone for whose acts they may be liable, the indemnification obligation under Section 3.18 shall not be limited by a limitation on amount or type of damages, compensation or benefits payable by or for the Contractor or a Subcontractor under workers' compensation acts, disability benefit acts or other employee benefit acts.

ARTICLE 4 ARCHITECT AND CONSTRUCTION MANAGER

§ 4.1 General

§ 4.1.1 The Owner shall retain an architect lawfully licensed to practice architecture or an entity lawfully practicing architecture in the jurisdiction where the Project is located. That person or entity is identified as the Architect in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 4.1.2 The Owner shall retain a construction manager lawfully licensed to practice construction management or an entity lawfully practicing construction management in the jurisdiction where the Project is located. That person or entity is identified as the Construction Manager in the Agreement and is referred to throughout the Contract Documents as if singular in number.

§ 4.1.3 Duties, responsibilities and limitations of authority of the Construction Manager and Architect as set forth in the Contract Documents shall not be restricted, modified or extended without written consent of the Owner, Construction Manager, Architect and Contractor. Consent shall not be unreasonably withheld.

§ 4.1.4 If the employment of the Construction Manager or Architect is terminated, the Owner shall employ a successor construction manager or architect as to whom the Contractor has no reasonable objection and whose status under the Contract Documents shall be that of the Construction Manager or Architect, respectively.

§ 4.2 Administration of the Contract

§ 4.2.1 The Construction Manager and Architect will provide administration of the Contract as described in the Contract Documents and will be the Owner's representatives during construction until the date the Architect issues the final Certificate for Payment. The Construction Manager and Architect will have authority to act on behalf of the Owner only to the extent provided in the Contract Documents.

§ 4.2.2 The Architect will visit the site at intervals appropriate to the stage of construction, or as otherwise agreed with the Owner, to become generally familiar with the progress and quality of the portion of the Work completed, and to determine in general if the Work observed is being performed in a manner indicating that the Work, when fully completed, will be in accordance with the Contract Documents. However, the Architect will not be required to make exhaustive or continuous on-site inspections to check the quality or quantity of the Work. On the basis of the site visits, the Architect will keep the Owner reasonably informed about the progress and quality of the portion of the Work completed, and report to the Owner and Construction Manager (1) known deviations from the Contract Documents and from the most recent Project schedule prepared by the Construction Manager, and (2) defects and deficiencies observed in the Work.

§ 4.2.3 The Construction Manager shall provide a staffing plan to include one or more representatives who shall be in attendance at the Project site whenever the Work is being performed. The Construction Manager will determine in general if the Work observed is being performed in accordance with the Contract Documents, will keep the Owner reasonably informed of the progress of the Work, and will report to the Owner and Architect (1) known deviations from the Contract Documents and the most recent Project schedule, and (2) defects and deficiencies observed in the Work.

§ 4.2.4 The Construction Manager will schedule and coordinate the activities of the Contractor and other Multiple Prime Contractors in accordance with the latest approved Project schedule.

§ 4.2.5 The Construction Manager, except to the extent required by Section 4.2.4, and Architect will not have control over, or charge of, construction means, methods, techniques, sequences or procedures, or for the safety precautions and programs in connection with the Work, since these are solely the Contractor's rights and responsibilities under the Contract Documents, except as provided in Section 3.3.1, and neither will be responsible for the Contractor's failure to perform the Work in accordance with the requirements of the Contract Documents. Neither the Construction Manager nor the Architect will have control over or charge of or be responsible for acts or omissions of the Contractor, Subcontractors, or their agents or employees, or of any other persons or entities performing portions of the Work.

§ 4.2.6 **Communications Facilitating Contract Administration.** Except as otherwise provided in the Contract Documents or when direct communications have been specially authorized, the Owner and Contractor shall endeavor to communicate with each other through the Construction Manager, and shall contemporaneously provide the same communications to the Architect about matters arising out of or relating to the Contract Documents. Communications by and with the Architect's consultants shall be through the Architect. Communications by and with Subcontractors and material suppliers shall be through the Contractor. Communications by and with other Multiple Prime Contractors shall be through the Construction Manager and shall be contemporaneously provided to the Architect if those communications are about matters arising out of or related to the Contract Documents. Communications by and with the Owner's own forces shall be through the Owner.

§ 4.2.7 The Construction Manager and Architect will review and certify all Applications for Payment by the Contractor, in accordance with the provisions of Article 9.

§ 4.2.8 The Architect and Construction Manager have authority to reject Work that does not conform to the Contract Documents and will notify each other about the rejection. The Construction Manager shall determine in general whether the Work of the Contractor is being performed in accordance with the requirements of the Contract Documents and notify the Owner, Contractor and Architect of defects and deficiencies in the Work. Whenever the Construction Manager considers it necessary or advisable, the Construction Manager will have authority to require additional inspection or testing of the Work in accordance with Sections 13.5.2 and 13.5.3, upon written authorization of the Owner, whether or not such Work is fabricated, installed or completed. The foregoing authority of the Construction Manager will be subject to the provisions of Sections 4.2.18 through 4.2.20 inclusive, with respect to interpretations and decisions of the Architect. However, neither the Architect's nor the Construction Manager's authority to act under this Section 4.2.8 nor a decision made by either of them in good faith either to exercise or not to exercise such authority shall give rise to a duty or responsibility of the Architect or the Construction Manager to the Contractor, Subcontractors, material and equipment suppliers, their agents or employees, or other persons performing any of the Work.

§ 4.2.9 The Construction Manager will receive and promptly review for conformance with the submittal requirements of the Contract Documents, all submittals from the Contractor such as Shop Drawings, Product Data and Samples. Where there are Multiple Prime Contractors, the Construction Manager will also check and coordinate the information contained within each submittal received from Contractor and other Multiple Prime Contractors, and transmit to the Architect those recommended for approval. By submitting Shop Drawings, Product Data, Samples and similar submittals, the Construction Manager represents to the Owner and Architect that the Construction Manager has reviewed and recommended them for approval. The Construction Manager's actions will be taken in accordance with the Project submittal schedule approved by the Architect or, in the absence of an approved Project submittal schedule, with reasonable promptness while allowing sufficient time to permit adequate review by the Architect.

§ 4.2.10 The Architect will review and approve or take other appropriate action upon the Contractor's submittals such as Shop Drawings, Product Data and Samples, but only for the limited purpose of checking for conformance with information given and the design concept expressed in the Contract Documents. The Architect's action will be taken in accordance with the submittal schedule approved by the Architect or, in the absence of an approved submittal schedule, with reasonable promptness while allowing sufficient time in the Architect's professional judgment to permit adequate review. Upon the Architect's completed review, the Architect shall transmit its submittal review to the Construction Manager.

§ 4.2.11 Review of the Contractor's submittals by the Construction Manager and Architect is not conducted for the purpose of determining the accuracy and completeness of other details such as dimensions and quantities, or for substantiating instructions for installation or performance of equipment or systems, all of which remain the responsibility of the Contractor as required by the Contract Documents. The Construction Manager and Architect's review of the Contractor's submittals shall not relieve the Contractor of the obligations under Sections 3.3, 3.5 and 3.12. The Construction Manager and Architect's review shall not constitute approval of safety precautions or, unless otherwise specifically stated by the Construction Manager and Architect, of any construction means, methods, techniques, sequences or procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component.

§ 4.2.12 The Construction Manager will prepare Change Orders and Construction Change Directives.

§ 4.2.13 The Construction Manager and the Architect will take appropriate action on Change Orders or Construction Change Directives in accordance with Article 7. and the Architect will have authority to order minor changes in the Work as provided in Section 7.4. The Architect, in consultation with the Construction Manager, will investigate and make determinations and recommendations regarding concealed and unknown conditions as provided in Section 3.7.4.

§ 4.2.14 Utilizing the documents provided by the Contractor, the Construction Manager will maintain at the site for the Owner one copy of all Contract Documents, approved Shop Drawings, Product Data, Samples and similar

required submittals, in good order and marked currently to record all changes and selections made during construction. These will be available to the Architect and the Contractor, and will be delivered to the Owner upon completion of the Project.

§ 4.2.15 The Construction Manager will assist the Architect in conducting inspections to determine the dates of Substantial Completion and the date of final completion; issue Certificates of Substantial Completion in conjunction with the Architect pursuant to Section 9.8; and receive and forward to the Owner written warranties and related documents required by the Contract and assembled by the Contractor pursuant to Section 9.10. The Construction Manager will forward to the Architect a final Application and Certificate for Payment or final Project Application and Project Certificate for Payment upon the Contractor's compliance with the requirements of the Contract Documents.

§ 4.2.16 If the Owner and Architect agree, the Architect will provide one or more project representatives to assist in carrying out the Architect's responsibilities at the site. The duties, responsibilities and limitations of authority of such project representatives shall be as set forth in an exhibit to be incorporated in the Contract Documents.

§ 4.2.17 The Architect will interpret and decide matters concerning performance under, and requirements of the Contract Documents on written request of the Construction Manager, Owner or Contractor through the Construction Manager. The Architect's response to such requests will be made in writing within any time limits agreed upon or otherwise with reasonable promptness.

§ 4.2.18 Interpretations and decisions of the Architect will be consistent with the intent of and reasonably inferable from the Contract Documents and will be in writing or in the form of drawings. When making such interpretations and decisions, the Architect will endeavor to secure faithful performance by both Owner and Contractor, will not show partiality to either and will not be liable for results of interpretations or decisions so rendered in good faith.

§ 4.2.19 The Architect's decisions on matters relating to aesthetic effect will be final if consistent with the intent expressed in the Contract Documents.

§ 4.2.20 The Construction Manager will receive and review requests for information from the Contractor, and forward each request for information to the Architect, with the Construction Manager's recommendation. The Architect will review and respond in writing to the Construction Manager to requests for information about the Contract Documents. The Construction Manager's recommendation and the Architect's response to each request will be made in writing within any time limits agreed upon or otherwise with reasonable promptness. If appropriate, the Architect will prepare and issue supplemental Drawings and Specifications in response to the requests for information.

ARTICLE 5 SUBCONTRACTORS

§ 5.1 Definitions

§ 5.1.1 A Subcontractor is a person or entity who has a direct contract with the Contractor to perform a portion of the Work at the site. The term "Subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Subcontractor or an authorized representative of the Subcontractor. The term "Subcontractor" does not include other Multiple Prime Contractors or subcontractors of other Multiple Prime Contractors.

§ 5.1.2 A Sub-subcontractor is a person or entity who has a direct or indirect contract with a Subcontractor to perform a portion of the Work at the site. The term "Sub-subcontractor" is referred to throughout the Contract Documents as if singular in number and means a Sub-subcontractor or an authorized representative of the Sub-subcontractor.

§ 5.2 Award of Subcontracts and Other Contracts for Portions of the Work

§ 5.2.1 Unless otherwise stated in the Contract Documents or the bidding requirements, the Contractor, as soon as practicable after award of the Contract, shall furnish in writing to the Construction Manager for review by the Owner, Construction Manager and Architect the names of persons or entities (including those who are to furnish materials or equipment fabricated to a special design) proposed for each principal portion of the Work. The Construction Manager may reply within 14 days to the Contractor in writing stating (1) whether the Owner, the Construction Manager or the Architect has reasonable objection to any such proposed person or entity or, (2) that the

Construction Manager, Architect or Owner requires additional time for review. Failure of the Construction Manager, Owner, or Architect to reply within the 14-day period shall constitute notice of no reasonable objection.

§ 5.2.2 The Contractor shall not contract with a proposed person or entity to whom the Owner, Construction Manager or Architect has made reasonable and timely objection. The Contractor shall not be required to contract with anyone to whom the Contractor has made reasonable objection.

§ 5.2.3 If the Owner, Construction Manager or Architect has reasonable objection to a person or entity proposed by the Contractor, the Contractor shall propose another to whom the Owner, Construction Manager or Architect has no reasonable objection. If the proposed but rejected Subcontractor was reasonably capable of performing the Work, the Contract Sum and Contract Time shall be increased or decreased by the difference, if any, occasioned by such change, and an appropriate Change Order shall be issued before commencement of the substitute Subcontractor's Work. However, no increase in the Contract Sum or Contract Time shall be allowed for such change unless the Contractor has acted promptly and responsively in submitting names as required.

§ 5.2.4 The Contractor shall not substitute a Subcontractor, person or entity previously selected if the Owner, Construction Manager or Architect makes reasonable objection to such substitution.

§ 5.3 Subcontractual Relations

By appropriate agreement, written where legally required for validity, the Contractor shall require each Subcontractor, to the extent of the Work to be performed by the Subcontractor, to be bound to the Contractor by terms of the Contract Documents, and to assume toward the Contractor all the obligations and responsibilities, including responsibility for safety of the Subcontractor's Work, which the Contractor, by these Documents, assumes toward the Owner, Construction Manager and Architect. Each subcontract agreement shall preserve and protect the rights of the Owner, Construction Manager and Architect under the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights, and shall allow to the Subcontractor, unless specifically provided otherwise in the subcontract agreement, the benefit of all rights, remedies and redress against the Contractor that the Contractor, by the Contract Documents, has against the Owner. Where appropriate, the Contractor shall require each Subcontractor to enter into similar agreements with Sub-subcontractors. The Contractor shall make available to each proposed Subcontractor, prior to the execution of the subcontract agreement, copies of the Contract Documents to which the Subcontractor will be bound, and, upon written request of the Subcontractor, identify to the Subcontractor terms and conditions of the proposed subcontract agreement that may be at variance with the Contract Documents. Subcontractors will similarly make copies of applicable portions of such documents available to their respective proposed Sub-subcontractors.

§ 5.4 Contingent Assignment of Subcontracts

§ 5.4.1 Each subcontract agreement for a portion of the Work is assigned by the Contractor to the Owner, provided that

- .1 assignment is effective only after termination of the Contract by the Owner for cause pursuant to Section 14.2 and only for those subcontract agreements that the Owner accepts by notifying the Subcontractor and Contractor in writing; and
- .2 assignment is subject to the prior rights of the surety, if any, obligated under bond relating to the Contract.

When the Owner accepts the assignment of a subcontract agreement, the Owner assumes the Contractor's rights and obligations under the subcontract.

§ 5.4.2 Upon such assignment, if the Work has been suspended for more than 30 days, the Subcontractor's compensation shall be equitably adjusted for increases in cost resulting from the suspension.

§ 5.4.3 Upon such assignment to the Owner under this Section 5.4, the Owner may further assign the subcontract to a successor Contractor or other entity. If the Owner assigns the subcontract to a successor Contractor or other entity, the Owner shall nevertheless remain legally responsible for all of the successor Contractor's obligations under the subcontract.

ARTICLE 6 CONSTRUCTION BY OWNER OR BY OTHER CONTRACTORS

§ 6.1 Owner's Right to Perform Construction with Own Forces and to Award Other Contracts

§ 6.1.1 The Owner reserves the right to perform construction or operations related to the Project with the Owner's own forces, which include persons or entities under separate contracts not administered by the Construction Manager, and to award other contracts in connection with other portions of the Project or other construction or operations on the site under Conditions of the Contract identical or substantially similar to these including those portions related to insurance and waiver of subrogation. If the Contractor claims that delay or additional cost is involved because of such action by the Owner, the Contractor shall make such Claim as provided in Article 15.

§ 6.1.2 When the Owner performs construction or operations with the Owner's own forces including persons or entities under separate contracts not administered by the Construction Manager, the Owner shall provide for coordination of such forces with the Work of the Contractor, who shall cooperate with them.

§ 6.1.3 Unless otherwise provided in the Contract Documents, when the Owner performs construction or operations related to the Project with the Owner's own forces, the Owner shall be deemed to be subject to the same obligations and to have the same rights that apply to the Contractor under the Conditions of the Contract, including, without excluding others, those stated in Article 3, this Article 6, and Articles 10, 11 and 12.

§ 6.2 Mutual Responsibility

§ 6.2.1 The Contractor shall afford the Owner's own forces, Construction Manager and other Multiple Prime Contractors reasonable opportunity for introduction and storage of their materials and equipment and performance of their activities, and shall connect and coordinate the Contractor's construction and operations with theirs as required by the Contract Documents.

§ 6.2.2 If part of the Contractor's Work depends for proper execution or results upon construction or operations by the Owner's own forces or other Multiple Prime Contractors, the Contractor shall, prior to proceeding with that portion of the Work, promptly report to the Construction Manager and Architect apparent discrepancies or defects in such other construction that would render it unsuitable for such proper execution and results. Failure of the Contractor so to report shall constitute an acknowledgment that the Owner's own forces or other Multiple Prime Contractors' completed or partially completed construction is fit and proper to receive the Contractor's Work, except as to defects not then reasonably discoverable.

§ 6.2.3 The Contractor shall reimburse the Owner for costs the Owner incurs, including costs that are payable to a separate contractor or to other Multiple Prime Contractors because of the Contractor's delays, improperly timed activities or defective construction. The Owner shall be responsible to the Contractor for costs the Contractor incurs because of delays, improperly timed activities, damage to the Work or defective construction by the Owner's own forces or other Multiple Prime Contractors.

§ 6.2.4 The Contractor shall promptly remedy damage the Contractor wrongfully causes to completed or partially completed construction or to property of the Owner, separate contractors, or other Multiple Prime Contractors as provided in Section 10.2.5.

§ 6.2.5 The Owner and other Multiple Prime Contractors shall have the same responsibilities for cutting and patching as are described for the Contractor in Section 3.14.

§ 6.3 Owner's Right to Clean Up

If a dispute arises among the Contractor, other Multiple Prime Contractors and the Owner as to the responsibility under their respective contracts for maintaining the premises and surrounding area free from waste materials and rubbish, the Owner may clean up and the Construction Manager, with notice to the Architect, will allocate the cost among those responsible.

ARTICLE 7 CHANGES IN THE WORK

§ 7.1 General

§ 7.1.1 Changes in the Work may be accomplished after execution of the Contract, and without invalidating the Contract, by Change Order, Construction Change Directive or order for a minor change in the Work, subject to the limitations stated in this Article 7 and elsewhere in the Contract Documents.

§ 7.1.2 A Change Order shall be based upon agreement among the Owner, Construction Manager, Architect and Contractor; a Construction Change Directive requires agreement by the Owner, Construction Manager and Architect and may or may not be agreed to by the Contractor; an order for a minor change in the Work may be issued by the Architect alone.

§ 7.1.3 Changes in the Work shall be performed under applicable provisions of the Contract Documents, and the Contractor shall proceed promptly, unless otherwise provided in the Change Order, Construction Change Directive or order for a minor change in the Work.

§ 7.2 Change Orders

A Change Order is a written instrument prepared by the Construction Manager and signed by the Owner, Construction Manager, Architect and Contractor, stating their agreement upon all of the following:

- .1 The change in the Work;
- .2 The amount of the adjustment, if any, in the Contract Sum; and
- .3 The extent of the adjustment, if any, in the Contract Time.

§ 7.3 Construction Change Directives

§ 7.3.1 A Construction Change Directive is a written order prepared by the Construction Manager and signed by the Owner, Construction Manager and Architect, directing a change in the Work prior to agreement on adjustment, if any, in the Contract Sum or Contract Time, or both. The Owner may by Construction Change Directive, without invalidating the Contract, order changes in the Work within the general scope of the Contract consisting of additions, deletions or other revisions, the Contract Sum and Contract Time being adjusted accordingly.

§ 7.3.2 A Construction Change Directive shall be used in the absence of total agreement on the terms of a Change Order.

§ 7.3.3 If the Construction Change Directive provides for an adjustment to the Contract Sum, the adjustment shall be based on one of the following methods:

- .1 Mutual acceptance of a lump sum properly itemized and supported by sufficient substantiating data to permit evaluation;
- .2 Unit prices stated in the Contract Documents or subsequently agreed upon;
- .3 Cost to be determined in a manner agreed upon by the parties and a mutually acceptable fixed or percentage fee; or
- .4 As provided in Section 7.3.7.

§ 7.3.4 If unit prices are stated in the Contract Documents or subsequently agreed upon, and if quantities originally contemplated are materially changed in a proposed Change Order or Construction Change Directive so that application of such unit prices to quantities of Work proposed will cause substantial inequity to the Owner or Contractor, the applicable unit prices shall be equitably adjusted.

§ 7.3.5 Upon receipt of a Construction Change Directive, the Contractor shall promptly proceed with the change in the Work involved and advise the Construction Manager and Architect of the Contractor's agreement or disagreement with the method, if any, provided in the Construction Change Directive for determining the proposed adjustment in the Contract Sum or Contract Time.

§ 7.3.6 A Construction Change Directive signed by the Contractor indicates the Contractor's agreement therewith, including adjustment in Contract Sum and Contract Time or the method for determining them. Such agreement shall be effective immediately and shall be recorded as a Change Order.

§ 7.3.7 If the Contractor does not respond promptly or disagrees with the method for adjustment in the Contract Sum, the Construction Manager shall determine the method and the adjustment on the basis of reasonable expenditures and savings of those performing the Work attributable to the change, including, in case of an increase in the Contract Sum, an amount for overhead and profit as set forth in the Agreement, or if no such amount is set forth in the Agreement, a reasonable amount. In such case, and also under Section 7.3.3.3, the Contractor shall keep and present, in such form as the Construction Manager may prescribe, an itemized accounting together with appropriate supporting data. Unless otherwise provided in the Contract Documents, costs for the purposes of this Section 7.3.7 shall be limited to the following:

- .1 Costs of labor, including social security, old age and unemployment insurance, fringe benefits required by agreement or custom, and workers compensation insurance;
- .2 Costs of materials, supplies and equipment, including cost of transportation, whether incorporated or consumed;
- .3 Rental costs of machinery and equipment, exclusive of hand tools, whether rented from the Contractor or others;
- .4 Costs of premiums for all bonds and insurance, permit fees, and sales, use or similar taxes related to the Work; and
- .5 Additional costs of supervision and field office personnel directly attributable to the change.

§ 7.3.8 The amount of credit to be allowed by the Contractor to the Owner for a deletion or change that results in a net decrease in the Contract Sum shall be actual net cost as confirmed by the Construction Manager and Architect. When both additions and credits covering related Work or substitutions are involved in a change, the allowance for overhead and profit shall be figured on the basis of net increase, if any, with respect to that change.

§ 7.3.9 Pending final determination of the total cost of a Construction Change Directive to the Owner, the Contractor may request payment for Work completed under the Construction Change Directive in Applications for Payment. The Construction Manager and Architect will make an interim determination for purposes of monthly certification for payment for those costs and certify for payment the amount that the Construction Manager and Architect determine to be reasonably justified. The interim determination of cost shall adjust the Contract Sum on the same basis as a Change Order, subject to the right of either party to disagree and assert a Claim in accordance with Article 15.

§ 7.3.10 When the Owner and Contractor agree with a determination made by the Construction Manager and Architect concerning the adjustments in the Contract Sum and Contract Time, or otherwise reach agreement upon the adjustments, such agreement shall be effective immediately and the Construction Manager shall prepare a Change Order. Change Orders may be issued for all or any part of a Construction Change Directive.

§ 7.4 Minor Changes in the Work

The Architect has authority to order minor changes in the Work not involving adjustment in the Contract Sum or extension of the Contract Time and not inconsistent with the intent of the Contract Documents. Such changes will be effected by written order issued through the Construction Manager and shall be binding on the Owner and Contractor.

ARTICLE 8 TIME

§ 8.1 Definitions

§ 8.1.1 Unless otherwise provided, Contract Time is the period of time, including authorized adjustments, allotted in the Contract Documents for Substantial Completion of the Work.

§ 8.1.2 The date of commencement of the Work is the date established in the Agreement.

§ 8.1.3 The date of Substantial Completion is the date certified by the Architect in accordance with Section 9.8.

§ 8.1.4 The term “day” as used in the Contract Documents shall mean calendar day unless otherwise specifically defined.

§ 8.2 Progress and Completion

§ 8.2.1 Time limits stated in the Contract Documents are of the essence of the Contract. By executing the Agreement the Contractor confirms that the Contract Time is a reasonable period for performing the Work.

§ 8.2.2 The Contractor shall not knowingly, except by agreement or instruction of the Owner in writing, prematurely commence operations on the site or elsewhere prior to the effective date of insurance required by Article 11 to be furnished by the Contractor and Owner. The date of commencement of the Work shall not be changed by the effective date of such insurance.

§ 8.2.3 The Contractor shall proceed expeditiously with adequate forces and shall achieve Substantial Completion within the Contract Time.

§ 8.3 Delays and Extensions of Time

§ 8.3.1 If the Contractor is delayed at any time in the commencement or progress of the Work by an act or neglect of the Owner, Owner's own forces, Construction Manager, Architect, any of the other Multiple Prime Contractors or an employee of any of them, or by changes ordered in the Work, or by labor disputes, fire, unusual delay in deliveries, unavoidable casualties or other causes beyond the Contractor's control; or by delay authorized by the Owner pending mediation and arbitration, or by other causes that the Architect, based on the recommendation of the Construction Manager, determines may justify delay, then the Contract Time shall be extended by Change Order for such reasonable time as the Architect may determine.

§ 8.3.2 Claims relating to time shall be made in accordance with applicable provisions of Article 15.

§ 8.3.3 This Section 8.3 does not preclude recovery of damages for delay by either party under other provisions of the Contract Documents.

ARTICLE 9 PAYMENTS AND COMPLETION

§ 9.1 Contract Sum

The Contract Sum is stated in the Agreement and, including authorized adjustments, is the total amount payable by the Owner to the Contractor for performance of the Work under the Contract Documents.

§ 9.2 Schedule of Values

Where the Contract is based on a Stipulated Sum or Guaranteed Maximum Price, the Contractor shall submit to the Construction Manager, before the first Application for Payment, a schedule of values allocating the entire Contract Sum to the various portions of the Work and prepared in such form and supported by such data to substantiate its accuracy as the Construction Manager and Architect may require. This schedule, unless objected to by the Construction Manager or Architect, shall be used as a basis for reviewing the Contractor's Applications for Payment. In the event there is one Contractor, the Construction Manager shall forward to the Architect the Contractor's schedule of values. If there are Multiple Prime Contractors responsible for performing different portions of the Project, the Construction Manager shall forward the Multiple Prime Contractors' schedules of values only if requested by the Architect.

§ 9.3 Applications for Payment

§ 9.3.1 At least fifteen days before the date established for each progress payment, the Contractor shall submit to the Construction Manager an itemized Application for Payment prepared in accordance with the schedule of values, if required under Section 9.2, for completed portions of the Work. Such application shall be notarized, if required, and supported by such data substantiating the Contractor's right to payment as the Owner, Construction Manager or Architect may require, such as copies of requisitions from Subcontractors and material suppliers, and shall reflect retainage if provided for in the Contract Documents.

§ 9.3.1.1 As provided in Section 7.3.9, such applications may include requests for payment on account of changes in the Work that have been properly authorized by Construction Change Directives, or by interim determinations of the Construction Manager and Architect, but not yet included in Change Orders.

§ 9.3.1.2 Applications for Payment shall not include requests for payment for portions of the Work for which the Contractor does not intend to pay a Subcontractor or material supplier unless such Work has been performed by others whom the Contractor intends to pay.

§ 9.3.2 Unless otherwise provided in the Contract Documents, payments shall be made on account of materials and equipment delivered and suitably stored at the site for subsequent incorporation in the Work. If approved in advance by the Owner, payment may similarly be made for materials and equipment suitably stored off the site at a location agreed upon in writing. Payment for materials and equipment stored on or off the site shall be conditioned upon compliance by the Contractor with procedures satisfactory to the Owner to establish the Owner's title to such materials and equipment or otherwise protect the Owner's interest, and shall include the costs of applicable insurance, storage and transportation to the site for such materials and equipment stored off the site.

§ 9.3.3 The Contractor warrants that title to all Work covered by an Application for Payment will pass to the Owner no later than the time of payment. The Contractor further warrants that upon submittal of an Application for

Payment all Work for which Certificates for Payment have been previously issued and payments received from the Owner shall, to the best of the Contractor's knowledge, information and belief, be free and clear of liens, claims, security interests or encumbrances in favor of the Contractor, Subcontractors, material suppliers, or other persons or entities making a claim by reason of having provided labor, materials and equipment relating to the Work.

§ 9.4 Certificates for Payment

§ 9.4.1 Where there is only one Contractor, the Construction Manager will, within seven days after the Construction Manager's receipt of the Contractor's Application for Payment, review the Application, certify the amount the Construction Manager determines is due the Contractor, and forward the Contractor's Application and Certificate for Payment to the Architect. Within seven days after the Architect receives the Contractor's Application for Payment from the Construction Manager, the Architect will either issue to the Owner a Certificate for Payment, with a copy to the Construction Manager, for such amount as the Architect determines is properly due, or notify the Construction Manager and Owner in writing of the Architect's reasons for withholding certification in whole or in part as provided in Section 9.5.1. The Construction Manager will promptly forward to the Contractor the Architect's notice of withholding certification.

§ 9.4.2 Where there are Multiple Prime Contractors performing portions of the Project, the Construction Manager will, within seven days after the Construction Manager receives the Multiple Prime Contractors' Applications for Payment: (1) review the Applications and certify the amount the Construction Manager determines is due each of the Multiple Prime Contractors; (2) prepare a Summary of Contractors' Applications for Payment by combining information from each Multiple Prime Contractors' application with information from similar applications for progress payments from other Multiple Prime Contractors; (3) prepare a Project Application and Certificate for Payment; (4) certify the amount the Construction Manager determines is due all Multiple Prime Contractors; and (5) forward the Summary of Contractors' Applications for Payment and Project Application and Certificate for Payment to the Architect.

§ 9.4.3 Within seven days after the Architect receives the Project Application and Project Certificate for Payment and the Summary of Contractors' Applications for Payment from the Construction Manager, the Architect will either issue to the Owner a Project Certificate for Payment, with a copy to the Construction Manager, for such amount as the Architect determines is properly due, or notify the Construction Manager and Owner in writing of the Architect's reasons for withholding certification in whole or in part as provided in Section 9.5.1. The Construction Manager will promptly forward the Architect's notice of withholding certification to the Contractors.

§ 9.4.4 The Construction Manager's certification of an Application for Payment or, in the case of Multiple Prime Contractors, a Project Application and Certificate for Payment shall be based upon the Construction Manager's evaluation of the Work and the information provided as part of the Application for Payment. The Construction Manager's certification will constitute a representation that, to the best of the Construction Manager's knowledge, information and belief, the Work has progressed to the point indicated and the quality of the Work is in accordance with the Contract Documents. The certification will also constitute a recommendation to the Architect and Owner that the Contractor be paid the amount certified.

§ 9.4.5 The Architect's issuance of a Certificate for Payment or in the case of Multiple Prime Contractors, Project Application and Certificate for Payment, shall be based upon the Architect's evaluation of the Work, the recommendation of the Construction Manager, and information provided as part of the Application for Payment or Project Application for Payment. The Architect's certification will constitute a representation that, to the best of the Architect's knowledge, information and belief, the Work has progressed to the point indicated, that the quality of the Work is in accordance with the Contract Documents, and that the Contractor is entitled to payment in the amount certified.

§ 9.4.6 The representations made pursuant to Sections 9.4.4 and 9.4.5 are subject to an evaluation of the Work for conformance with the Contract Documents upon Substantial Completion, to results of subsequent tests and inspections, to correction of minor deviations from the Contract Documents prior to completion and to specific qualifications expressed by the Construction Manager or Architect.

§ 9.4.7 The issuance of a separate Certificate for Payment or a Project Certificate for Payment will not be a representation that the Construction Manager or Architect has (1) made exhaustive or continuous on-site inspections to check the quality or quantity of the Work, (2) reviewed the Contractor's construction means, methods, techniques,

sequences or procedures, (3) reviewed copies of requisitions received from Subcontractors and material suppliers and other data requested by the Owner to substantiate the Contractor's right to payment or (4) made examination to ascertain how or for what purpose the Contractor has used money previously paid on account of the Contract Sum.

§ 9.5 Decisions to Withhold Certification

§ 9.5.1 The Construction Manager or Architect may withhold a Certificate for Payment or Project Certificate for Payment in whole or in part, to the extent reasonably necessary to protect the Owner, if in the Construction Manager's or Architect's opinion the representations to the Owner required by Section 9.4.4 and 9.4.5 cannot be made. If the Construction Manager or Architect is unable to certify payment in the amount of the Application, the Construction Manager will notify the Contractor and Owner as provided in Section 9.4.1 and 9.4.3. If the Contractor, Construction Manager and Architect cannot agree on a revised amount, the Architect will promptly issue a Certificate for Payment or a Project Certificate for Payment for the amount for which the Architect is able to make such representations to the Owner. The Construction Manager or Architect may also withhold a Certificate for Payment or, because of subsequently discovered evidence or subsequent observations, may nullify the whole or a part of a Certificate for Payment or Project Certificate for Payment previously issued, to such extent as may be necessary in the Construction Manager's or Architect's opinion to protect the Owner from loss for which the Contractor is responsible, including loss resulting from the acts and omissions described in Section 3.3.2 because of

- .1 defective Work not remedied;
- .2 third party claims filed or reasonable evidence indicating probable filing of such claims unless security acceptable to the Owner is provided by the Contractor;
- .3 failure of the Contractor to make payments properly to Subcontractors or for labor, materials or equipment;
- .4 reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract Sum;
- .5 damage to the Owner or a separate contractor;
- .6 reasonable evidence that the Work will not be completed within the Contract Time, and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay; or
- .7 repeated failure to carry out the Work in accordance with the Contract Documents.

§ 9.5.2 When the above reasons for withholding certification are removed, certification will be made for amounts previously withheld.

§ 9.5.3 If the Architect or Construction Manager withholds certification for payment under Section 9.5.1, the Owner may, at its sole option, issue joint checks to the Contractor and to any Subcontractor or material or equipment suppliers to whom the Contractor failed to make payment for Work properly performed or material or equipment suitably delivered. If the Owner makes payments by joint check, the Owner shall notify the Architect and the Construction Manager and both will reflect such payment on the next Certificate for Payment.

§ 9.6 Progress Payments

§ 9.6.1 After the Architect has issued a Certificate for Payment or Project Certificate for Payment, the Owner shall make payment in the manner and within the time provided in the Contract Documents, and shall so notify the Construction Manager and Architect.

§ 9.6.2 The Contractor shall pay each Subcontractor, no later than seven days after receipt of payment from the Owner the amount to which the Subcontractor is entitled, reflecting percentages actually retained from payments to the Contractor on account of the Subcontractor's portion of the Work. The Contractor shall, by appropriate agreement with each Subcontractor, require each Subcontractor to make payments to Sub-subcontractors in a similar manner.

§ 9.6.3 The Construction Manager will, on request, furnish to a Subcontractor, if practicable, information regarding percentages of completion or amounts applied for by the Contractor and action taken thereon by the Owner, Construction Manager and Architect on account of portions of the Work done by such Subcontractor.

§ 9.6.4 The Owner has the right to request written evidence from the Contractor that the Contractor has properly paid Subcontractors and material and equipment suppliers amounts paid by the Owner to the Contractor for subcontracted Work. If the Contractor fails to furnish such evidence within seven days, the Owner shall have the right to contact Subcontractors to ascertain whether they have been properly paid. Neither the Owner, Construction Manager nor

Architect shall have an obligation to pay or to see to the payment of money to a Subcontractor except as may otherwise be required by law.

§ 9.6.5 Contractor payments to material and equipment suppliers shall be treated in a manner similar to that provided in Sections 9.6.2, 9.6.3 and 9.6.4.

§ 9.6.6 A Certificate for Payment, a progress payment, or partial or entire use or occupancy of the Project by the Owner shall not constitute acceptance of Work not in accordance with the Contract Documents.

§ 9.6.7 Unless the Contractor provides the Owner with a payment bond in the full penal sum of the Contract Sum, payments received by the Contractor for Work properly performed by Subcontractors and suppliers shall be held by the Contractor for those Subcontractors or suppliers who performed Work or furnished materials, or both, under contract with the Contractor for which payment was made by the Owner. Nothing contained herein shall require money to be placed in a separate account and not commingled with money of the Contractor, shall create any fiduciary liability or tort liability on the part of the Contractor for breach of trust or shall entitle any person or entity to an award of punitive damages against the Contractor for breach of the requirements of this provision.

§ 9.7 Failure of Payment

If the Construction Manager and Architect do not issue a Certificate for Payment or a Project Certificate for Payment, through no fault of the Contractor, within fourteen days after the Construction Manager's receipt of the Contractor's Application for Payment, or if the Owner does not pay the Contractor within seven days after the date established in the Contract Documents the amount certified by the Construction Manager and Architect or awarded by binding dispute resolution, then the Contractor may, upon seven additional days' written notice to the Owner, Construction Manager and Architect, stop the Work until payment of the amount owing has been received. The Contract Time shall be extended appropriately and the Contract Sum shall be increased by the amount of the Contractor's reasonable costs of shut-down, delay and start-up, plus interest as provided for in the Contract Documents.

§ 9.8 Substantial Completion

§ 9.8.1 Substantial Completion is the stage in the progress of the Work when the Work or designated portion thereof is sufficiently complete in accordance with the Contract Documents so the Owner can occupy or utilize the Work for its intended use.

§ 9.8.2 When the Contractor considers that the Work, or a portion thereof which the Owner agrees to accept separately, is substantially complete, the Contractor shall notify the Construction Manager, and the Contractor and Construction Manager shall jointly prepare and submit to the Architect a comprehensive list of items to be completed or corrected prior to final payment. Failure to include an item on such list does not alter the responsibility of the Contractor to complete all Work in accordance with the Contract Documents.

§ 9.8.3 Upon receipt of the list, the Architect, assisted by the Construction Manager, will make an inspection to determine whether the Work or designated portion thereof is substantially complete. If the Architect's inspection discloses any item, whether or not included on the list, which is not sufficiently complete in accordance with the requirements of the Contract Documents so that the Owner can occupy or utilize the Work or designated portion thereof for its intended use, the Contractor shall, before issuance of the Certificate of Substantial Completion, complete or correct such item upon notification by the Architect. In such case, the Contractor shall then submit a request for another inspection by the Architect, assisted by the Construction Manager, to determine Substantial Completion.

§ 9.8.4 When the Architect, assisted by the Construction Manager, determines that the Work or designated portion thereof is substantially complete, the Construction Manager will prepare, and the Construction Manager and Architect shall execute a Certificate of Substantial Completion that shall establish the date of Substantial Completion, shall establish responsibilities of the Owner and Contractor for security, maintenance, heat, utilities, damage to the Work and insurance, and shall fix the time within which the Contractor shall finish all items on the list accompanying the Certificate. Warranties required by the Contract Documents shall commence on the date of Substantial Completion of the Work or designated portion thereof unless otherwise provided in the Certificate of Substantial Completion.

§ 9.8.5 The Certificate of Substantial Completion shall be submitted to the Owner and Contractor for their written acceptance of responsibilities assigned to them in such Certificate. Upon such acceptance and consent of surety, if any, the Owner shall make payment of retainage applying to such Work or designated portion thereof. Such payment shall be adjusted for Work that is incomplete or not in accordance with the requirements of the Contract Documents.

§ 9.9 Partial Occupancy or Use

§ 9.9.1 The Owner may occupy or use any completed or partially completed portion of the Work at any stage when such portion is designated by separate agreement with the Contractor, provided such occupancy or use is consented to by the insurer as required under Section 11.3.1.5 and authorized by public authorities having jurisdiction over the Project. Such partial occupancy or use may commence whether or not the portion is substantially complete, provided the Owner and Contractor have accepted in writing the responsibilities assigned to each of them for payments, retainage if any, security, maintenance, heat, utilities, damage to the Work and insurance, and have agreed in writing concerning the period for correction of the Work and commencement of warranties required by the Contract Documents. When the Contractor considers a portion substantially complete, the Contractor and Construction Manager shall jointly prepare and submit a list to the Architect as provided under Section 9.8.2. Consent of the Contractor to partial occupancy or use shall not be unreasonably withheld. The stage of the progress of the Work shall be determined by written agreement between the Owner and Contractor or, if no agreement is reached, by decision of the Architect after consultation with the Construction Manager.

§ 9.9.2 Immediately prior to such partial occupancy or use, the Owner, Construction Manager, Contractor and Architect shall jointly inspect the area to be occupied or portion of the Work to be used in order to determine and record the condition of the Work.

§ 9.9.3 Unless otherwise agreed upon, partial occupancy or use of a portion or portions of the Work shall not constitute acceptance of Work not complying with the requirements of the Contract Documents.

§ 9.10 Final Completion and Final Payment

§ 9.10.1 Upon completion of the Work, the Contractor shall forward to the Construction Manager a written notice that the Work is ready for final inspection and acceptance and shall also forward to the Construction Manager a final Contractor's Application for Payment. Upon receipt, the Construction Manager will evaluate the completion of Work of the Contractor and then forward the notice and Application, with the Construction Manager's recommendations, to the Architect who will promptly make such inspection. When the Architect, finds the Work acceptable under the Contract Documents and the Contract fully performed, the Construction Manager and Architect will promptly issue a final Certificate for Payment or Project Certificate for Payment stating that to the best of their knowledge, information and belief, and on the basis of their on-site visits and inspections, the Work has been completed in accordance with terms and conditions of the Contract Documents and that the entire balance found to be due the Contractor and noted in the final Certificate is due and payable. The Construction Manager's and Architect's final Certificate for Payment or Project Certificate for Payment will constitute a further representation that conditions listed in Section 9.10.2 as precedent to the Contractor's being entitled to final payment have been fulfilled.

§ 9.10.2 Neither final payment nor any remaining retained percentage shall become due until the Contractor submits to the Architect through the Construction Manager (1) an affidavit that payrolls, bills for materials and equipment, and other indebtedness connected with the Work for which the Owner or the Owner's property might be responsible or encumbered (less amounts withheld by Owner) have been paid or otherwise satisfied, (2) a certificate evidencing that insurance required by the Contract Documents to remain in force after final payment is currently in effect and will not be canceled or allowed to expire until at least 30 days' prior written notice has been given to the Owner, (3) a written statement that the Contractor knows of no substantial reason that the insurance will not be renewable to cover the period required by the Contract Documents, (4) consent of surety, if any, to final payment and (5), if required by the Owner, other data establishing payment or satisfaction of obligations, such as receipts, releases and waivers of liens, claims, security interests or encumbrances arising out of the Contract, to the extent and in such form as may be designated by the Owner. If a Subcontractor refuses to furnish a release or waiver required by the Owner, the Contractor may furnish a bond satisfactory to the Owner to indemnify the Owner against such lien. If such lien remains unsatisfied after payments are made, the Contractor shall refund to the Owner all money that the Owner may be compelled to pay in discharging such lien, including all costs and reasonable attorneys' fees.

§ 9.10.3 If, after Substantial Completion of the Work, final completion thereof is materially delayed through no fault of the Contractor or by issuance of Change Orders affecting final completion, and the Construction Manager and Architect so confirm, the Owner shall, upon application by the Contractor and certification by the Construction Manager and Architect, and without terminating the Contract, make payment of the balance due for that portion of the Work fully completed and accepted. If the remaining balance for Work not fully completed or corrected is less than retainage stipulated in the Contract Documents, and if bonds have been furnished, the written consent of surety to payment of the balance due for that portion of the Work fully completed and accepted shall be submitted by the Contractor to the Architect through the Construction Manager prior to certification of such payment. Such payment shall be made under terms and conditions governing final payment, except that it shall not constitute a waiver of Claims.

§ 9.10.4 The making of final payment shall constitute a waiver of Claims by the Owner except those arising from

- .1 liens, Claims, security interests or encumbrances arising out of the Contract and unsettled;
- .2 failure of the Work to comply with the requirements of the Contract Documents; or
- .3 terms of special warranties required by the Contract Documents.

§ 9.10.5 Acceptance of final payment by the Contractor, a Subcontractor or material supplier shall constitute a waiver of claims by that payee except those previously made in writing and identified by that payee as unsettled at the time of final Application for Payment.

ARTICLE 10 PROTECTION OF PERSONS AND PROPERTY

§ 10.1 Safety Precautions and Programs

The Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the performance of the Contract. The Contractor shall submit the Contractor's safety program to the Construction Manager for review and coordination with the safety programs of other Contractors.

The Construction Manager's responsibilities for review and coordination of safety programs shall not extend to direct control over or charge of the acts or omissions of the Contractors, Subcontractors, agents or employees of the Contractors or Subcontractors, or any other persons performing portions of the Work and not directly employed by the Construction Manager.

§ 10.2 Safety of Persons and Property

§ 10.2.1 The Contractor shall take reasonable precautions for safety of, and shall provide reasonable protection to prevent damage, injury or loss to

- .1 employees on the Work and other persons who may be affected thereby;
- .2 the Work and materials and equipment to be incorporated therein, whether in storage on or off the site, under care, custody or control of the Contractor or the Contractor's Subcontractors or Sub-subcontractors;
- .3 other property at the site or adjacent thereto, such as trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal, relocation or replacement in the course of construction; and
- .4 construction or operations by the Owner or other Contractors.

§ 10.2.2 The Contractor shall comply with and give notices required by applicable laws, statutes, ordinances, codes, rules and regulations and lawful orders of public authorities bearing on safety of persons or property or their protection from damage, injury or loss.

§ 10.2.3 The Contractor shall erect and maintain, as required by existing conditions and performance of the Contract, reasonable safeguards for safety and protection, including posting danger signs and other warnings against hazards, promulgating safety regulations and notifying owners and users of adjacent sites and utilities.

§ 10.2.4 When use or storage of explosives or other hazardous materials or equipment or unusual methods are necessary for execution of the Work, the Contractor shall exercise utmost care and carry on such activities under supervision of properly qualified personnel.

§ 10.2.5 The Contractor shall promptly remedy damage and loss (other than damage or loss insured under property insurance required by the Contract Documents) to property referred to in Sections 10.2.1.2, 10.2.1.3 and 10.2.1.4 caused in whole or in part by the Contractor, a Subcontractor, a Sub-subcontractor, or anyone directly or indirectly

employed by any of them, or by anyone for whose acts they may be liable and for which the Contractor is responsible under Sections 10.2.1.2, 10.2.1.3 and 10.2.1.4, except damage or loss attributable to acts or omissions of the Owner, Construction Manager or Architect or anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable, and not attributable to the fault or negligence of the Contractor. The foregoing obligations of the Contractor are in addition to the Contractor's obligations under Section 3.18.

§ 10.2.6 The Contractor shall designate a responsible member of the Contractor's organization at the site whose duty shall be the prevention of accidents. This person shall be the Contractor's superintendent unless otherwise designated by the Contractor in writing to the Owner, Construction Manager and Architect.

§ 10.2.7 The Contractor shall not permit any part of the construction or site to be loaded so as to cause damage or create an unsafe condition.

§ 10.2.8 Injury or Damage to Person or Property

If either party suffers injury or damage to person or property because of an act or omission of the other party, or of others for whose acts such party is legally responsible, written notice of such injury or damage, whether or not insured, shall be given to the other party within a reasonable time not exceeding 21 days after discovery. The notice shall provide sufficient detail to enable the other party to investigate the matter.

§ 10.3 Hazardous Materials

§ 10.3.1 The Contractor is responsible for compliance with any requirements included in the Contract Documents regarding hazardous materials. If the Contractor encounters a hazardous material or substance not addressed in the Contract Documents and if reasonable precautions will be inadequate to prevent foreseeable bodily injury or death to persons resulting from a material or substance, including but not limited to, asbestos or polychlorinated biphenyl (PCB), encountered on the site by the Contractor, the Contractor shall, upon recognizing the condition, immediately stop Work in the affected area and report the condition to the Owner, Construction Manager and Architect in writing.

§ 10.3.2 Upon receipt of the Contractor's written notice, the Owner shall obtain the services of a licensed laboratory to verify a presence or absence of the material or substance reported by the Contractor and, in the event such material or substance is found to be present, to cause it to be rendered harmless. Unless otherwise required by the Contract Documents, the Owner shall furnish in writing to the Contractor, Construction Manager and Architect the names and qualifications of persons or entities who are to perform tests verifying the presence or absence of such material or substance or who are to perform the task of removal or safe containment of such material or substance. The Contractor, the Construction Manager and the Architect will promptly reply to the Owner in writing stating whether or not any of them has reasonable objection to the persons or entities proposed by the Owner. If the Contractor, Construction Manager or Architect has an objection to a person or entity proposed by the Owner, the Owner shall propose another to whom the Contractor, the Construction Manager and the Architect have no reasonable objection. When the material or substance has been rendered harmless, Work in the affected area shall resumed upon written agreement of the Owner and Contractor. By Change Order, the Contract Time shall be extended appropriately and the Contract Sum shall be increased in the amount of the Contractor's reasonable additional costs of shut-down, delay and start-up.

§ 10.3.3 To the fullest extent permitted by law, the Owner shall indemnify and hold harmless the Contractor, Subcontractors, Construction Manager, Architect, their consultants, and agents and employees of any of them from and against claims, damages, losses and expenses, including but not limited to attorneys' fees, arising out of or resulting from performance of the Work in the affected area if in fact the material or substance presents the risk of bodily injury or death as described in Section 10.3.1 and has not been rendered harmless, provided that such claim, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property (other than the Work itself), except to the extent that such damage, loss or expense is due to the fault or negligence of the party seeking indemnity.

§ 10.3.4 The Owner shall not be responsible under this Section 10.3 for materials or substances the Contractor brings to the site unless such materials or substances are required by the Contract Documents. The Owner shall be responsible for materials or substances required by the Contract Documents, except to the extent of the Contractor's fault or negligence in the use and handling of such materials or substances.

§ 10.3.5 The Contractor shall indemnify the Owner for the cost and expense the Owner incurs (1) for remediation of a material or substance the Contractor brings to the site and negligently handles, or (2) where the Contractor fails to perform its obligations under Section 10.3.1, except to the extent that the cost and expense are due to the Owner's fault or negligence.

§ 10.3.6 If, without negligence on the part of the Contractor, the Contractor is held liable by a government agency for the cost of remediation of a hazardous material or substance solely by reason of performing Work as required by the Contract Documents, the Owner shall indemnify the Contractor for all cost and expense thereby incurred.

§ 10.4 Emergencies

In an emergency affecting safety of persons or property, the Contractor shall act, at the Contractor's discretion, to prevent threatened damage, injury or loss. Additional compensation or extension of time claimed by the Contractor on account of an emergency shall be determined as provided in Article 15 and Article 7.

ARTICLE 11 INSURANCE AND BONDS

§ 11.1 Contractor's Liability Insurance

§ 11.1.1 The Contractor shall purchase from and maintain in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located such insurance as will protect the Contractor from claims set forth below which may arise out of or result from the Contractor's operations and completed operations under the Contract and for which the Contractor may be legally liable, whether such operations be by the Contractor or by a Subcontractor or by anyone directly or indirectly employed by any of them, or by anyone for whose acts any of them may be liable:

- .1 Claims under workers' compensation, disability benefit and other similar employee benefit acts which are applicable to the Work to be performed;
- .2 Claims for damages because of bodily injury, occupational sickness or disease, or death of the Contractor's employees;
- .3 Claims for damages because of bodily injury, sickness or disease, or death of any person other than the Contractor's employees;
- .4 Claims for damages insured by usual personal injury liability coverage;
- .5 Claims for damages, other than to the Work itself, because of injury to or destruction of tangible property, including loss of use resulting therefrom;
- .6 Claims for damages because of bodily injury, death of a person or property damage arising out of ownership, maintenance or use of a motor vehicle; and
- .7 Claims for bodily injury or property damage arising out of completed operations; and
- .8 Claims involving contractual liability insurance applicable to the Contractor's obligations under Section 3.18.

§ 11.1.2 The insurance required by Section 11.1.1 shall be written for not less than limits of liability specified in the Contract Documents or required by law, whichever coverage is greater. Coverages, whether written on an occurrence or claims-made basis, shall be maintained without interruption from the date of commencement of the Work until the date of final payment and termination of any coverage required to be maintained after final payment and, with respect to the Contractor's completed operations coverage, until the expiration of the period for correction of Work or for such other period for maintenance of completed operations coverage as specified in the Contract Documents.

§ 11.1.3 Certificates of insurance acceptable to the Owner shall be submitted to the Construction Manager for transmittal to the Owner with a copy to the Architect prior to commencement of the Work and thereafter upon renewal or replacement of each required policy of insurance. These certificates and the insurance policies required by this Section 11.1 shall contain a provision that coverages afforded under the policies will not be canceled or allowed to expire until at least 30 days' prior written notice has been given to the Owner. An additional certificate evidencing continuation of liability coverage, including coverage for completed operations, shall be submitted with the final Application for Payment as required by Section 9.10.2 and thereafter upon renewal or replacement of such coverage until the expiration of the time required by Section 11.1.2. Information concerning reduction of coverage shall be furnished by the Contractor with reasonable promptness.

§ 11.1.4 The Contractor shall cause the commercial liability coverage required by the Contract Documents to include (1) the Construction Manager, the Construction Manager's consultants, the Owner, the Architect, and the Architect's

consultants as additional insureds for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's operations; and (2) the Owner as an additional insured for claims caused in whole or in part by the Contractor's negligent acts or omissions during the Contractor's completed operations.

§ 11.2 Owner's Liability Insurance

The Owner shall be responsible for purchasing and maintaining the Owner's usual liability insurance.

§ 11.3 Property Insurance

§ 11.3.1 Unless otherwise provided, the Owner shall purchase and maintain, in a company or companies lawfully authorized to do business in the jurisdiction in which the Project is located, property insurance written on a builder's risk "all risk" or equivalent policy form in the amount of the initial Contract Sum, plus value of subsequent Contract modifications and cost of materials supplied or installed by others, comprising total value for the entire Project at the site on a replacement cost basis without optional deductibles. Such property insurance shall be maintained, unless otherwise provided in the Contract Documents or otherwise agreed in writing by all persons and entities who are beneficiaries of such insurance, until final payment has been made as provided in Section 9.10 or until no person or entity other than the Owner has an insurable interest in the property required by this Section 11.3 to be covered, whichever is later. This insurance shall include interests of the Owner, the Contractor, Subcontractors and Sub-subcontractors in the Project.

§ 11.3.1.1 Property insurance shall be on an "all-risk" or equivalent policy form and shall include, without limitation, insurance against the perils of fire (with extended coverage) and physical loss or damage including, without duplication of coverage, theft, vandalism, malicious mischief, collapse, earthquake, flood, windstorm, falsework, testing and startup, temporary buildings and debris removal including demolition occasioned by enforcement of any applicable legal requirements, and shall cover reasonable compensation for the Architect's, Contractor's, and Construction Manager's services and expenses required as a result of such insured loss.

§ 11.3.1.2 If the Owner does not intend to purchase such property insurance required by the Contract and with all of the coverages in the amount described above, the Owner shall so inform the Contractor in writing prior to commencement of the Work. The Contractor may then effect insurance that will protect the interests of the Contractor, Subcontractors and Sub-subcontractors in the Work, and by appropriate Change Order the cost thereof shall be charged to the Owner. If the Contractor is damaged by the failure or neglect of the Owner to purchase or maintain insurance as described above, without so notifying the Contractor in writing, then the Owner shall bear all reasonable costs properly attributable thereto.

§ 11.3.1.3 If the property insurance requires deductibles, the Owner shall pay costs not covered because of such deductibles.

§ 11.3.1.4 This property insurance shall cover portions of the Work stored off the site, and also portions of the Work in transit.

§ 11.3.1.5 Partial occupancy or use in accordance with Section 9.9 shall not commence until the insurance company or companies providing property insurance have consented to such partial occupancy or use by endorsement or otherwise. The Owner and the Contractor shall take reasonable steps to obtain consent of the insurance company or companies and shall, without mutual written consent, take no action with respect to partial occupancy or use that would cause cancellation, lapse or reduction of insurance.

§ 11.3.2 Boiler and Machinery Insurance. The Owner shall purchase and maintain boiler and machinery insurance required by the Contract Documents or by law, which shall specifically cover such insured objects during installation and until final acceptance by the Owner; this insurance shall include interests of the Owner, Construction Manager, Contractor, Subcontractors and Sub-subcontractors in the Work, and the Owner and Contractor shall be named insureds.

§ 11.3.3 Loss of Use Insurance. The Owner, at the Owner's option, may purchase and maintain such insurance as will insure the Owner against loss of use of the Owner's property due to fire or other hazards, however caused. The Owner waives all rights of action against the Contractor for loss of use of the Owner's property, including consequential losses due to fire or other hazards however caused.

§ 11.3.4 If the Contractor requests in writing that insurance for risks other than those described herein or other special causes of loss be included in the property insurance policy, the Owner shall, if possible, include such insurance, and the cost thereof shall be charged to the Contractor by appropriate Change Order.

§ 11.3.5 If during the Project construction period the Owner insures properties, real or personal or both, adjoining or adjacent to the site by property insurance under policies separate from those insuring the Project, or if after final payment property insurance is to be provided on the completed Project through a policy or policies other than those insuring the Project during the construction period, the Owner shall waive all rights in accordance with the terms of Section 11.3.7 for damages caused by fire or other causes of loss covered by this separate property insurance. All separate policies shall provide this waiver of subrogation by endorsement or otherwise.

§ 11.3.6 Before an exposure to loss may occur, the Owner shall file with the Contractor a copy of each policy that includes insurance coverages required by this Section 11.3. Each policy shall contain all generally applicable conditions, definitions, exclusions and endorsements related to this Project. Each policy shall contain a provision that the policy will not be canceled or allowed to expire, and that its limits will not be reduced, until at least 30 days' prior written notice has been given to the Contractor.

§ 11.3.7 **Waivers of Subrogation.** The Owner and Contractor waive all rights against (1) each other and any of their subcontractors, sub-subcontractors, agents and employees each of the other, and (2) the Construction Manager, Architect, Architect's consultants, separate contractors described in Article 6, if any, and any of their subcontractors, sub-subcontractors, agents and employees, for damages caused by fire or other causes of loss to the extent covered by property insurance obtained pursuant to this Section 11.3 or other property insurance applicable to the Work, except such rights as the Owner and Contractor may have to the proceeds of such insurance held by the Owner as fiduciary. The Owner or Contractor, as appropriate, shall require of the Construction Manager, Construction Manager's consultants, Architect, Architect's consultants, Owner's separate contractors described in Article 6, if any, and the subcontractors, sub-subcontractors, agents and employees of any of them, by appropriate agreements, written where legally required for validity, similar waivers each in favor of other parties enumerated herein. The policies shall provide such waivers of subrogation by endorsement or otherwise. A waiver of subrogation shall be effective as to a person or entity even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, did not pay the insurance premium directly or indirectly, and whether or not the person or entity had an insurable interest in the property damaged.

§ 11.3.8 A loss insured under the Owner's property insurance shall be adjusted by the Owner as fiduciary and made payable to the Owner as fiduciary for the insureds, as their interests may appear, subject to requirements of any applicable mortgagee clause and of Section 11.3.10. The Contractor shall pay Subcontractors their just shares of insurance proceeds received by the Contractor, and by appropriate agreements, written where legally required for validity, shall require Subcontractors to make payments to their Sub-subcontractors in similar manner.

§ 11.3.9 If required in writing by a party in interest, the Owner as fiduciary shall, upon occurrence of an insured loss, give bond for proper performance of the Owner's duties. The cost of required bonds shall be charged against proceeds received as fiduciary. The Owner shall deposit in a separate account proceeds so received, which the Owner shall distribute in accordance with such agreement as the parties in interest may reach, or as determined in accordance with the method of binding dispute resolution selected in the Agreement between the Owner and Contractor. If after such loss no other special agreement is made and unless the Owner terminates the Contract for convenience, replacement of damaged property shall be performed by the Contractor after notification of a Change in the Work in accordance with Article 7.

§ 11.3.10 The Owner as fiduciary shall have power to adjust and settle a loss with insurers unless one of the parties in interest shall object in writing within five days after occurrence of loss to the Owner's exercise of this power; if such objection is made, the dispute shall be resolved in the manner selected by the Owner and Contractor as the method of binding dispute resolution in the Agreement. If the Owner and Contractor have selected arbitration as the method of binding dispute resolution, the Owner as fiduciary shall make settlement with insurers or distribution of insurance proceeds in accordance with the direction of the arbitrators.

§ 11.4 Performance Bond and Payment Bond

§ 11.4.1 The Owner shall have the right to require the Contractor to furnish bonds covering faithful performance of the Contract and payment of obligations arising thereunder as stipulated in bidding requirements or specifically required in the Contract Documents on the date of execution of the Contract.

§ 11.4.2 Upon the request of any person or entity appearing to be a potential beneficiary of bonds covering payment of obligations arising under the Contract, the Contractor shall promptly furnish a copy of the bonds or shall authorize a copy to be furnished.

ARTICLE 12 UNCOVERING AND CORRECTION OF WORK

§ 12.1 Uncovering of Work

§ 12.1.1 If a portion of the Work is covered contrary to the Construction Manager's or Architect's request or to requirements specifically expressed in the Contract Documents, it must, if requested in writing by either, be uncovered for their observation and be replaced at the Contractor's expense without change in the Contract Time.

§ 12.1.2 If a portion of the Work has been covered which the Construction Manager or Architect has not specifically requested to observe prior to its being covered, the Construction Manager or Architect may request to see such Work and it shall be uncovered by the Contractor. If such Work is in accordance with the Contract Documents, costs of uncovering and replacement shall, by appropriate Change Order, be at the Owner's expense. If such Work is not in accordance with the Contract Documents, such costs and the cost of correction shall be at the Contractor's expense unless the condition was caused by the Owner or one of the other Contractors in which event the Owner shall be responsible for payment of such costs.

§ 12.2 Correction of Work

§ 12.2.1 Before or After Substantial Completion

The Contractor shall promptly correct Work rejected by the Construction Manager or Architect or failing to conform to the requirements of the Contract Documents, whether discovered before or after Substantial Completion and whether or not fabricated, installed or completed. Costs of correcting such rejected Work, including additional testing and inspections, the cost of uncovering and replacement, and compensation for the Construction Manager's and Architect's services and expenses made necessary thereby, shall be at the Contractor's expense.

§ 12.2.2 After Substantial Completion

§ 12.2.2.1 In addition to the Contractor's obligations under Section 3.5, if, within one year after the date of Substantial Completion of the Work or designated portion thereof, or after the date for commencement of warranties established under Section 9.9.1, or by terms of an applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, the Contractor shall correct it promptly after receipt of written notice from the Owner to do so unless the Owner has previously given the Contractor a written acceptance of such condition. The Owner shall give such notice promptly after discovery of the condition. During the one-year period for correction of Work, if the Owner fails to notify the Contractor and give the Contractor an opportunity to make the correction, the Owner waives the rights to require correction by the Contractor and to make a claim for breach of warranty. If the Contractor fails to correct nonconforming Work within a reasonable time during that period after receipt of notice from the Owner or Architect, the Owner may correct it in accordance with Section 2.4.

§ 12.2.2.2 The one-year period shall be extended with respect to portions of Work first performed after Substantial Completion by the period of time between Substantial Completion and the actual completion of that portion of the Work.

§ 12.2.2.3 The one-year period for correction of Work shall not be extended by corrective Work performed by the Contractor pursuant to this Section 12.2.

§ 12.2.3 The Contractor shall remove from the site portions of the Work that are not in accordance with the requirements of the Contract Documents and are neither corrected by the Contractor nor accepted by the Owner.

§ 12.2.4 The Contractor shall bear the cost of correcting destroyed or damaged construction, whether completed or partially completed, of the Owner or separate contractors or other Multiple Prime Contractors caused by the

Contractor's correction or removal of Work that is not in accordance with the requirements of the Contract Documents.

§ 12.2.5 Nothing contained in this Section 12.2 shall be construed to establish a period of limitation with respect to other obligations the Contractor has under the Contract Documents. Establishment of the one-year period for correction of Work as described in Section 12.2.2 relates only to the specific obligation of the Contractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Contractor's liability with respect to the Contractor's obligations other than specifically to correct the Work.

§ 12.3 Acceptance of Nonconforming Work

If the Owner prefers to accept Work that is not in accordance with the requirements of the Contract Documents, the Owner may do so instead of requiring its removal and correction, in which case the Contract Sum will be reduced as appropriate and equitable. Such adjustment shall be effected whether or not final payment has been made.

ARTICLE 13 MISCELLANEOUS PROVISIONS

§ 13.1 Governing Law

The Contract shall be governed by the law of the place where the Project is located except that, if the parties have selected arbitration as the method of binding dispute resolution, the Federal Arbitration Act shall govern Section 15.4.

§ 13.2 Successors and Assigns

§ 13.2.1 The Owner and Contractor respectively bind themselves, their partners, successors, assigns and legal representatives to covenants, agreements and obligations contained in the Contract Documents. Except as provided in Section 13.2.2, neither party to the Contract shall assign the Contract as a whole without written consent of the other. If either party attempts to make such an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations under the Contract.

§ 13.2.2 The Owner may, without consent of the Contractor, assign the Contract to a lender providing construction financing for the Project, if the lender assumes the Owner's rights and obligations under the Contract Documents. The Contractor shall execute all consents reasonably required to facilitate such assignment.

§ 13.3 Written Notice

Written notice shall be deemed to have been duly served if delivered in person to the individual, to a member of the firm or entity or to an officer of the corporation for which it was intended; or if delivered at or sent by registered or certified mail or by courier service providing proof of delivery to, the last business address known to the party giving notice.

§ 13.4 Rights and Remedies

§ 13.4.1 Duties and obligations imposed by the Contract Documents and rights and remedies available thereunder shall be in addition to and not a limitation of duties, obligations, rights and remedies otherwise imposed or available by law.

§ 13.4.2 No action or failure to act by the Owner, Construction Manager, Architect or Contractor shall constitute a waiver of a right or duty afforded them under the Contract, nor shall such action or failure to act constitute approval of or acquiescence in a breach thereunder, except as may be specifically agreed in writing.

§ 13.5 Tests and Inspections

§ 13.5.1 Tests, inspections and approvals of portions of the Work shall be made as required by the Contract Documents and by applicable laws, statutes, ordinances, codes, rules and regulations or lawful orders of public authorities. Unless otherwise provided, the Contractor shall make arrangements for such tests, inspections and approvals with an independent testing laboratory or entity acceptable to the Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections and approvals. The Contractor shall give the Construction Manager and Architect timely notice of when and where tests and inspections are to be made so that the Construction Manager and Architect may be present for such procedures. The Owner shall bear costs of (1) tests, inspections or approvals that do not become requirements until after bids are received or negotiations concluded, and

(2) tests, inspections or approvals where building codes or applicable laws or regulations prohibit the Owner from delegating their cost to the Contractor.

§ 13.5.2 If the Construction Manager, Architect, Owner or public authorities having jurisdiction determine that portions of the Work require additional testing, inspection or approval not included under Section 13.5.1, the Construction Manager and Architect will, upon written authorization from the Owner, instruct the Contractor to make arrangements for such additional testing, inspection or approval by an entity acceptable to the Owner, and the Contractor shall give timely notice to the Construction Manager and Architect of when and where tests and inspections are to be made so that the Construction Manager and Architect may be present for such procedures. Such costs except as provided in Section 13.5.3, shall be at the Owner's expense.

§ 13.5.3 If such procedures for testing, inspection or approval under Sections 13.5.1 and 13.5.2 reveal failure of the portions of the Work to comply with requirements established by the Contract Documents, all costs made necessary by such failure including those of repeated procedures and compensation for the Construction Manager's and Architect's services and expenses shall be at the Contractor's expense.

§ 13.5.4 Required certificates of testing, inspection or approval shall, unless otherwise required by the Contract Documents, be secured by the Contractor and promptly delivered to the Construction Manager for transmittal to the Architect.

§ 13.5.5 If the Construction Manager or Architect is to observe tests, inspections or approvals required by the Contract Documents, the Construction Manager or Architect will do so promptly and, where practicable, at the normal place of testing.

§ 13.5.6 Tests or inspections conducted pursuant to the Contract Documents shall be made promptly to avoid unreasonable delay in the Work.

§ 13.6 Interest

Payments due and unpaid under the Contract Documents shall bear interest from the date payment is due at such rate as the parties may agree upon in writing or, in the absence thereof, at the legal rate prevailing from time to time at the place where the Project is located.

§ 13.7 Time Limits on Claims

The Owner and the Contractor shall commence all claims and causes of action, whether in contract, tort, breach of warranty or otherwise, against the other arising out of or related to the Contract in accordance with the requirements of the final dispute resolution method selected in the Agreement within the time period specified by applicable law, but in any case not more than 10 years after the date of Substantial Completion of the Work. The Owner and the Contractor waive all claims and causes of action not commenced in accordance with this Section 13.7.

ARTICLE 14 TERMINATION OR SUSPENSION OF THE CONTRACT

§ 14.1 Termination by the Contractor

§ 14.1.1 The Contractor may terminate the Contract if the Work is stopped for a period of 30 consecutive days through no act or fault of the Contractor or a Subcontractor, Sub-subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, for any of the following reasons:

- .1 Issuance of an order of a court or other public authority having jurisdiction that requires all Work to be stopped;
- .2 An act of government, such as a declaration of national emergency that requires all Work to be stopped;
- .3 Because the Construction Manager has not certified or the Architect has not issued a Certificate for Payment and has not notified the Contractor of the reason for withholding certification as provided in Section 9.4, or because the Owner has not made payment on a Certificate for Payment within the time stated in the Contract Documents; or
- .4 The Owner has failed to furnish to the Contractor promptly, upon the Contractor's request, reasonable evidence as required by Section 2.2.1.

§ 14.1.2 The Contractor may terminate the Contract if, through no act or fault of the Contractor or a Subcontractor, Sub-subcontractor or their agents or employees or any other persons or entities performing portions of the Work under direct or indirect contract with the Contractor, repeated suspensions, delays or interruptions of the entire Work by the Owner as described in Section 14.3 constitute in the aggregate more than 100 percent of the total number of days scheduled for completion, or 120 days in any 365-day period, whichever is less.

§ 14.1.3 If one of the reasons described in Section 14.1.1 or 14.1.2 exists, the Contractor may, upon seven days' written notice to the Owner, Construction Manager and Architect, terminate the Contract and recover from the Owner payment for Work executed including reasonable overhead and profit, costs incurred by reason of such termination, and damages.

§ 14.1.4 If the Work is stopped for a period of 60 consecutive days through no act or fault of the Contractor or a Subcontractor or their agents or employees or any other persons performing portions of the Work under contract with the Contractor because the Owner has repeatedly failed to fulfill the Owner's obligations under the Contract Documents with respect to matters important to the progress of the Work, the Contractor may, upon seven additional days' written notice to the Owner, Construction Manager and Architect, terminate the Contract and recover from the Owner as provided in Section 14.1.3.

§ 14.2 Termination by the Owner for Cause

§ 14.2.1 The Owner may terminate the Contract if the Contractor

- .1 repeatedly refuses or fails to supply enough properly skilled workers or proper materials;
- .2 fails to make payment to Subcontractors for materials or labor in accordance with the respective agreements between the Contractor and the Subcontractors;
- .3 repeatedly disregards applicable laws, statutes, ordinances, codes, rules and regulations, or lawful orders of a public authority; or
- .4 otherwise is guilty of substantial breach of a provision of the Contract Documents.

§ 14.2.2 When any of the above reasons exist, the Owner, after consultation with the Construction Manager, and upon certification by the Initial Decision Maker that sufficient cause exists to justify such action, may without prejudice to any other rights or remedies of the Owner and after giving the Contractor and the Contractor's surety, if any, seven days' written notice, terminate employment of the Contractor and may, subject to any prior rights of the surety:

- .1 Exclude the Contractor from the site and take possession of all materials, equipment, tools, and construction equipment and machinery thereon owned by the Contractor;
- .2 Accept assignment of subcontracts pursuant to Section 5.4; and
- .3 Finish the Work by whatever reasonable method the Owner may deem expedient. Upon written request of the Contractor, the Owner shall furnish to the Contractor a detailed accounting of the costs incurred by the Owner in finishing the Work.

§ 14.2.3 When the Owner terminates the Contract for one of the reasons stated in Section 14.2.1, the Contractor shall not be entitled to receive further payment until the Work is finished.

§ 14.2.4 If the unpaid balance of the Contract Sum exceeds costs of finishing the Work, including compensation for the Construction Manager's and Architect's services and expenses made necessary thereby, and other damages incurred by the Owner and not expressly waived, such excess shall be paid to the Contractor. If such costs and damages exceed the unpaid balance, the Contractor shall pay the difference to the Owner. The amount to be paid to the Contractor or Owner, as the case may be, shall, upon application, be certified by the Initial Decision Maker after consultation with the Construction Manager, and this obligation for payment shall survive termination of the Contract.

§ 14.3 Suspension by the Owner for Convenience

§ 14.3.1 The Owner may, without cause, order the Contractor in writing to suspend, delay or interrupt the Work in whole or in part for such period of time as the Owner may determine.

§ 14.3.2 The Contract Sum and the Contract Time shall be adjusted for increases in the cost and time caused by suspension, delay or interruption as described in Section 14.3.1. Adjustment of the Contract Sum shall include profit. No adjustment shall be made to the extent:

- .1 that performance is, was or would have been so suspended, delayed or interrupted by another cause for which the Contractor is responsible; or
- .2 that an equitable adjustment is made or denied under another provision of this Contract.

§ 14.4 Termination by the Owner for Convenience

§ 14.4.1 The Owner may, at any time, terminate the Contract for the Owner's convenience and without cause.

§ 14.4.2 Upon receipt of written notice from the Owner of such termination for the Owner's convenience, the Contractor shall

- .1 cease operations as directed by the Owner in the notice;
- .2 take actions necessary, or that the Owner may direct, for the protection and preservation of the Work; and
- .3 except for Work directed to be performed prior to the effective date of termination stated in the notice, terminate all existing subcontracts and purchase orders and enter into no further subcontracts and purchase orders.

§ 14.4.3 In case of such termination for the Owner's convenience, the Contractor shall be entitled to receive payment for Work executed, and costs incurred by reason of such termination, along with reasonable overhead and profit on the Work not executed.

ARTICLE 15 CLAIMS AND DISPUTES

§ 15.1 Claims

§ 15.1.1 Definition. A Claim is a demand or assertion by one of the parties seeking, as a matter of right, payment of money, or other relief with respect to the terms of the Contract. The term "Claim" also includes other disputes and matters in question between the Owner and Contractor arising out of or relating to the Contract. The responsibility to substantiate Claims shall rest with the party making the Claim.

§ 15.1.2 Notice of Claims. Claims by either the Owner or Contractor must be initiated by written notice to the other party and to the Initial Decision Maker with a copy sent to the Construction Manager and Architect, if the Construction Manager and or Architect is not serving as the Initial Decision Maker. Claims by either party must be initiated within 21 days after occurrence of the event giving rise to such Claim or within 21 days after the claimant first recognizes the condition giving rise to the Claim, whichever is later.

§ 15.1.3 Continuing Contract Performance. Pending final resolution of a Claim, except as otherwise agreed in writing or as provided in Section 9.7 and Article 14, the Contractor shall proceed diligently with performance of the Contract and the Owner shall continue to make payments in accordance with the Contract Documents. The Construction Manager will prepare Change Orders and the Architect will issue a Certificate for Payment or Project Certificate for Payment in accordance with the decisions of the Initial Decision Maker.

§ 15.1.4 Claims for Additional Cost. If the Contractor wishes to make a Claim for an increase in the Contract Sum, written notice as provided herein shall be given before proceeding to execute the Work. Prior notice is not required for Claims relating to an emergency endangering life or property arising under Section 10.3.

§ 15.1.5 Claims for Additional Time

§ 15.1.5.1 If the Contractor wishes to make a Claim for an increase in the Contract Time, written notice as provided herein shall be given. The Contractor's Claim shall include an estimate of cost and of probable effect of delay on progress of the Work. In the case of a continuing delay only one Claim is necessary.

§ 15.1.5.2 If adverse weather conditions are the basis for a Claim for additional time, such Claim shall be documented by data substantiating that weather conditions were abnormal for the period of time, could not have been reasonably anticipated and had an adverse effect on the scheduled construction.

§ 15.1.6 Claims for Consequential Damages. The Contractor and Owner waive Claims against each other for consequential damages arising out of or relating to this Contract. This mutual waiver includes

- .1 damages incurred by the Owner for rental expenses, for losses of use, income, profit, financing, business and reputation, and for loss of management or employee productivity or of the services of such persons; and

- .2 damages incurred by the Contractor for principal office expenses including the compensation of personnel stationed there, for losses of financing, business and reputation, and for loss of profit except anticipated profit arising directly from the Work.

This mutual waiver is applicable, without limitation, to all consequential damages due to either party's termination in accordance with Article 14. Nothing contained in this Section 15.1.6 shall be deemed to preclude an award of liquidated damages, when applicable, in accordance with the requirements of the Contract Documents.

§ 15.2 Initial Decision

§ 15.2.1 Claims, excluding those arising under Sections 10.3, 10.4, 11.3.9, and 11.3.10, shall be referred to the Initial Decision Maker for initial decision. The Architect will serve as the Initial Decision Maker, unless otherwise indicated in the Agreement. Except for those Claims excluded by this Section 15.2.1, an initial decision shall be required as a condition precedent to mediation of any Claim arising prior to the date final payment is due, unless 30 days have passed after the Claim has been referred to the Initial Decision Maker with no decision having been rendered. Unless the Initial Decision Maker and all affected parties agree, the Initial Decision Maker will not decide disputes between the Contractor and persons or entities other than the Owner.

§ 15.2.2 The Initial Decision Maker will review Claims and within ten days of the receipt of a Claim take one or more of the following actions: (1) request additional supporting data from the claimant or a response with supporting data from the other party, (2) reject the Claim in whole or in part, (3) approve the Claim, (4) suggest a compromise, or (5) advise the parties that the Initial Decision Maker is unable to resolve the Claim if the Initial Decision Maker lacks sufficient information to evaluate the merits of the Claim or if the Initial Decision Maker concludes that, in the Initial Decision Maker's sole discretion, it would be inappropriate for the Initial Decision Maker to resolve the Claim.

§ 15.2.3 In evaluating Claims, the Initial Decision Maker may, but shall not be obligated to, consult with or seek information from either party or from persons with special knowledge or expertise who may assist the Initial Decision Maker in rendering a decision. The Initial Decision Maker may request the Owner to authorize retention of such persons at the Owner's expense.

§ 15.2.4 If the Initial Decision Maker requests a party to provide a response to a Claim or to furnish additional supporting data, such party shall respond, within ten days after receipt of such request, and shall either (1) provide a response on the requested supporting data, (2) advise the Initial Decision Maker when the response or supporting data will be furnished or (3) advise the Initial Decision Maker that no supporting data will be furnished. Upon receipt of the response or supporting data, if any, the Initial Decision Maker will either reject or approve the Claim in whole or in part.

§ 15.2.5 The Initial Decision Maker will render an initial decision approving or rejecting the Claim, or indicating that the Initial Decision Maker is unable to resolve the Claim. This initial decision shall (1) be in writing; (2) state the reasons therefor; and (3) notify the parties and the Architect and Construction Manager, if the Architect or Construction Manager is not serving as the Initial Decision Maker, of any change in the Contract Sum or Contract Time or both. The initial decision shall be final and binding on the parties but subject to mediation and, if the parties fail to resolve their dispute through mediation, to binding dispute resolution.

§ 15.2.6 Either party may file for mediation of an initial decision at any time, subject to the terms of Section 15.2.6.1.

§ 15.2.6.1 Either party may, within 30 days from the date of an initial decision, demand in writing that the other party file for mediation within 60 days of the initial decision. If such a demand is made and the party receiving the demand fails to file for mediation within the time required, then both parties waive their rights to mediate or pursue binding dispute resolution proceedings with respect to the initial decision.

§ 15.2.7 In the event of a Claim against the Contractor, the Owner may, but is not obligated to, notify the surety, if any of the nature and amount of the Claim. If the Claim relates to a possibility of a Contractor's default, the Owner may, but is not obligated to, notify the surety and request the surety's assistance in resolving the controversy.

§ 15.2.8 If a Claim relates to or is the subject of a mechanic's lien, the party asserting such Claim may proceed in accordance with applicable law to comply with the lien notice or filing deadlines.

§ 15.3 Mediation

§ 15.3.1 Claims, disputes, or other matters in controversy arising out of or related to the Contract except those waived as provided for in Sections 9.10.4, 9.10.5, and 15.1.6 shall be subject to mediation as a condition precedent to binding dispute resolution.

§ 15.3.2 The parties shall endeavor to resolve their Claims by mediation which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Mediation Procedures in effect on the date of the Agreement. A request for mediation shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the mediation. The request may be made concurrently with the filing of binding dispute resolution proceedings but, in such event, mediation shall proceed in advance of binding dispute resolution proceedings, which shall be stayed pending mediation for a period of 60 days from the date of filing, unless stayed for a longer period by agreement of the parties or court order. If an arbitration is stayed pursuant to this Section 15.3.2, the parties may nonetheless proceed to the selection of the arbitrator(s) and agree upon a schedule for later proceedings.

§ 15.3.3 The parties shall share the mediator's fee and any filing fees equally. The mediation shall be held in the place where the Project is located, unless another location is mutually agreed upon. Agreements reached in mediation shall be enforceable as settlement agreements in any court having jurisdiction thereof.

§ 15.4 Arbitration

§ 15.4.1 If the parties have selected arbitration as the method for binding dispute resolution in the Agreement, any Claim subject to, but not resolved by, mediation shall be subject to arbitration which, unless the parties mutually agree otherwise, shall be administered by the American Arbitration Association in accordance with its Construction Industry Arbitration Rules in effect on the date of the Agreement. A demand for arbitration shall be made in writing, delivered to the other party to the Contract, and filed with the person or entity administering the arbitration. The party filing a notice of demand for arbitration must assert in the demand all Claims then known to that party on which arbitration is permitted to be demanded.

§ 15.4.1.1 A demand for arbitration shall be made no earlier than concurrently with the filing of a request for mediation, but in no event shall it be made after the date when the institution of legal or equitable proceedings based on the Claim would be barred by the applicable statute of limitations. For statute of limitations purposes, receipt of a written demand for arbitration by the person or entity administering the arbitration shall constitute the institution of legal or equitable proceedings based on the Claim.

§ 15.4.2 The award rendered by the arbitrator or arbitrators shall be final, and judgment may be entered upon it in accordance with applicable law in any court having jurisdiction thereof.

§ 15.4.3 The foregoing agreement to arbitrate and other agreements to arbitrate with an additional person or entity duly consented to by parties to the Agreement shall be specifically enforceable under applicable law in any court having jurisdiction thereof.

§ 15.4.4 Consolidation or Joinder

§ 15.4.4.1 Either party, at its sole discretion, may consolidate an arbitration conducted under this Agreement with any other arbitration to which it is a party provided that (1) the arbitration agreement governing the other arbitration permits consolidation, (2) the arbitrations to be consolidated substantially involve common questions of law or fact, and (3) the arbitrations employ materially similar procedural rules and methods for selecting arbitrator(s).

§ 15.4.4.2 Either party, at its sole discretion, may include by joinder persons or entities substantially involved in a common question of law or fact whose presence is required if complete relief is to be accorded in arbitration, provided that the party sought to be joined consents in writing to such joinder. Consent to arbitration involving an additional person or entity shall not constitute consent to arbitration of any claim, dispute or other matter in question not described in the written consent.

§ 15.4.4.3 The Owner and Contractor grant to any person or entity made a party to an arbitration conducted under this Section 15.4, whether by joinder or consolidation, the same rights of joinder and consolidation as the Owner and Contractor under this Agreement.

Additions and Deletions Report for

AIA® Document A232™ – 2009

This Additions and Deletions Report, as defined on page 1 of the associated document, reproduces below all text the author has added to the standard form AIA document in order to complete it, as well as any text the author may have added to or deleted from the original AIA text. Added text is shown underlined. Deleted text is indicated with a horizontal line through the original AIA text.

Note: This Additions and Deletions Report is provided for information purposes only and is not incorporated into or constitute any part of the associated AIA document. This Additions and Deletions Report and its associated document were generated simultaneously by AIA software at 12:24:07 on 08/24/2016.

PAGE 1

Midland CUSD #7 New Elementary School
Lacon, IL

...

Midwest Construction Professionals
520 E. Highland
Morton, IL 61550

...

Midland Community Unit School District No. 7
1830 State Route 17
Varna, IL 61375

...

CBJ Architects, Professional Corporation
3521 Wintergreen
Algonquin, IL 60102

Certification of Document's Authenticity

AIA® Document D401™ – 2003

I, , hereby certify, to the best of my knowledge, information and belief, that I created the attached final document simultaneously with its associated Additions and Deletions Report and this certification at 12:24:07 on 08/24/2016 under Order No. 7834146880 from AIA Contract Documents software and that in preparing the attached final document I made no changes to the original text of AIA® Document A232™ - 2009, General Conditions of the Contract for Construction, Construction Manager as Adviser Edition, as published by the AIA in its software, other than those additions and deletions shown in the associated Additions and Deletions Report.

(Signed)

(Title)

(Dated)

SECTION 01 4216
DEFINITIONS

PART 1 GENERAL

1.01 SUMMARY

- A. This section supplements the definitions contained in the General Conditions.
- B. Other definitions are included in individual specification sections.

1.02 DEFINITIONS

- A. Furnish: To supply, deliver, unload, and inspect for damage.
- B. Install: To unpack, assemble, erect, apply, place, finish, cure, protect, clean, start up, and make ready for use.
- C. Product: Material, machinery, components, equipment, fixtures, and systems forming the work result. Not materials or equipment used for preparation, fabrication, conveying, or erection and not incorporated into the work result. Products may be new, never before used, or re-used materials or equipment.
- D. Project Manual: The book-sized volume that includes the procurement requirements (if any), the contracting requirements, and the specifications.
- E. Provide: To furnish and install.
- F. Supply: Same as Furnish.

PART 2 PRODUCTS - NOT USED

PART 3 EXECUTION - NOT USED

END OF SECTION

SECTION 07 9200
JOINT SEALANTS

PART 1 GENERAL

1.01 SECTION INCLUDES

- A. Nonsag gunnable joint sealants.
- B. Self-leveling pourable joint sealants.
- C. Joint backings and accessories.

1.02 RELATED REQUIREMENTS

1.03 REFERENCE STANDARDS

- A. ASTM C794 - Standard Test Method for Adhesion-In-Peel of Elastomeric Joint Sealants; 2015.
- B. ASTM C920 - Standard Specification for Elastomeric Joint Sealants; 2014.
- C. ASTM C1087 - Standard Test Method for Determining Compatibility of Liquid-Applied Sealants with Accessories Used in Structural Glazing Systems; 2000 (Reapproved 2011).
- D. ASTM C1193 - Standard Guide for Use of Joint Sealants; 2016.
- E. ASTM C1248 - Standard Test Method for Staining of Porous Substrate by Joint Sealants; 2008 (Reapproved 2012).

1.04 SUBMITTALS

- A. See Section 01 3000 - Administrative Requirements, for submittal procedures.
- B. Product Data for Sealants: Submit manufacturer's technical data sheets for each product to be used, that includes the following.
 - 1. Physical characteristics, including movement capability, VOC content, hardness, cure time, and color availability.
 - 2. List of backing materials approved for use with the specific product.
 - 3. Substrates that product is known to satisfactorily adhere to and with which it is compatible.
 - 4. Substrates the product should not be used on.
- C. Preconstruction Laboratory Test Reports: Submit at least four weeks prior to start of installation.

1.05 QUALITY ASSURANCE

- A. Preconstruction Laboratory Testing: Arrange for sealant manufacturer(s) to test each combination of sealant, substrate, backing, and accessories.
 - 1. Adhesion Testing: In accordance with ASTM C794.
 - 2. Compatibility Testing: In accordance with ASTM C1087.
 - 3. Allow sufficient time for testing to avoid delaying the work.
 - 4. Deliver to manufacturer sufficient samples for testing.
 - 5. Report manufacturer's recommended corrective measures, if any, including primers or techniques not indicated in product data submittals.
 - 6. Testing is not required if sealant manufacturer provides data showing previous testing, not older than 24 months, that shows satisfactory adhesion, lack of staining, and compatibility.

1.06 WARRANTY

- A. See Section 01 7800 - Closeout Submittals, for additional warranty requirements.
- B. Correct defective work within a five year period after Date of Substantial Completion.
- C. Warranty: Include coverage for installed sealants and accessories that fail to achieve watertight seal , exhibit loss of adhesion or cohesion, or do not cure.

PART 2 PRODUCTS

2.01 MANUFACTURERS

- A. Non-Sag Sealants: Permits application in joints on vertical surfaces without sagging or slumping.
- B. Self-Leveling Sealants: Pourable or self-leveling sealant that has sufficient flow to form a smooth, level surface when applied in a horizontal joint.

2.02 JOINT SEALANT APPLICATIONS

- A. Scope:
 - 1. Exterior Joints: Seal open joints, whether or not the joint is indicated on the drawings, unless specifically indicated not to be sealed. Exterior joints to be sealed include, but are not limited to, the following items.
 - a. Wall expansion and control joints.
 - b. Joints between door, window, and other frames and adjacent construction.
 - c. Joints between different exposed materials.
 - d. Openings below ledge angles in masonry.
 - e. Other joints indicated below.
 - 2. Interior Joints: Do not seal interior joints unless specifically indicated to be sealed. Interior joints to be sealed include, but are not limited to, the following items.
 - a. Joints between door, window, and other frames and adjacent construction.
 - b. Other joints indicated below.
 - 3. Do not seal the following types of joints.
 - a. Intentional weepholes in masonry.
 - b. Joints indicated to be treated with manufactured expansion joint cover or some other type of sealing device.
 - c. Joints where sealant is specified to be provided by manufacturer of product to be sealed.
 - d. Joints where installation of sealant is specified in another section.
 - e. Joints between suspended panel ceilings/grid and walls.
- B. Exterior Joints: Use non-sag non-staining silicone sealant, unless otherwise indicated.
 - 1. Control and Expansion Joints in Concrete Paving: Self-leveling polyurethane "traffic-grade" sealant.
- C. Interior Joints: Use non-sag polyurethane sealant, unless otherwise indicated.

2.03 JOINT SEALANTS - GENERAL

2.04 NONSAG JOINT SEALANTS

- A. Non-Staining Silicone Sealant: ASTM C920, Grade NS, Uses M and A; not expected to withstand continuous water immersion or traffic.
 - 1. Movement Capability: Plus and minus 50 percent, minimum.
 - 2. Non-Staining To Porous Stone: Non-staining to light-colored natural stone when tested in accordance with ASTM C1248.
 - 3. Dirt Pick-Up: Reduced dirt pick-up compared to other silicone sealants.
- B. Polyurethane Sealant: ASTM C920, Grade NS, Uses M and A; single or multi-component; not expected to withstand continuous water immersion or traffic.
 - 1. Movement Capability: Plus and minus 25 percent, minimum.

2.05 SELF-LEVELING SEALANTS

- A. Self-Leveling Polyurethane Sealant: ASTM C920, Grade P, Uses M and A; single or multi-component; explicitly approved by manufacturer for traffic exposure; not expected to withstand continuous water immersion .
 - 1. Movement Capability: Plus and minus 25 percent, minimum.

2.06 ACCESSORIES

- A. Backer Rod: Cylindrical cellular foam rod with surface that sealant will not adhere to, compatible with specific sealant used, and recommended by backing and sealant manufacturers for specific application.
- B. Backing Tape: Self-adhesive polyethylene tape with surface that sealant will not adhere to and recommended by tape and sealant manufacturers for specific application.

PART 3 EXECUTION

3.01 EXAMINATION

- A. Verify that joints are ready to receive work.
- B. Verify that backing materials are compatible with sealants.
- C. Verify that backer rods are of the correct size.

3.02 PREPARATION

- A. Remove loose materials and foreign matter that could impair adhesion of sealant.
- B. Clean joints, and prime as necessary, in accordance with manufacturer's instructions.
- C. Perform preparation in accordance with manufacturer's instructions and ASTM C1193.
- D. Mask elements and surfaces adjacent to joints from damage and disfigurement due to sealant work; be aware that sealant drips and smears may not be completely removable.

3.03 INSTALLATION

- A. Perform work in accordance with sealant manufacturer's requirements for preparation of surfaces and material installation instructions.
- B. Perform installation in accordance with ASTM C1193.
- C. Install bond breaker backing tape where backer rod cannot be used.
- D. Install sealant free of air pockets, foreign embedded matter, ridges, and sags, and without getting sealant on adjacent surfaces.
- E. Do not install sealant when ambient temperature is outside manufacturer's recommended temperature range, or will be outside that range during the entire curing period, unless manufacturer's approval is obtained and instructions are followed.
- F. Nonsag Sealants: Tool surface concave, unless otherwise indicated; remove masking tape immediately after tooling sealant surface.

3.04 FIELD QUALITY CONTROL

- A. Perform field quality control inspection/testing as specified in PART 1 under QUALITY ASSURANCE article.
- B. Remove and replace failed portions of sealants using same materials and procedures as indicated for original installation.

END OF SECTION
